A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION : Dhaloy, Hathajari, Chittagong.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING : 24.0m	R. L.: 0.91m below from Road Level.
CLIENT : TM International, Bangladesh Ltd.	DATE OF BORING : 08-06-2006	G. W. T : 0.10m above from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Light gray 10YR (7/2), medium plastic, soft, silty Clay, CL.		UD-1, UD-2	D-1, D-2	4, 3		
2.0m	Very dark gray 10YR (3/1), very soft, organic soil.			D-3, D-4, D-5	2, 1, 2		
16.0m	Gray 10YR (6/1), medium plastic, very soft to soft, silty Clay, CL.			D-6, D-7, D-8, D-9, D-10, D-11, D-12, D-13, D-14, D-15, D-16	1, 2, 2, 1, 1, 3, 4, 2, 3, 2, 4		
3.45m	Light gray 10YR (7/2), dense to very dense, fine sand, SM.			D-17, D-18, D-19	25, 27, 38		

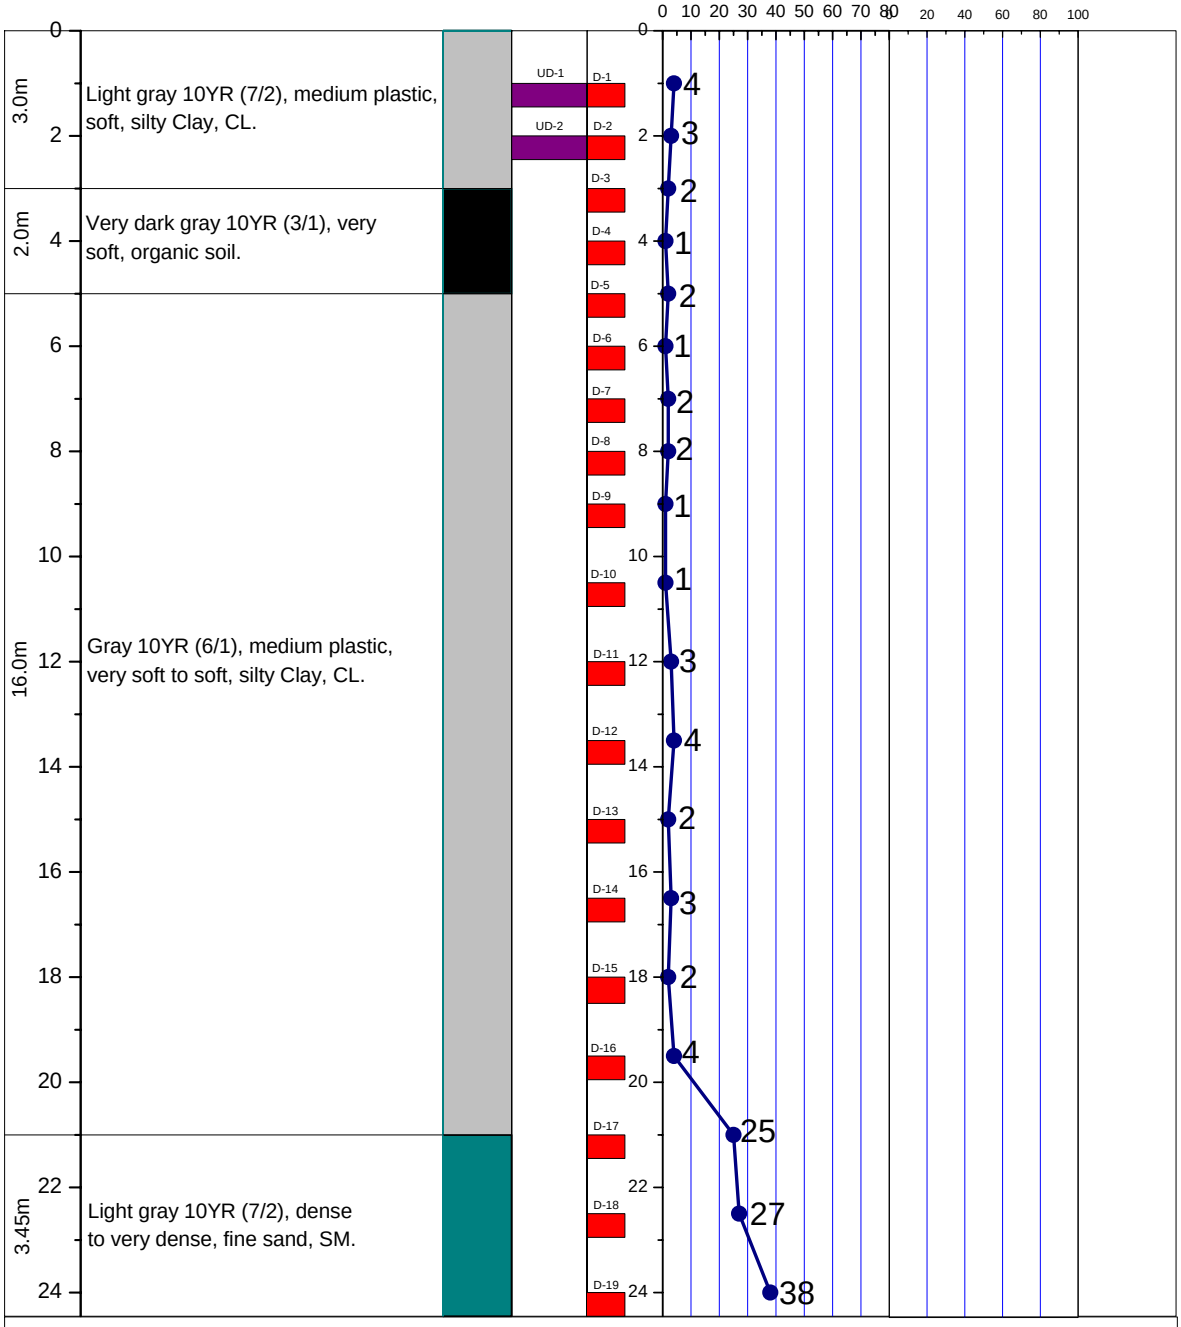

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
