| | | | | |
|---|---|---|---|---|
| **A2** | **PROSOIL** | **Borehole No: BH-2** | **Easting: 230769.12** | **Northing: 2643179.80** |
| | | **Location: Uttara, Dhaka.** | | **Borehole Depth: 31.0m** |
| **Name of Project:** DHAKA MASS RAPID TRANSIT DEVELOPMENT PROJECT LINE-6. (CONTRACT NO. CP-07) | | **Type of Drill Rig: Hydraulic Rotary.** | | **R.L.: 7.152m** |
| **CLIENT: L&T CONSTRUCTION** | | **Date of Boring: 01-12-2018 to 03-12-2018** | | **B. W. T : 4.80m below from E. G. L.** |

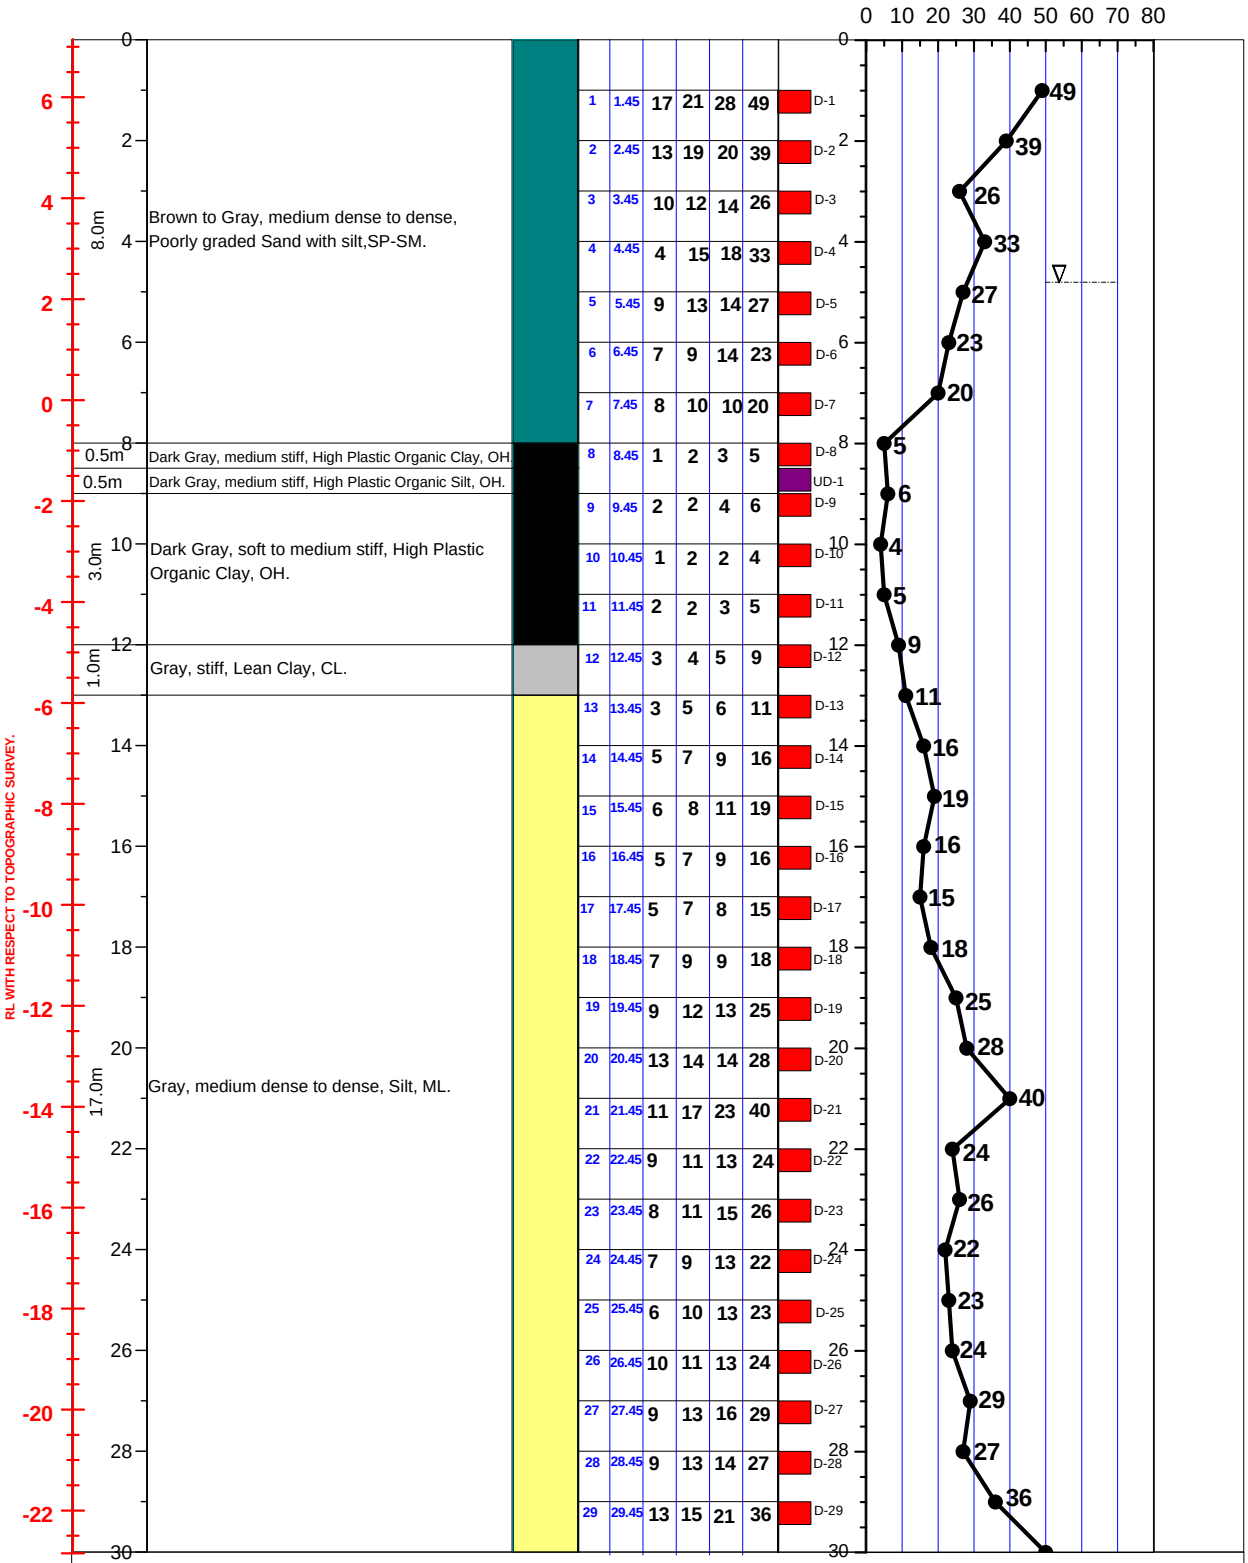


| | FROM (m) | TO (m) | 0-150 (mm) | 150-300 (mm) | 300-450 (mm) | N | DISTURBED SAMPLE | SPT VALUES |
|---|---|---|---|---|---|---|---|---|
| 1 | 1.45 | | 17 | 21 | 28 | 49 | D-1 | 49 |
| 2 | 2.45 | | 13 | 19 | 20 | 39 | D-2 | 39 |
| 3 | 3.45 | | 10 | 12 | 14 | 26 | D-3 | 26 |
| 4 | 4.45 | | 4 | 15 | 18 | 33 | D-4 | 33 |
| 5 | 5.45 | | 9 | 13 | 14 | 27 | D-5 | 27 |
| 6 | 6.45 | | 7 | 9 | 14 | 23 | D-6 | 23 |
| 7 | 7.45 | | 8 | 10 | 10 | 20 | D-7 | 20 |
| 8 | 8.45 | | 1 | 2 | 3 | 5 | D-8 | 5 |
| | | | | | | | UD-1 | |
| 9 | 9.45 | | 2 | 2 | 4 | 6 | D-9 | 6 |
| 10 | 10.45 | | 1 | 2 | 2 | 4 | D-10 | 4 |
| 11 | 11.45 | | 2 | 2 | 3 | 5 | D-11 | 5 |
| 12 | 12.45 | | 3 | 4 | 5 | 9 | D-12 | 9 |
| 13 | 13.45 | | 3 | 5 | 6 | 11 | D-13 | 11 |
| 14 | 14.45 | | 5 | 7 | 9 | 16 | D-14 | 16 |
| 15 | 15.45 | | 6 | 8 | 11 | 19 | D-15 | 19 |
| 16 | 16.45 | | 5 | 7 | 9 | 16 | D-16 | 16 |
| 17 | 17.45 | | 5 | 7 | 8 | 15 | D-17 | 15 |
| 18 | 18.45 | | 7 | 9 | 9 | 18 | D-18 | 18 |
| 19 | 19.45 | | 9 | 12 | 13 | 25 | D-19 | 25 |
| 20 | 20.45 | | 13 | 14 | 14 | 28 | D-20 | 28 |
| 21 | 21.45 | | 11 | 17 | 23 | 40 | D-21 | 40 |
| 22 | 22.45 | | 9 | 11 | 13 | 24 | D-22 | 24 |
| 23 | 23.45 | | 8 | 11 | 15 | 26 | D-23 | 26 |
| 24 | 24.45 | | 7 | 9 | 13 | 22 | D-24 | 22 |
| 25 | 25.45 | | 6 | 10 | 13 | 23 | D-25 | 23 |
| 26 | 26.45 | | 10 | 11 | 13 | 24 | D-26 | 24 |
| 27 | 27.45 | | 9 | 13 | 16 | 29 | D-27 | 29 |
| 28 | 28.45 | | 9 | 13 | 14 | 27 | D-28 | 27 |
| 29 | 29.45 | | 13 | 15 | 21 | 36 | D-29 | 36 |

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

| | | | |
|---|---|---|---|
| PLASTIC CLAY | SILT | PEAT/HIGHLY ORGANIC SOIL | UNDISTURBED SAMPLE |
| MICACEOUS FINE SAND/SILT | SAND | SHALE | DISTURBED SAMPLE |

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^m PENETRATION= 50 BLOWS. AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED

| | | | | |
|---|---|---|---|---|
| **A2** | **PROSOIL** | **Borehole No: BH-2** | **Easting: 230769.12** | **Northing: 2643179.80** |
| | | **Location: Uttara, Dhaka.** | | **Borehole Depth: 31.0m** |
| **Name of Project:** DHAKA MASS RAPID TRANSIT DEVELOPMENT PROJECT LINE-6. (CONTRACT NO. CP-07) | | **Type of Drill Rig: Hydraulic Rotary.** | | **R.L.: 7.152m** |
| **CLIENT: L&T CONSTRUCTION** | | **Date of Boring: 01-12-2018 to 03-12-2018** | | **B. W. T : 4.80m below from E. G. L.** |

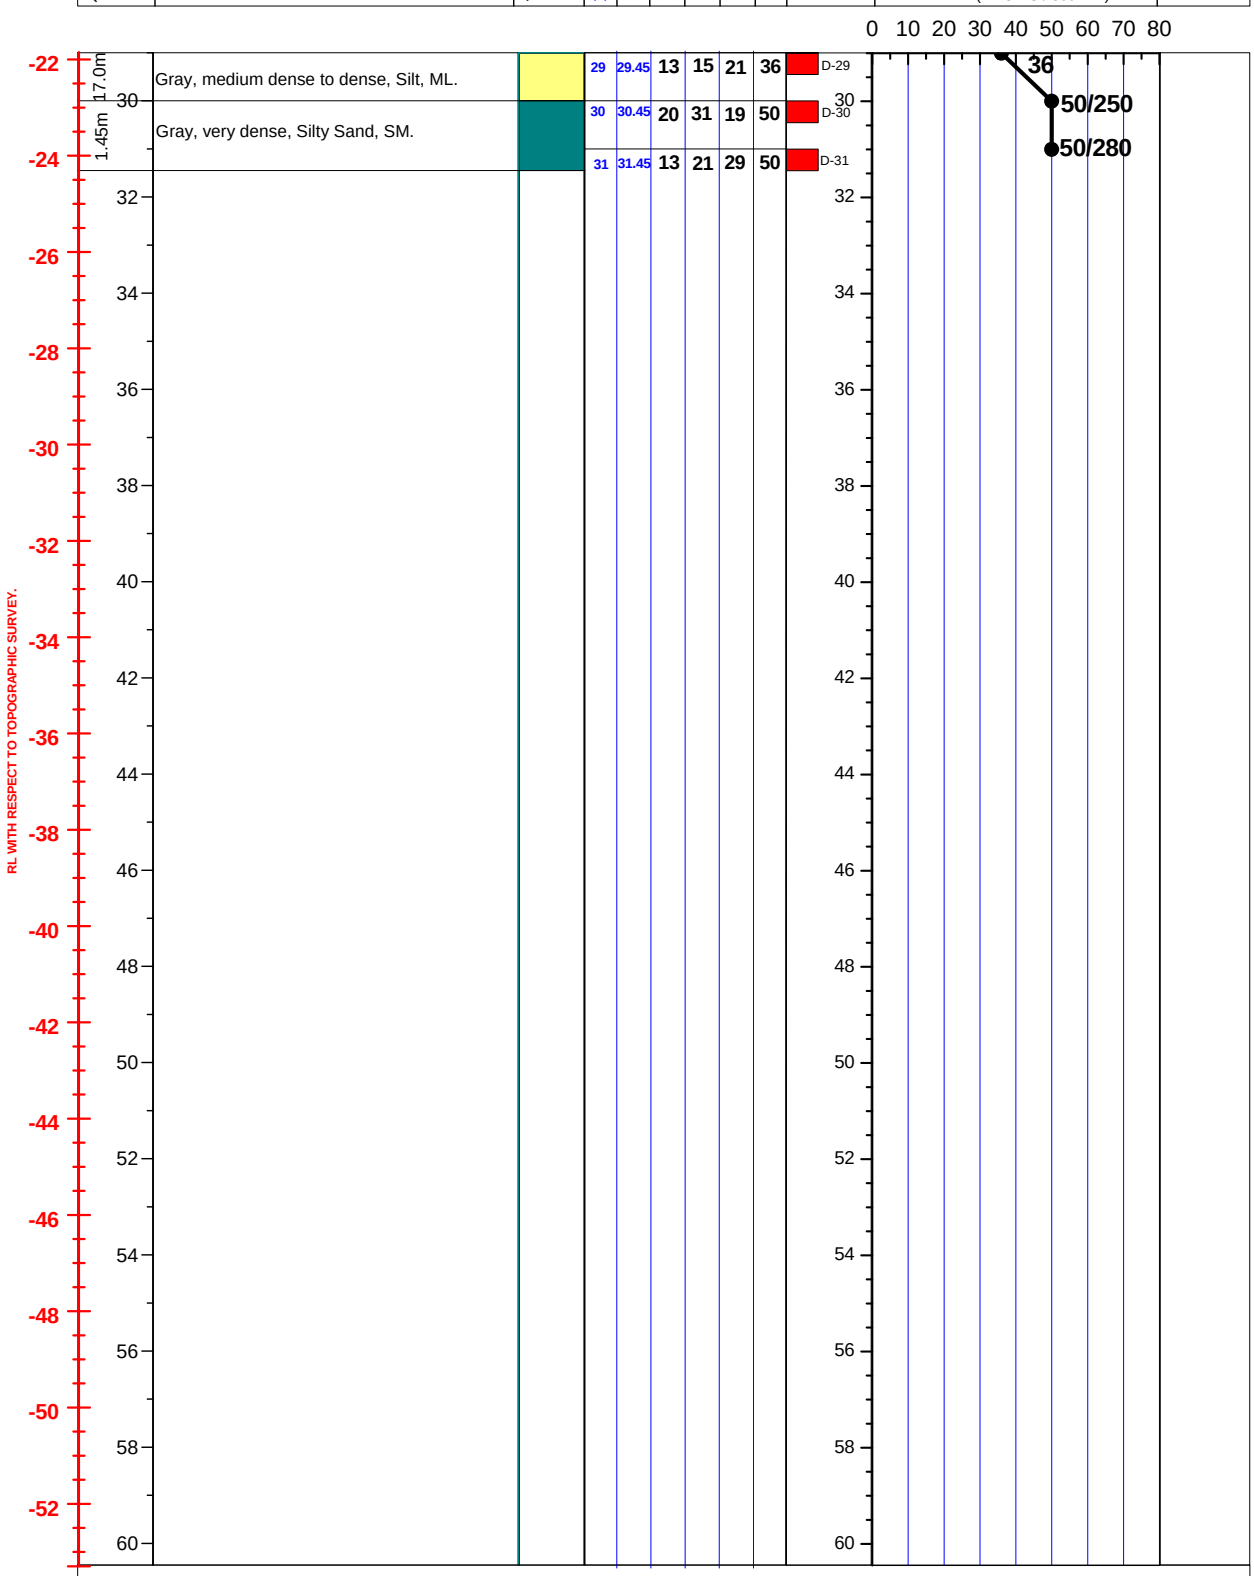


LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

| | | | |
|---|---|---|---|
| PLASTIC CLAY | SILT | PEAT/HIGHLY ORGANIC SOIL | UNDISTURBED SAMPLE |
| MICACEOUS FINE SAND/SILT | SAND | SHALE | DISTURBED SAMPLE |

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX$^{m}$ PENETRATION= 50 BLOWS. AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
