A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION : Durduria, Fulbaria, Mymensingh.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING : 21.0m	R. L.: 0.76m below from Road Level.
CLIENT : Grameenphone Ltd.	DATE OF BORING : 07-07-2007.	G. W. T : 1.82m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
2.0m	Very pale brown 10YR (7/3), medium dense, cohesionless Silt, SM.			D-1 to D-2	7, 10		
1.0m	Gray 10YR (6/1), medium dense to dense, cohesionless Silt, SM.			D-2 to D-3	10, 17		
3.0m	Light gray 10YR (7/2), dense to loose, fine sand, SM.			D-3 to D-6	17, 20, 34, 5		
1.5m	Very pale brown 10YR (7/3), medium plastic, soft, silty Clay, CL.			D-6 to D-7	5, 5		
1.5m	Dark gray 10YR (4/1), Organic soil.			D-7 to D-8	5, 28		
4.5m	Very pale brown 10YR (7/3), medium plastic, very stiff, silty Clay, CL.			D-8 to D-11	28, 25, 26, 28		
7.95m	Yellow 10YR (8/6), dense to very dense,cohesionless Silt, SM.			D-11 to D-16	28, 30, 33, 35, 37, 40		

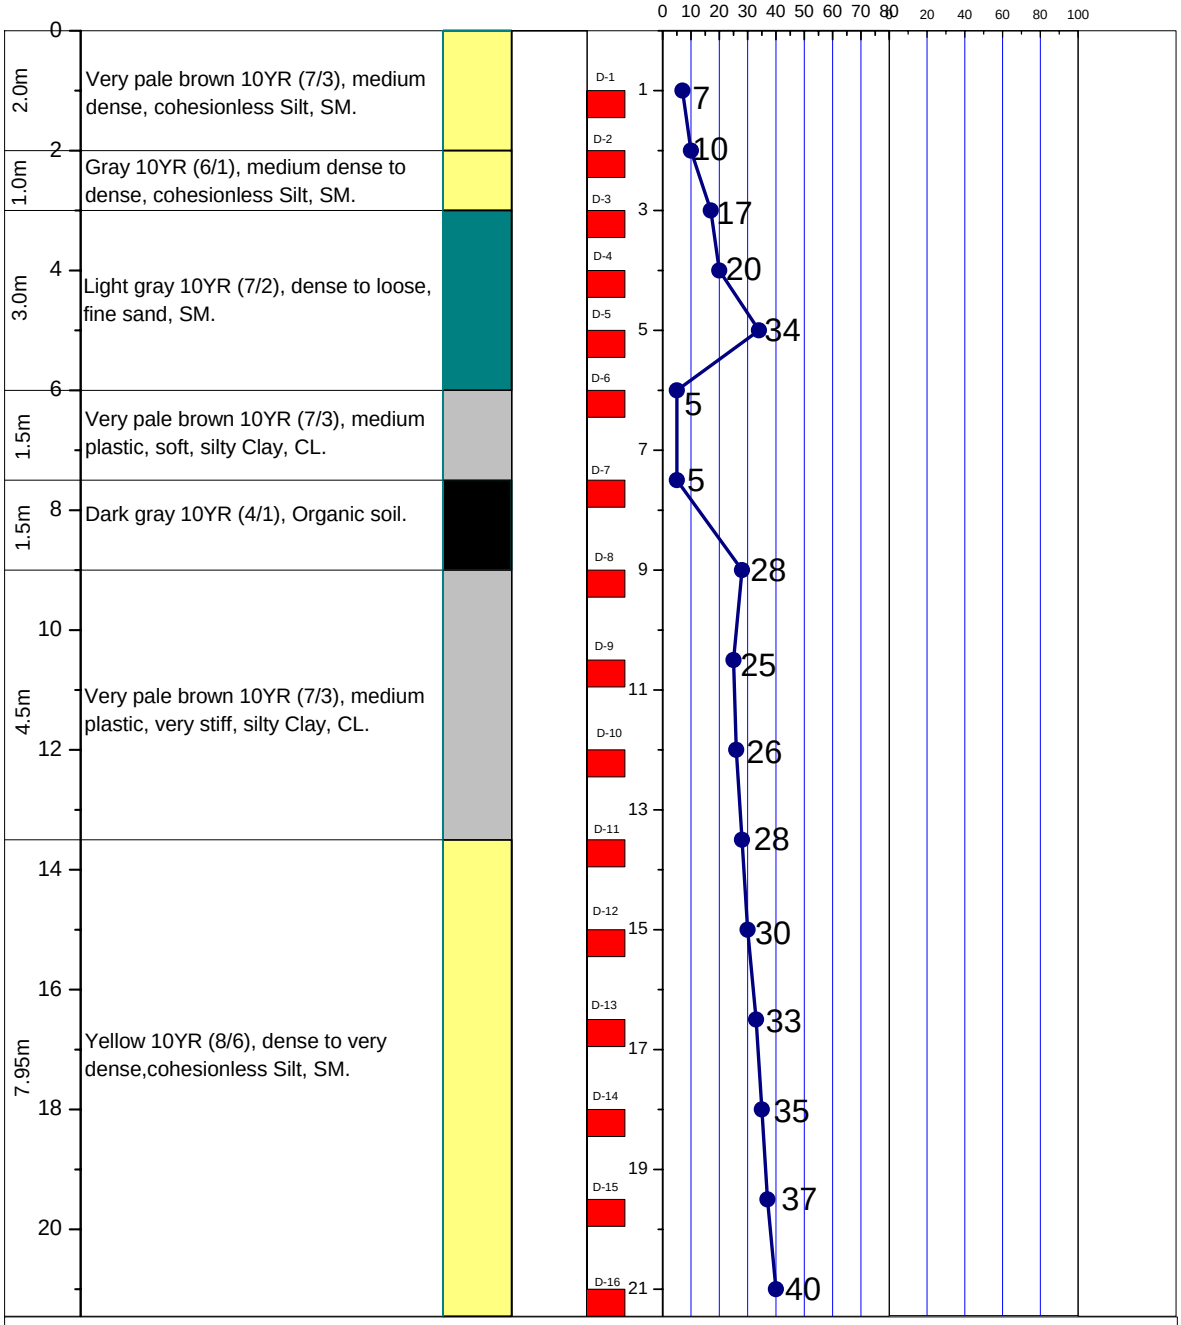

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
