A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION: Ashighor, Judhishthipur, Fenchuganj, Sylhet.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING: 21.0m	R. L.: 0.76m below from Road Level.
CLIENT : Grameenphone Ltd.		DATE OF BORING: 23-10-2013.	G. W. T : 0.30m above from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
6.0m	Yellow 10YR (7/8), high plasticity, soft to stiff, silty Clay, CH.		UD-1, UD-2, UD-3, UD-4	D-1 to D-6	6, 7, 9, 11, 14, 18		
15.45m	Gray 10YR (5/1), dense to very dense, fine Sand, SM.			D-7 to D-16	27, 31, 35, 39, 47, 48, 50, 50, 50, 50		Over, Over, Over, Over

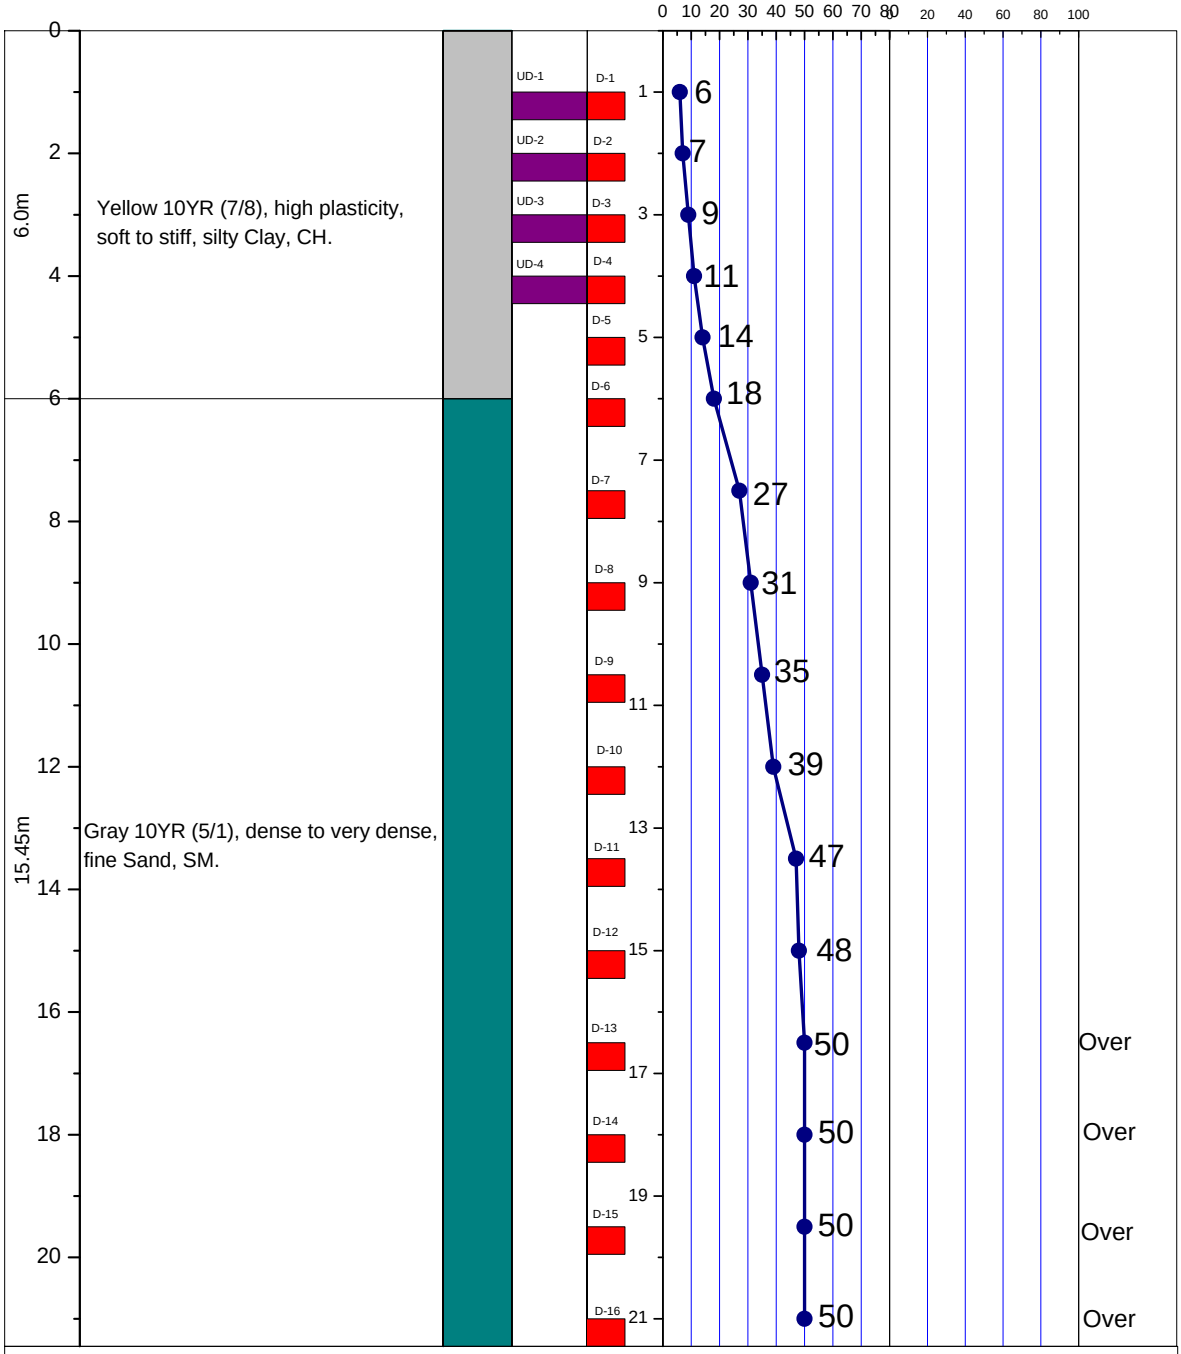

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SHALE	SILT	SAND
PEAT/HIGHLY ORGANIC SOIL	MICACEOUS FINE SAND/SILT	UNDISTURBED SAMPLE	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
