A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION : Sonapur, Baliakandi, Rajbari.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING : 21.0m	R. L.: 0.76m below from Road Level.
CLIENT : Grameen phone Ltd.	DATE OF BORING : 01-04-2005	G. W. T : 2.50m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Light brownish gray 10YR (6/2), very loose to loose, fine sand, SM.			D-1 D-2 D-3	6, 2, 8		
2.0m	Light brownish gray 10YR (6/2), loose, silty Sand, SM.			D-4 D-5	3, 3		
2.5m	Gray colour 10YR (5/1), medium plastic, soft to medium stiff, silty Clay, CL.			D-6 D-7	6, 8		
1.5m	Light brownish gray colour 10YR (6/2), non plastic, medium dense, sandy Silt, SM.			D-8	6		
1.5m	Gray colour 10YR (5/1), medium plastic, medium stiff, silty Clay, CL.			D-9	10		
3.0m	Gray colour 10YR (5/1), medium dense, silty Sand, SM.			D-10	16		
3.0m	Gray colour 10YR (5/1), dense, fine sand, SM.			D-11 D-12	25, 24		
3.0m	Gray colour 10YR (6/1), dense to very dense, fine sand, SM.			D-13 D-14	30, 33		
1.95m	Gray colour 10YR (5/1), very dense, fine sand, SM.			D-15 D-16	31, 34		

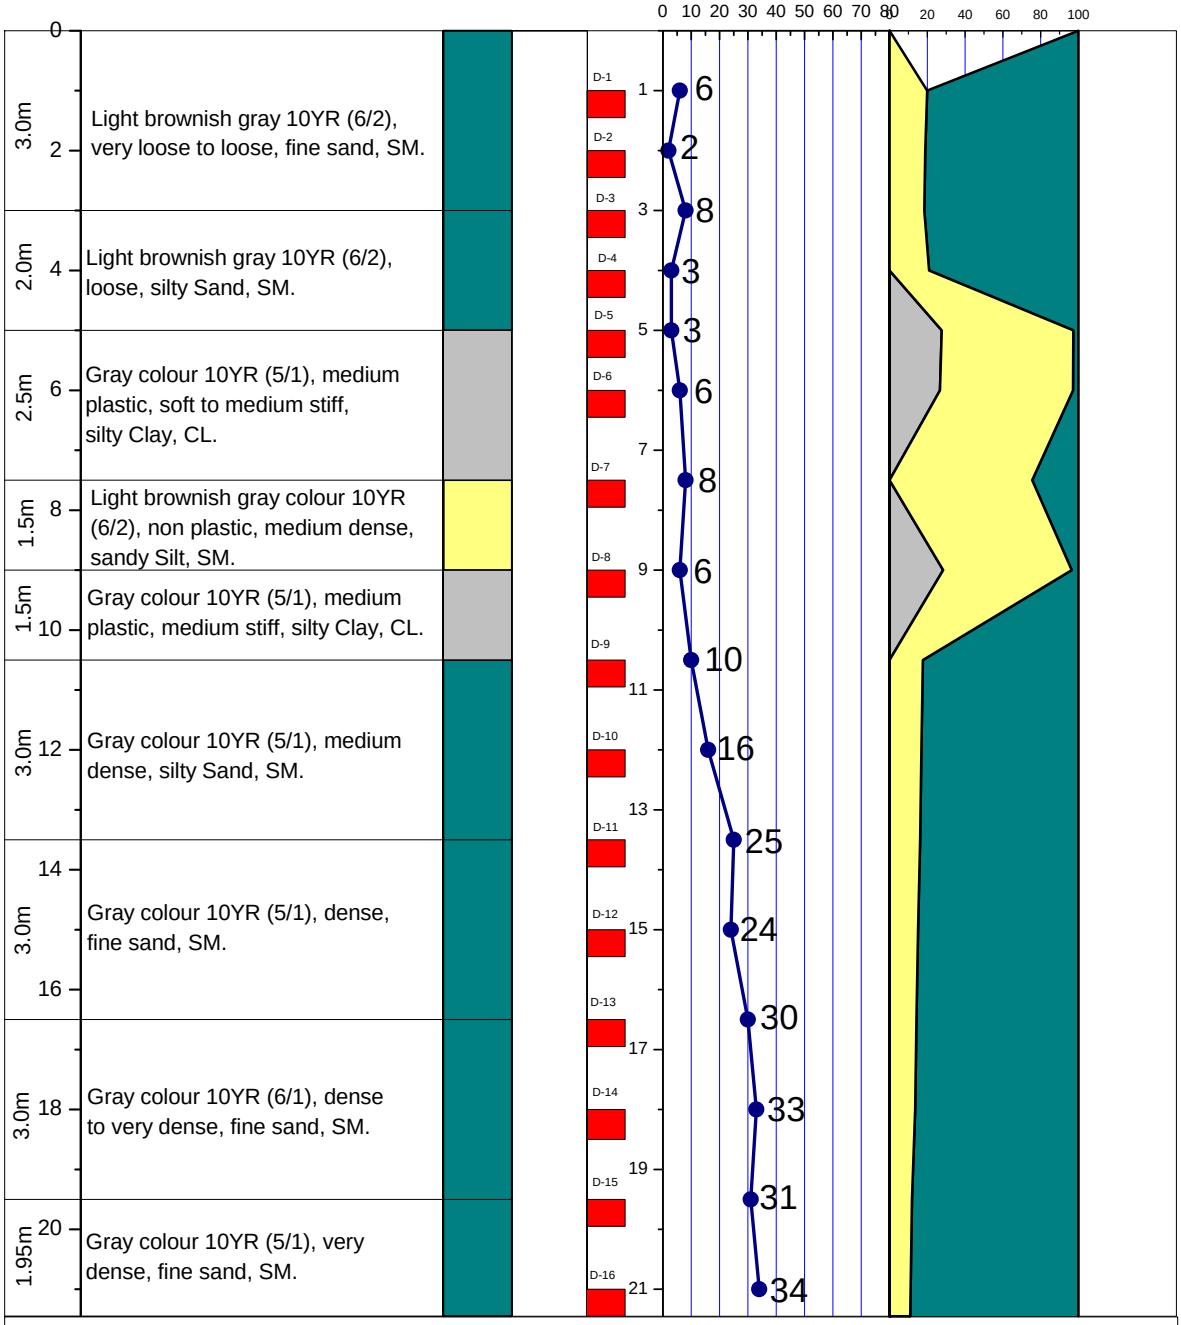

ID FOR BORELOG A RAIN SIZE DISTRIBU

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

UNDISTURBED SAMPLE

ORGANIC

DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
