A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION : Kuakata, Kalapara, Patuakhali.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING : 21.0m	R. L.: On Road Level.
CLIENT : Warid Telecom International Ltd.		DATE OF BORING: 26-02-2011.	G. W. T : 2.44m below from E.G.L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
4.5m	Gray 7.5YR (5/1), high plasticity, very soft to stiff, Clay, CH.		UD-1, UD-2	D-1, D-2	2, 1		
4.5m	Gray 7.5YR (5/1), dense to loose, very fine Sand, ML.			D-3, D-4, D-5, D-6	16, 21, 21, 5		
1.5m	Dark Gray 7.5YR (3/1), medium plasticity, soft to stiff, silty Clay with Mica, CL.			D-7	12		
6.0m	Gray 7.5YR (5/1), medium dense to dense, micaceous Silt, MH.			D-8, D-9, D-10	12, 12, 10		
4.95m	Gray 7.5YR (5/1), dense to very dense, Silt, ML.			D-11, D-12, D-13, D-14	27, 35, 37, 40		

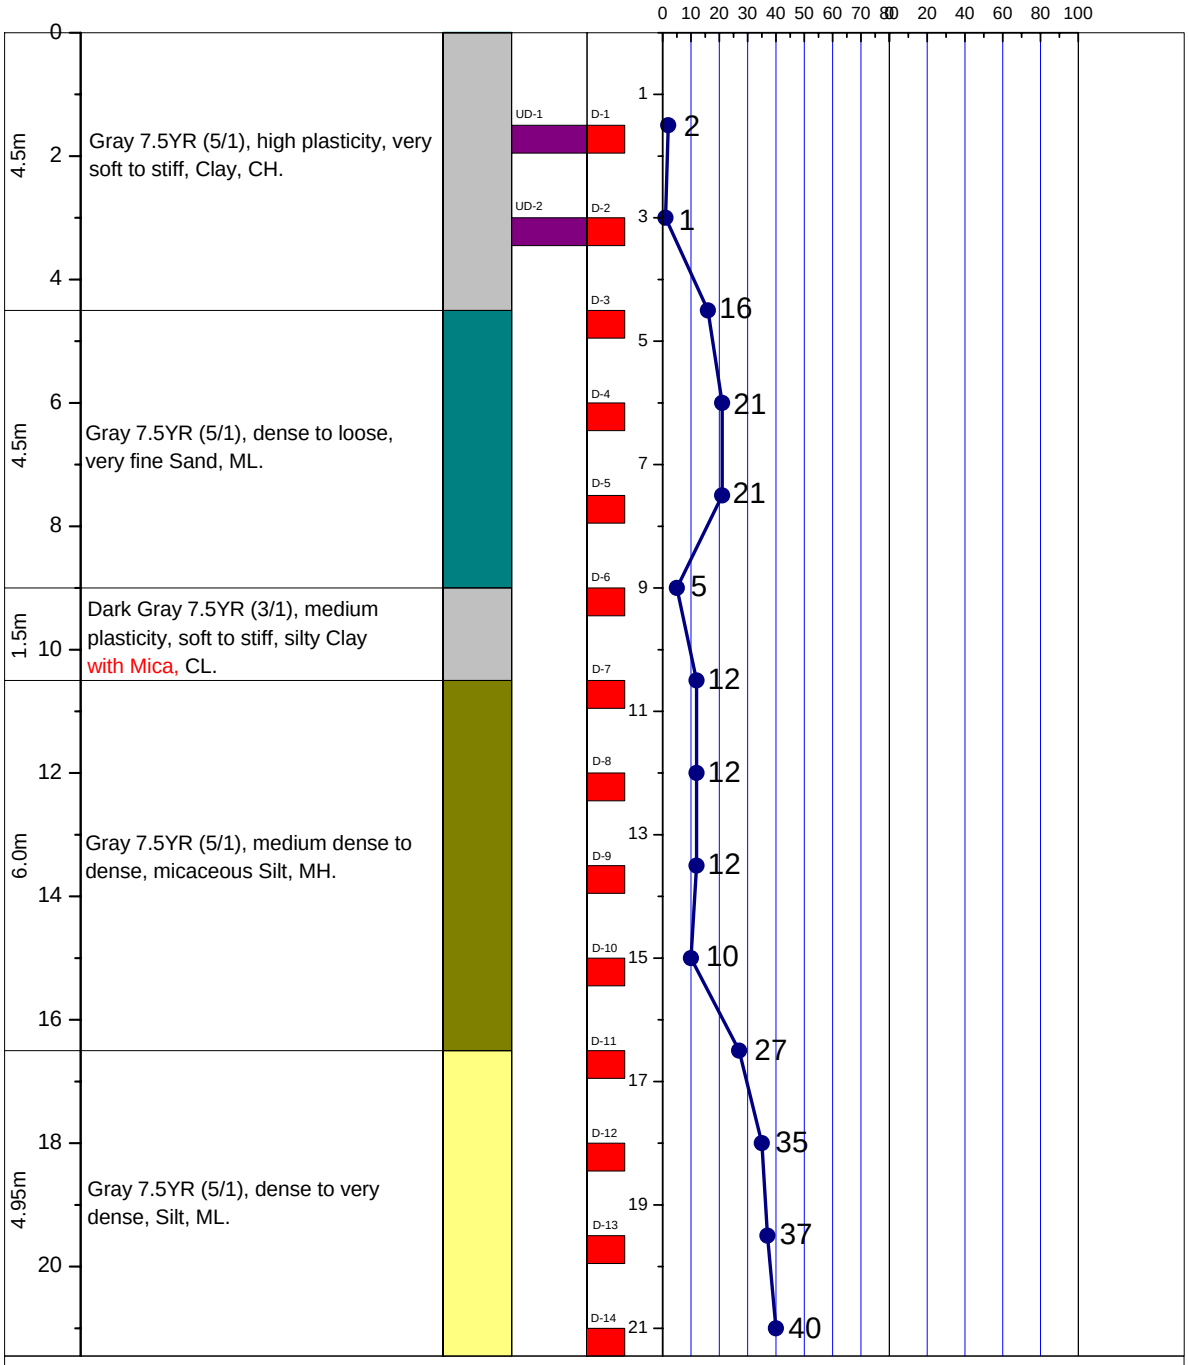

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SAND	SHALE	UNDISTURBED SAMPLE
MICACEOUS FINE SAND/SILT	SILT	PEAT/HIGHLY ORGANIC SOIL	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
