A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION: Ajotari, Gongar Hat, 6 No Kashipur, Fulbari, Kurigram.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING: 21.0m	R. L.: 0.60m below fromRoad Level.
CLIENT : Grameenphone Ltd.		DATE OF BORING: 19-07-2012.	G. W. T : 0.30m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
2.0m	Brown 10YR (6/1), very loose, Silt, ML.			D-1, D-2	2, 2		
3.0m	Brown 10YR (6/1), very loose to loose, silty Sand, SM.			D-3, D-4, D-5	4, 4, 5		
2.5m	Gray 10YR (6/1), loose, fine Sand, SM.			D-6, D-7	5, 6		
1.5m	Gray 10YR (6/1), loose to medium dense, fine Sand (with mica), SM.			D-8	10		
12.45m	Gray 10YR (6/1), medium dense to very dense, fine Sand, SM.			D-9, D-10, D-11, D-12, D-13, D-14, D-15, D-16	12, 14, 20, 27, 19, 30, 30, 31		

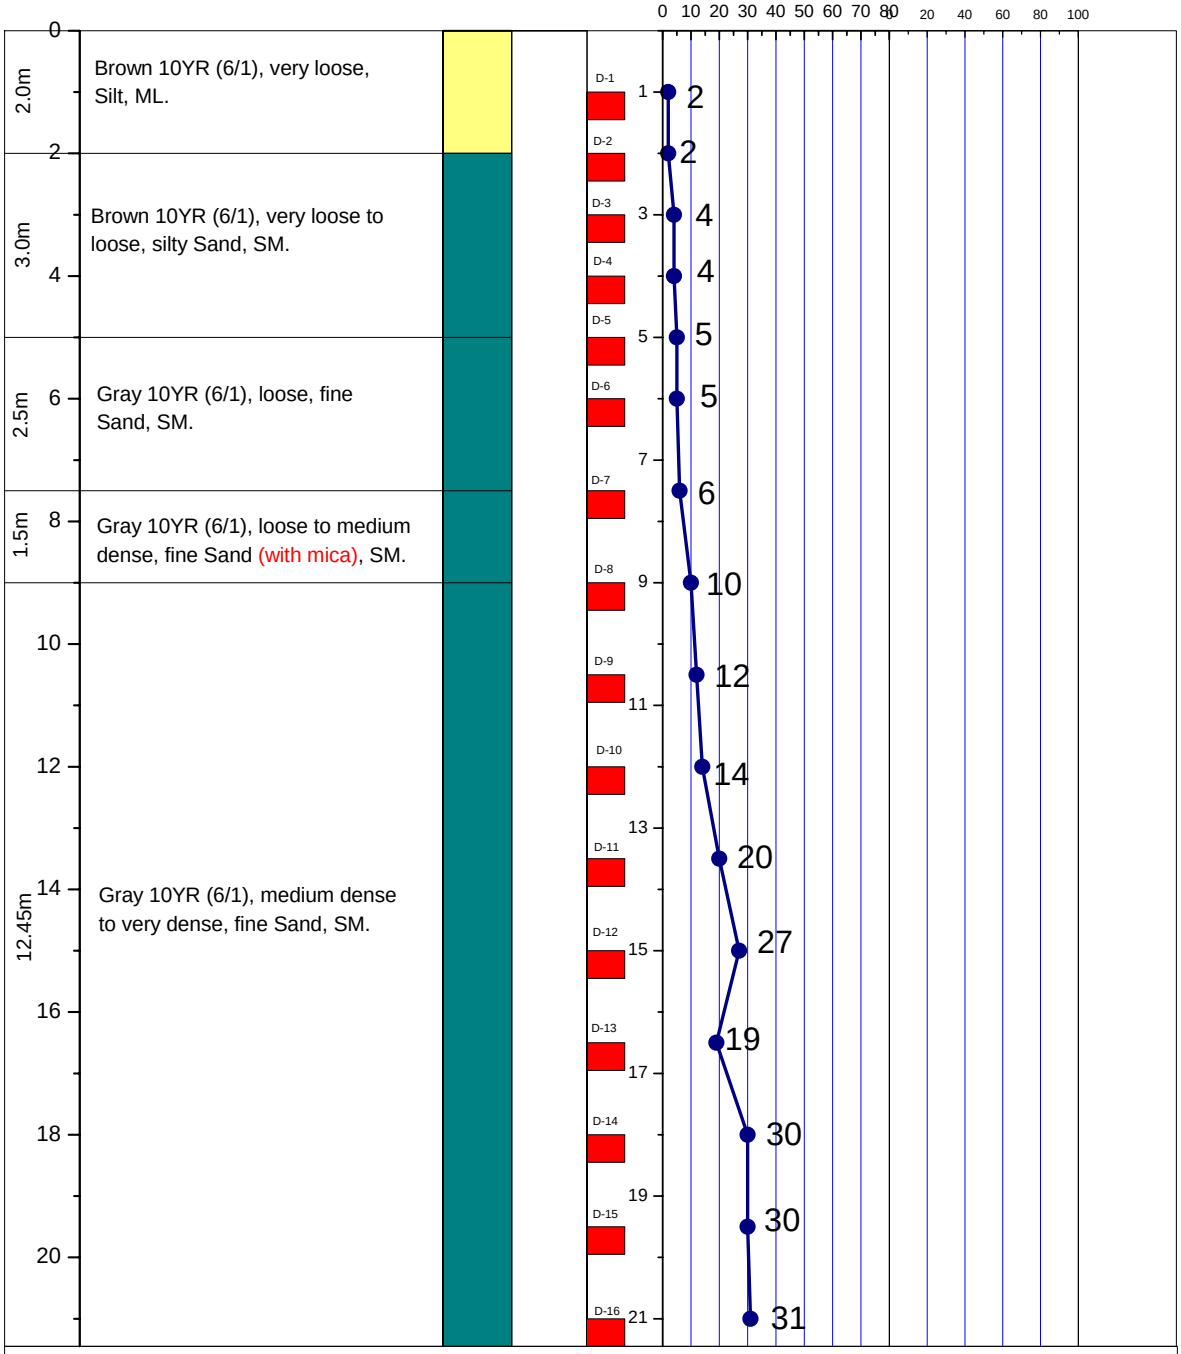

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY | SHALE | SILT | SAND

PEAT/HIGHLY ORGANIC SOIL | MICACEOUS FINE SAND/SILT | UNDISTURBED SAMPLE | DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
