A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION : Kattoli Jame Mosjid, Kattoli Bazar, Longgodu, Rangamati.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING : 10.5m	R. L.: On Road Level.
CLIENT : TELETALK BANGLADESH LTD.		DATE OF BORING: 08-11-2012.	G. W. T : 1.22m below from E.G.L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
6.0m	Week Red 10YR (5/4), medium dense to very dense, silty Sand, SM.			D-1, D-2, D-3, D-4	9, 12, 24, 42		
3.0m	Grayish Brown 10YR (5/2), very dense, clayey Silt, ML.			D-5	50		Over
1.95m	Week Red 10YR (5/4), very dense, fine Sand, SM.			D-6	50		Over
	Boring was not possible due to very dense fine Sand.			D-7	50		Over

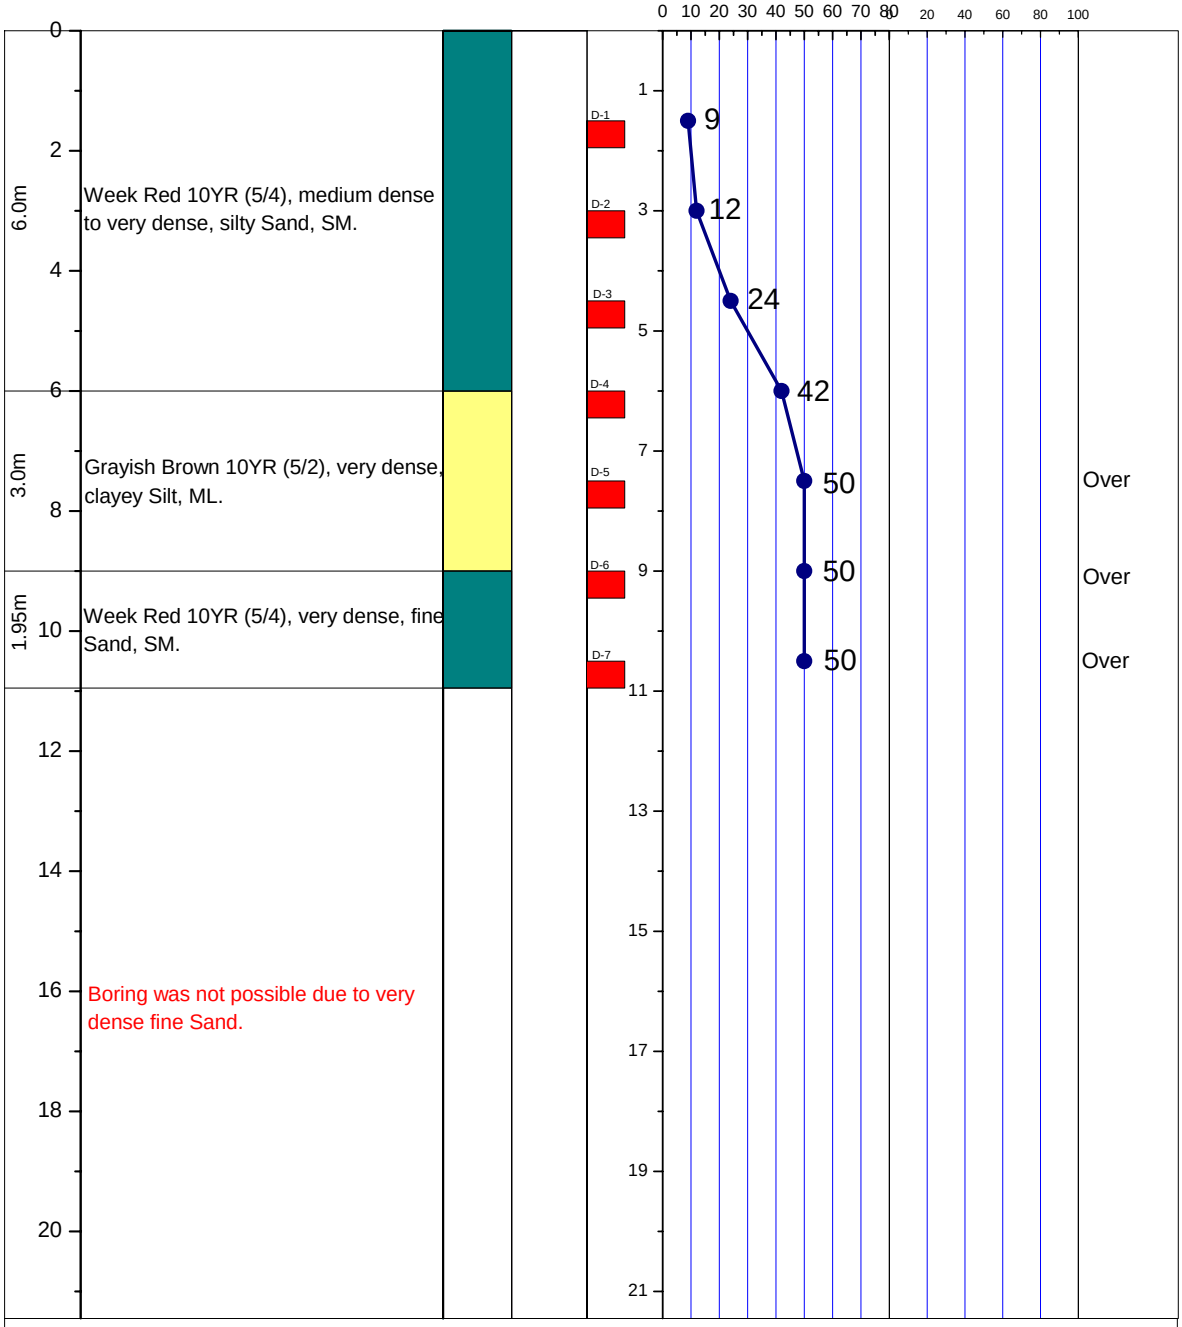

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SAND	SHALE	UNDISTURBED SAMPLE
MICACEOUS FINE SAND/SILT	SILT	PEAT/HIGHLY ORGANIC SOIL	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
