A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION: Panihara, 5 No Rosulpur, Niamotpur, Naogaon.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING: 21.0m	R. L.: Road Level.
CLIENT : Grameenphone Ltd.	DATE OF BORING: 12-08-2012.	G. W. T : 0.61m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
2.0m	Gray Gley2 (7/1), high plasticity, stiff, silty Clay, CL. **(Weathered)**			D-1 D-2 D-3 D-4 D-5 D-6 D-7 D-8	16 23 27 38 45 50 50 50		Over Over
7.45m	Gray Gley2 (7/1), high plasticity, stiff to very stiff, silty Clay, CH.						
12.0m	**Boring was terminated due to high palsticity, very stiff, silty clay, CH.**						

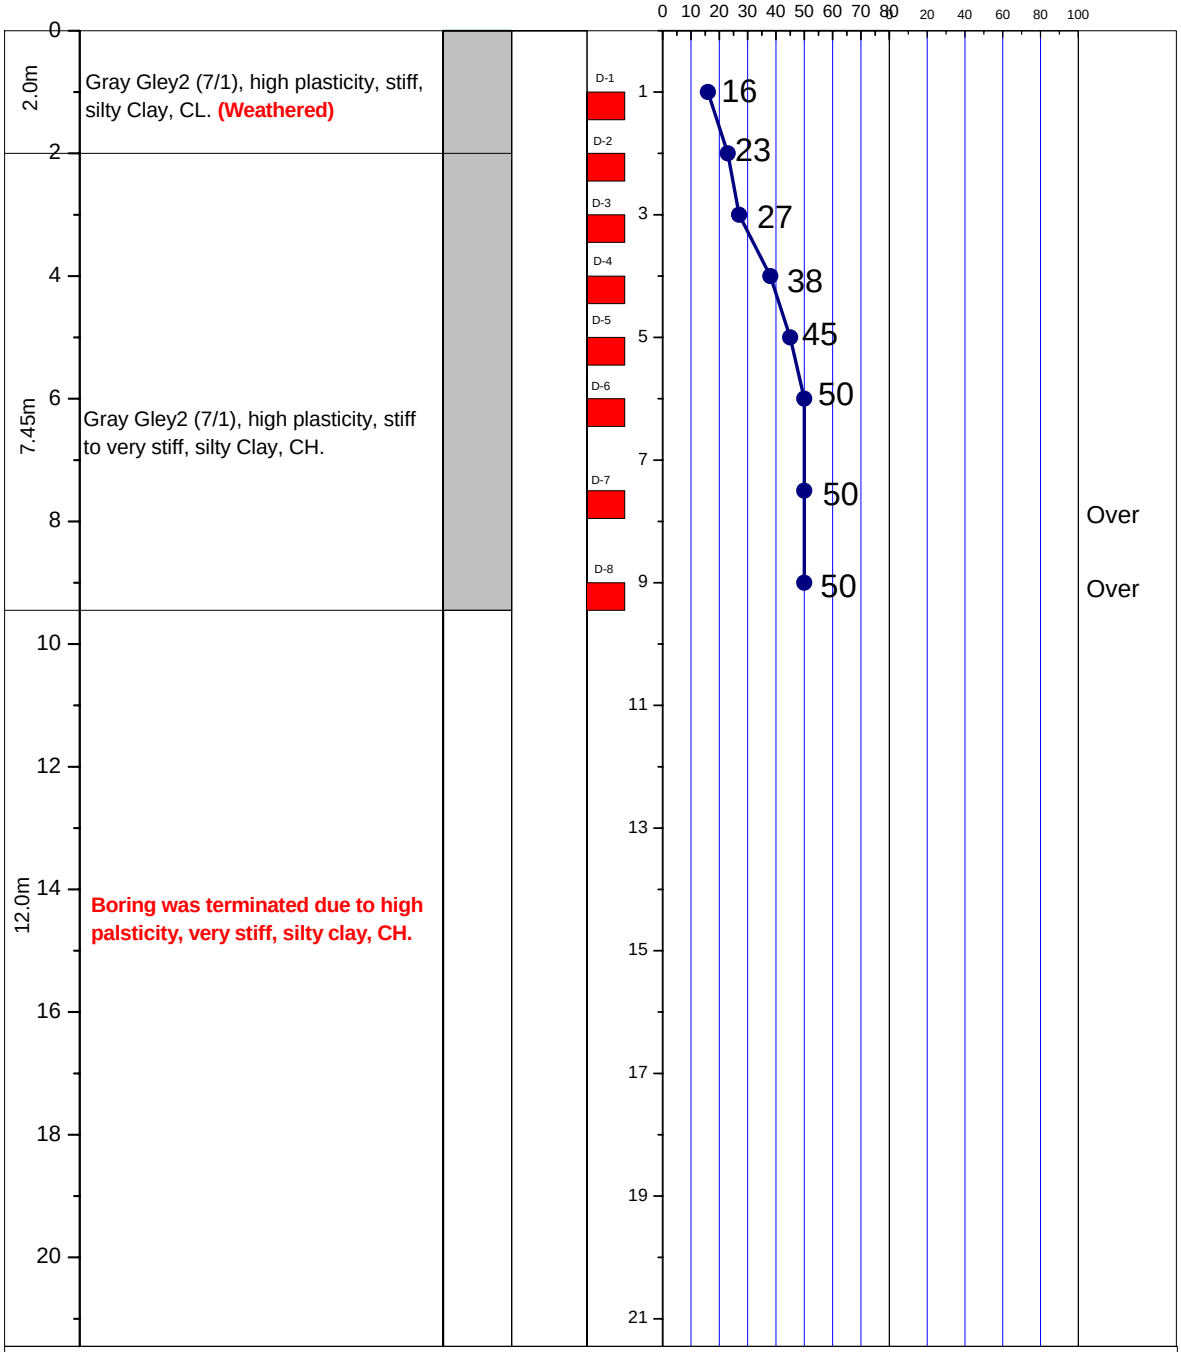

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SHALE	SILT	SAND
PEAT/HIGHLY ORGANIC SOIL	MICACEOUS FINE SAND/SILT	UNDISTURBED SAMPLE	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
