A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION: Shakarbati Biswaspara, 6 No. Shankarbati Union, Bat Tolar Hat, Sadar, Chapai Nawabganj.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING: 21.0m	R. L.: 0.15m below from Road Level.
CLIENT : Grameenphone Ltd.		DATE OF BORING: 02-05-2012.	G. W. T : 2.13m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Light Gray 10YR (7/1), medium plasticity, stiff to very stiff, silty Clay, CL.		UD-1, UD-2, UD-3, UD-4	D-1 to D-16	14, 20, 27, 27, 26, 27, 26, 27, 30, 31, 29, 30, 32, 34, 35, 36		
18.45m	Light Gray 10YR (7/1), high plasticity, very stiff, Clay, CH.						

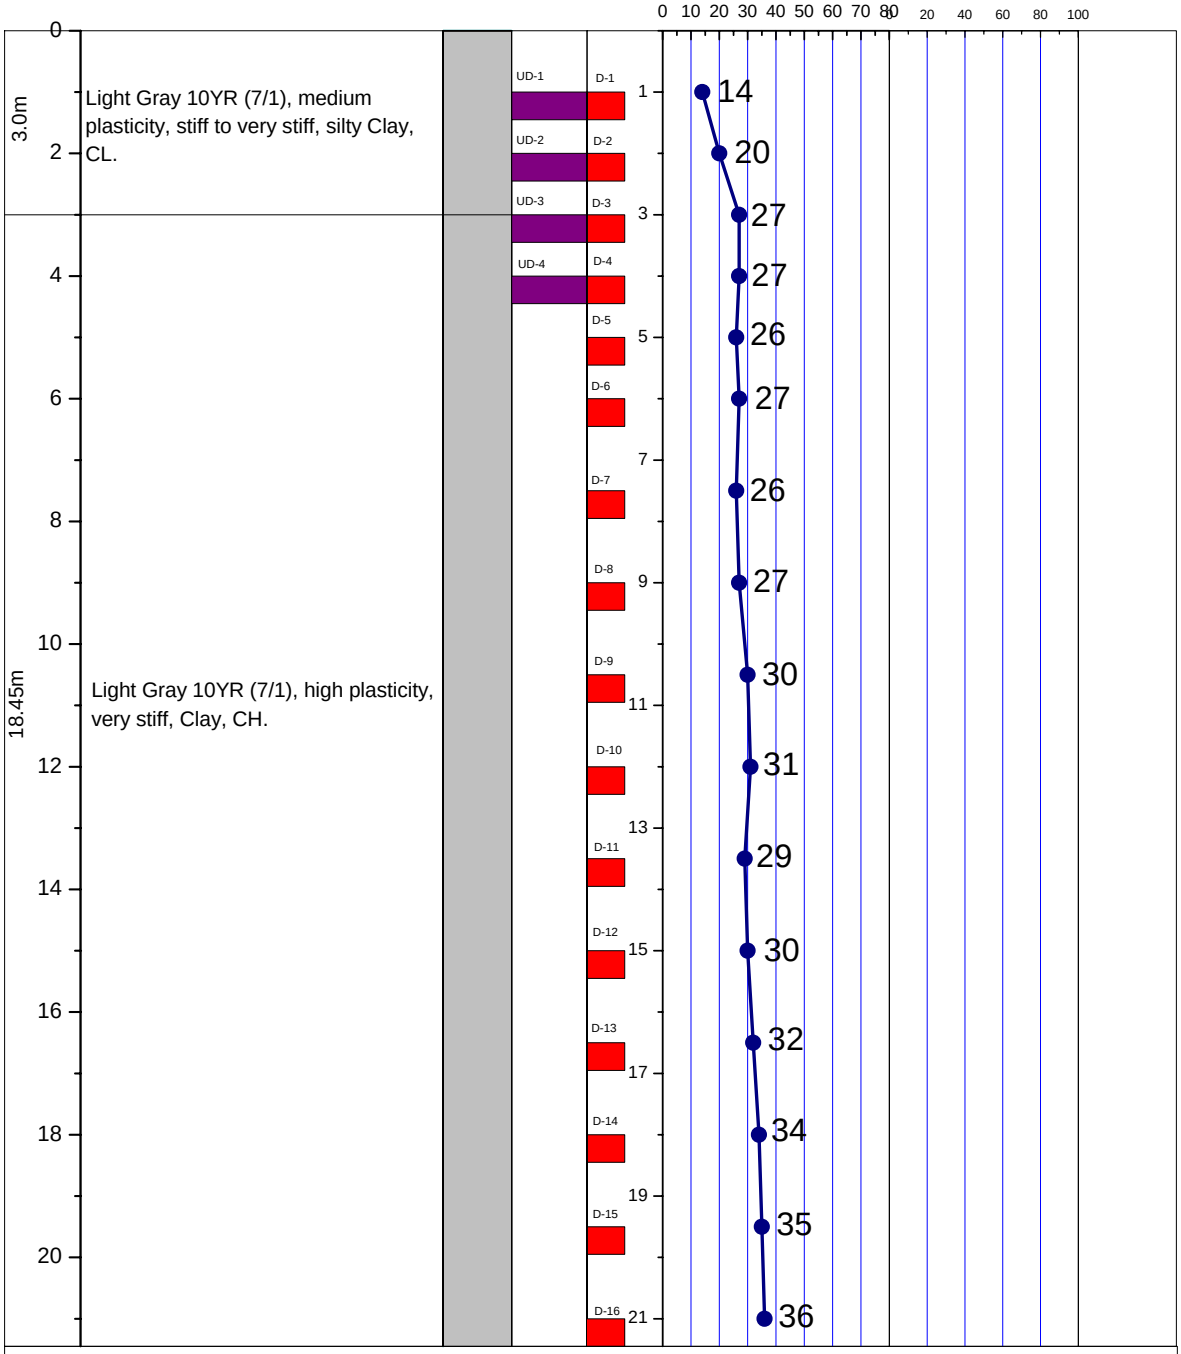

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY | SHALE | SILT | SAND

PEAT/HIGHLY ORGANIC SOIL | MICACEOUS FINE SAND/SILT | UNDISTURBED SAMPLE | DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
