A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION: Chowmohani, Saidpur, Nilphamari.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING: 21.0m	R. L.: 0.91m below from Road Level.
CLIENT : Orascom Telecom Bangladesh Limited.		DATE OF BORING : 09-09-2011.	G. W. T : 0.91m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
2.0m	Light Gray 10YR (7/1), very loose to loose, silty Sand, SM.			D-1 to D-2	2, 5		
8.5m	Gray 10YR (5/1), loose to dense, fine Sand, SM.			D-3 to D-9	7, 7, 8, 12, 13, 20, 26		
10.95m	Light Gray 10YR (7/1), dense to very dense, fine Sand, SM.			D-10 to D-16	28, 26, 35, 38, 40, 42, 45		

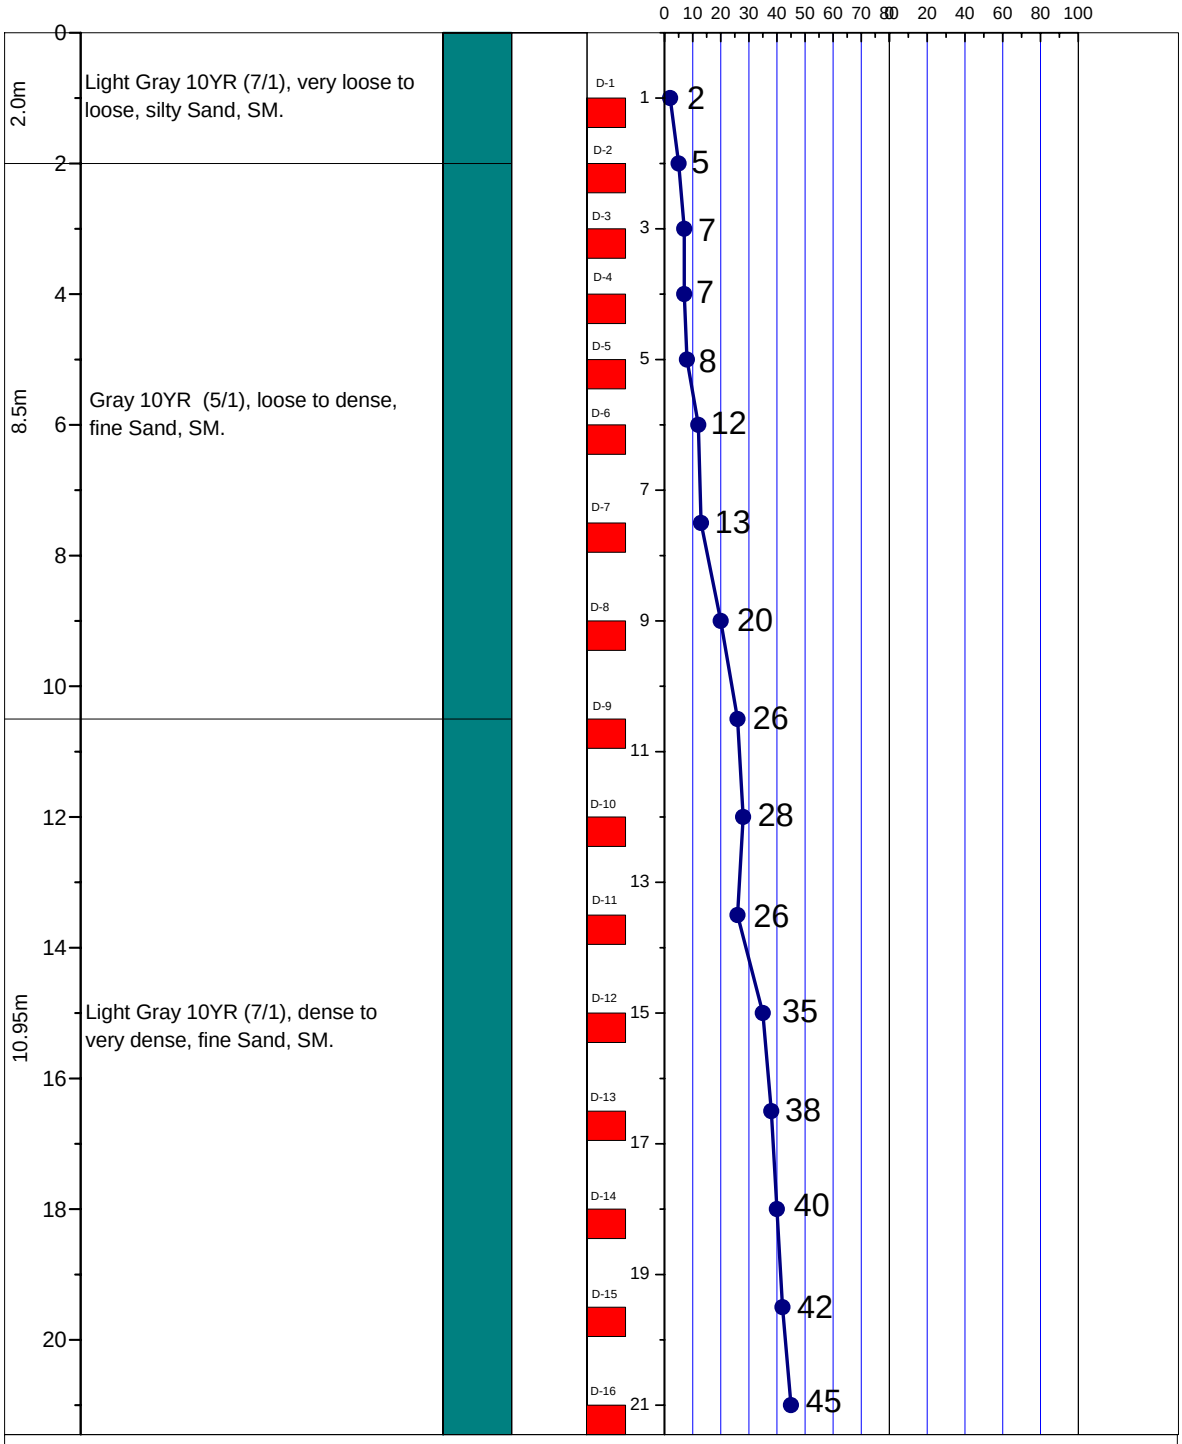

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SAND	SILT	SHALE
PEAT/HIGHLY ORGANIC SOIL	MICACEOUS FINE SAND/SILT	UNDISTURBED SAMPLE	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS
AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
