A2	PROSOIL	BOREHOLE NO: BH-1	
		Vill: Char Bisnopur, Po: Char Bisnopur,Ps: Sadarpur, Dist: Faridpur.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING: 21.0m	R. L.: 2.13m below from Road Level.
CLIENT : AXIATA (Bangladesh) Ltd.		DATE OF BORING: 11-01-2015.	B. W. T : 3.35m below from E. G. L.

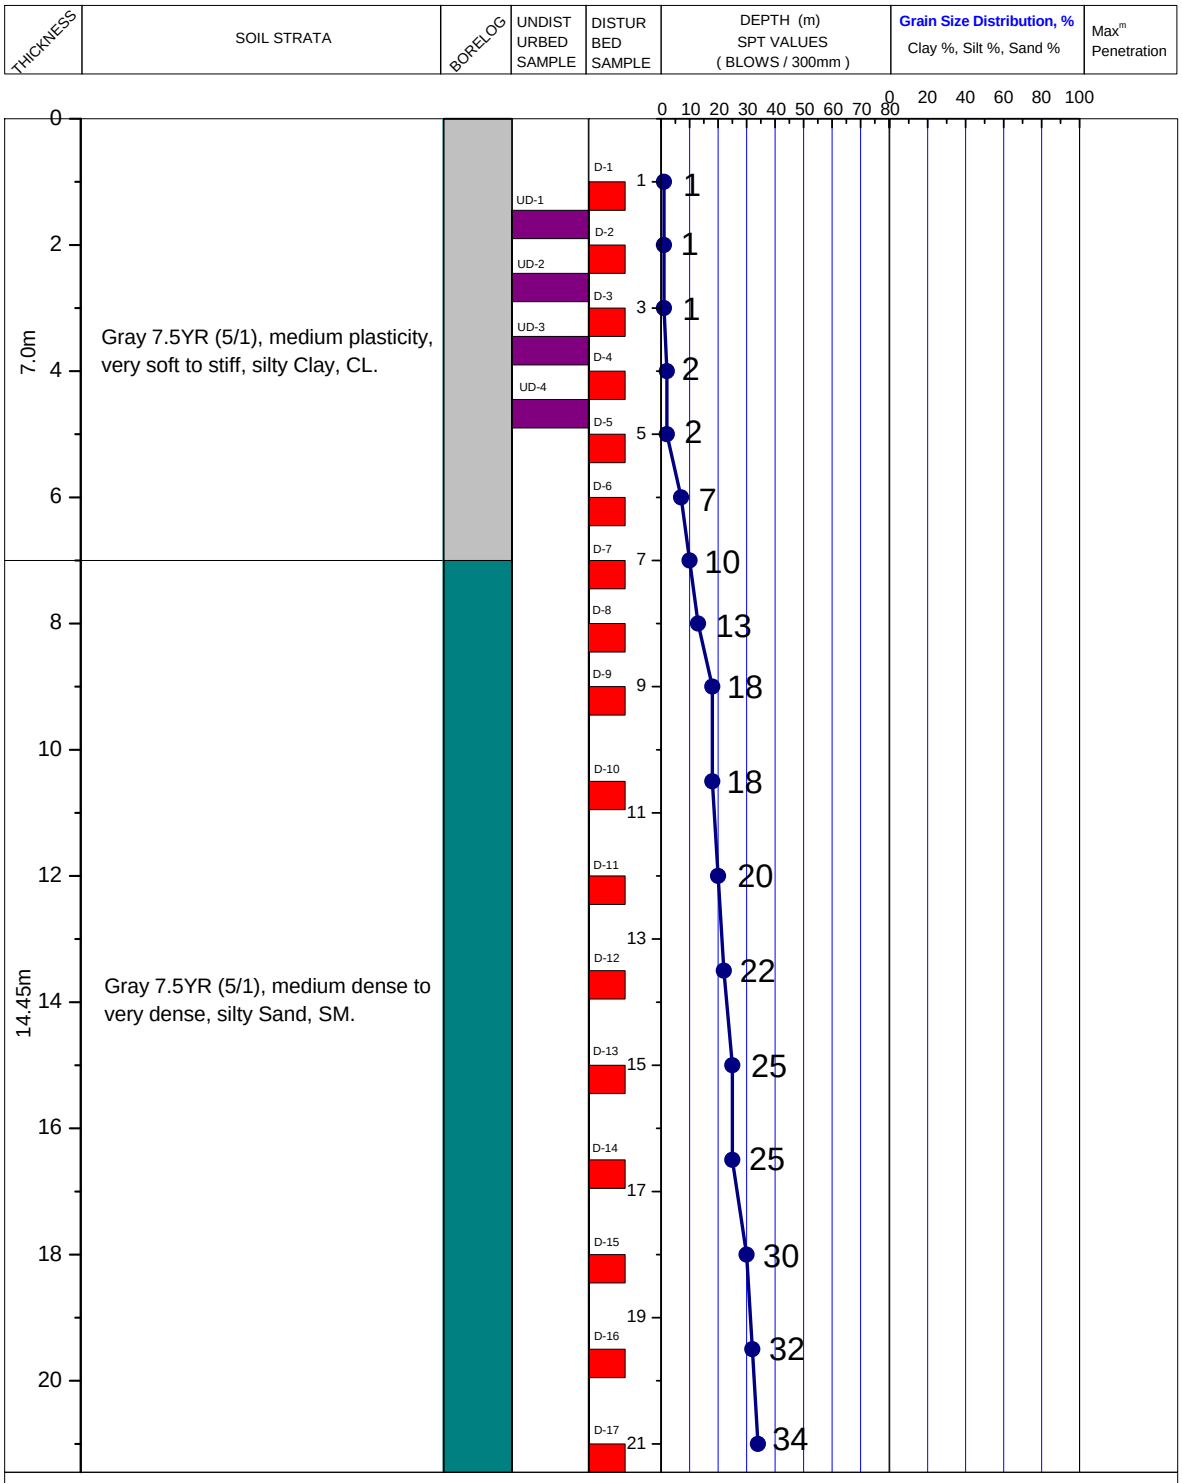

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SAND	SILT	SHALE
PEAT/HIGHLY ORGANIC SOIL	MICACEOUS FINE SAND/SILT	UNDISTURBED SAMPLE	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^m PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED

PROSOIL FOUNDATION CONSULTANT DHAKA-1205 68/B, INDIRA ROAD

Md. Shamsul Islam

(Engr. Md. Shamsul Islam)
B. Sc. Engg. (Civil, BUET),
M. Engg. (Geotech), MCSD, FIEB, CCPE
Chief Executive
Prosoil Foundation Consultant
