A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION : Vorasar Bazar, Burichong, Comilla.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING : 21.0m	R. L.: 0.30m below from Road Level.
CLIENT : Sheba Telecom (PVT.) Ltd.	DATE OF BORING : 13-07-2007.	G. W. T : 0.60m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
1.06m	Dust of rice mill.			D-2	18		
1.94m	Light gray 10YR (7/2), dense, cohesionless silt, SM.			D-3	20		
2.0m	Brown 10YR (5/3), dense, cohesionless silt, SM.			D-4	24		
4.0m	Light gray 10YR (7/2), dense, cohesionless silt, SM.			D-5 D-6 D-7	27 30 23		
12.45m	Light gray 10YR (7/2), medium plastic, very stiff, silty Clay, CL.			D-8 D-9 D-10 D-11 D-12 D-13 D-14 D-15 D-16	26 28 30 29 31 33 32 32 31		

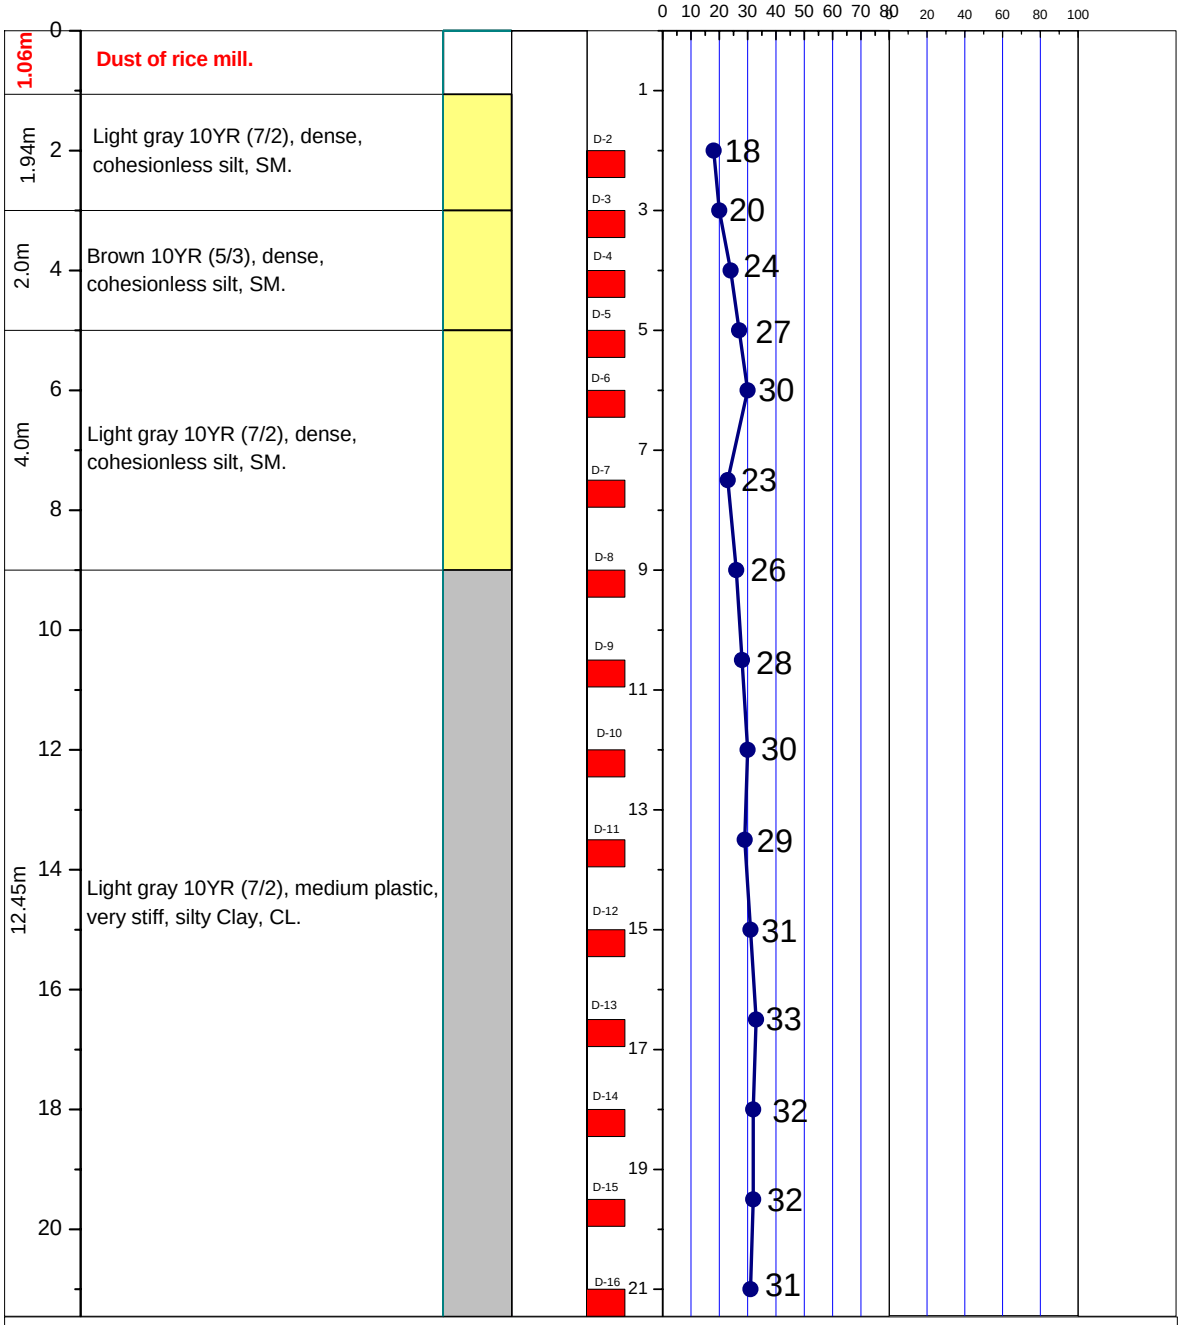

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
