A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION: Rupbaburhat, Shariatpur.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING: 21.0m	R. L.: 1.52m below from Road Level.
CLIENT : AXIATA (Bangladesh) Ltd.		DATE OF BORING: 03-07-2010.	G. W. T : 3.96m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Brown 7.5YR (8/3), loose, silty Sand, SM.			D-1 to D-3	3, 3, 3		
5.0m	Bluish Gray Gley2 (6/1), loose to dense, fine Sand, SM.			D-4 to D-7	4, 20, 27, 18		
2.5m	Dark Gray Gley2 (4/1), medium dense, fine Sand, SM.			D-8 to D-10	8, 6, 14		
9.95m	Light bluish Gray Gley2 (7/1), medium dense to very dense, fine Sand, SM.			D-10 to D-17	18, 21, 25, 28, 35, 45, 48		

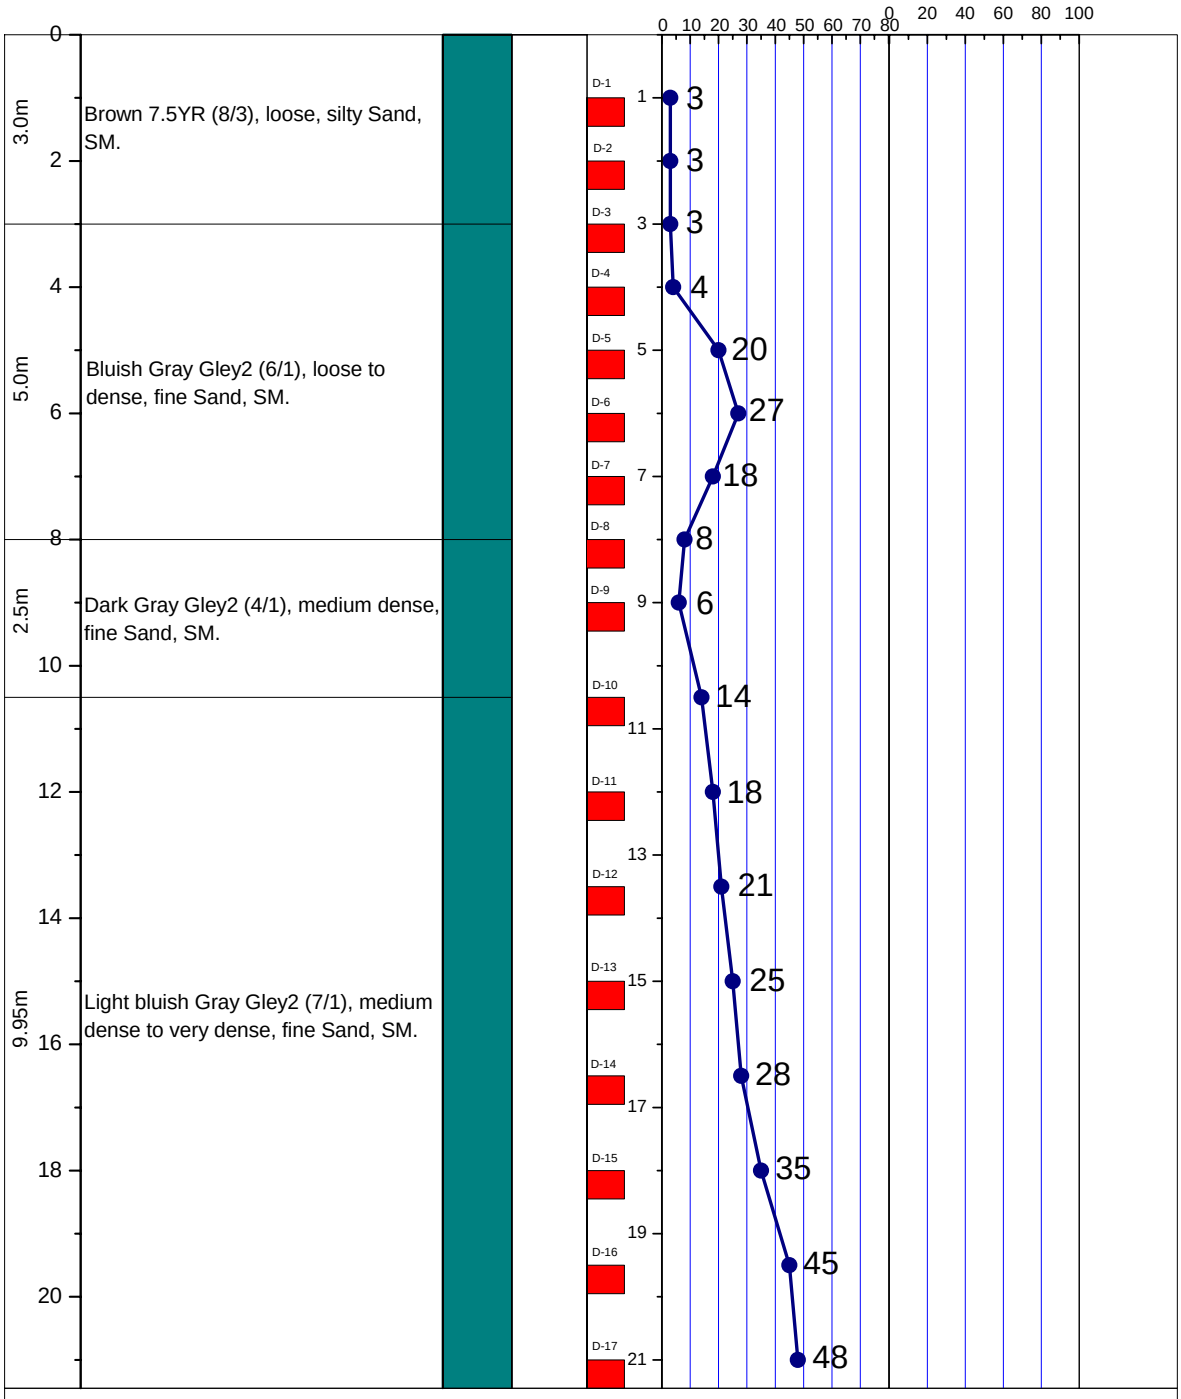

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SAND	SILT	SHALE
PEAT/HIGHLY ORGANIC SOIL	MICACEOUS FINE SAND/SILT	UNDISTURBED SAMPLE	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
