A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION : Darogarhat, Sagolnyea, Feni.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING : 21.0m	R. L.: 2.13m below from Road Level.
CLIENT : Sheba Telecom (PVT.) Ltd.	DATE OF BORING : 07-02-2008.	G. W. T : 0.07m above from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
5.0m	Gray 10YR (5/1), medium plastic, soft to medium stiff, silty Clay, CL.		UD-1, UD-2, UD-3, UD-4	D-1 to D-5	4, 3, 7, 8, 9		
2.5m	Very pale brown 10YR (6/3), medium plastic, medium stiff to very stiff, silty Clay, CL.			D-6	13		
1.5m	Gray 10YR (5/1), dense, fine sand, SM.			D-7, D-8	22, 25		
12.45m	Very pale brown 10YR (6/3), high plastic, very stiff, silty Clay, CH.			D-9 to D-16	30, 34, 40, 35, 33, 36, 38, 41		

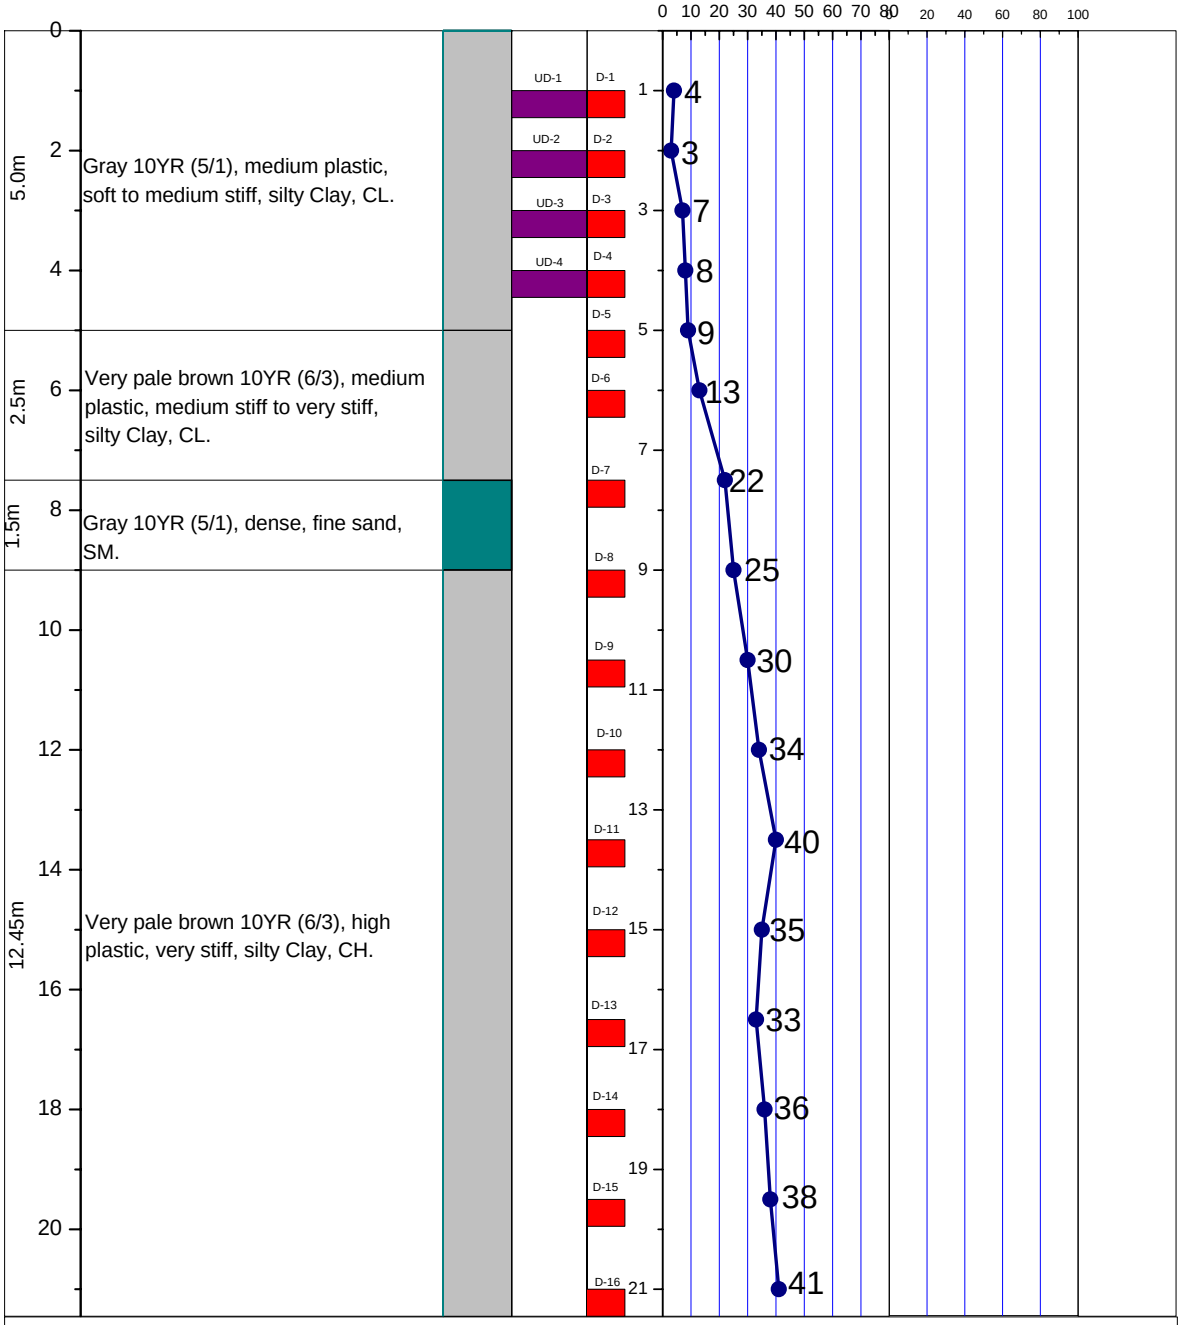

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
