A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION: Habispur, Doulatnagar, 4 No. Bahubal Union, Bahubal, Hobiganj.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING: 21.0m	R. L.: 0.66m below from Road Level.
CLIENT : Grameenphone Ltd.		DATE OF BORING: 07-05-2013.	G. W. T : 1.22m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration

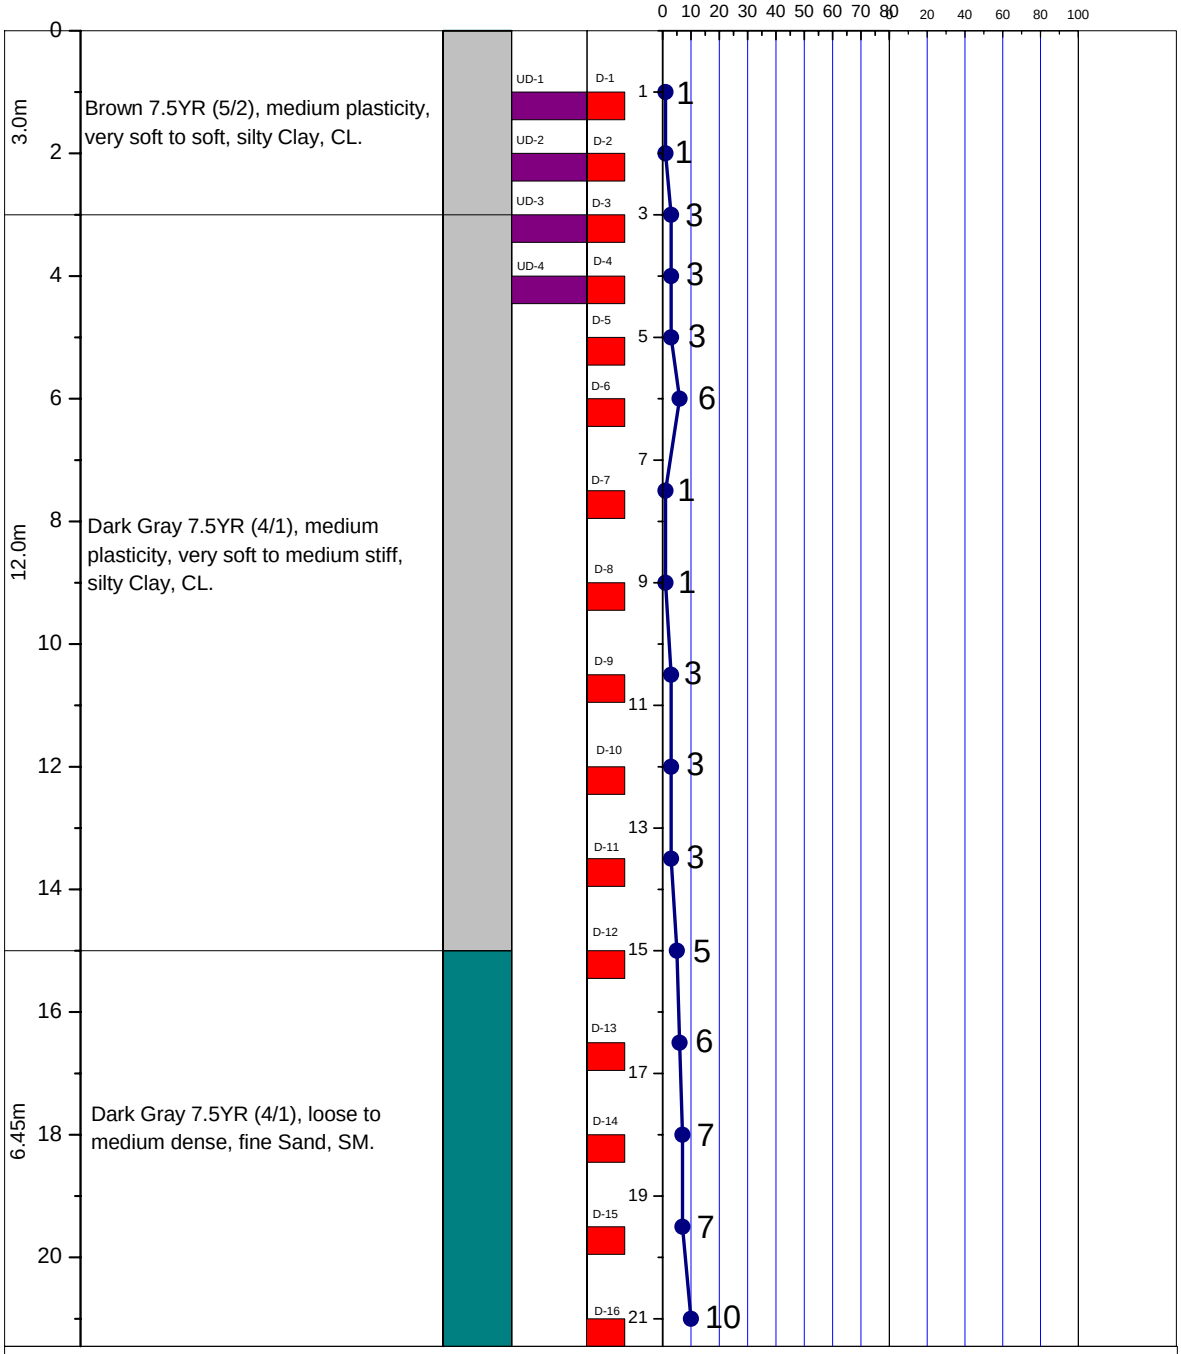

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY | SHALE | SILT | SAND

PEAT/HIGHLY ORGANIC SOIL | MICACEOUS FINE SAND/SILT | UNDISTURBED SAMPLE | DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED

A2	PROSOIL	BOREHOLE NO: BH-2	
		LOCATION: Habispur, Doulatnagar, 4 No. Bahubal Union, Bahubal, Hobiganj.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING: 21.0m	R. L.: 0.66m below from Road Level.
CLIENT : Grameenphone Ltd.		DATE OF BORING: 08-05-2013.	G. W. T : 1.22m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Brown 7.5YR (5/2), medium plasticity, very soft to soft, silty Clay, CL.		UD-1, UD-2, UD-3, UD-4	D-1 to D-5	1, 1, 4, 3, 2		
12.0m	Dark Gray 7.5YR (4/1), medium plasticity, very soft to medium stiff, silty Clay, CL.			D-6 to D-10	5, 1, 1, 2, 6		
6.45m	Dark Gray 7.5YR (4/1), loose to medium dense, fine Sand, SM.			D-11 to D-16	6, 5, 5, 8, 9, 10		

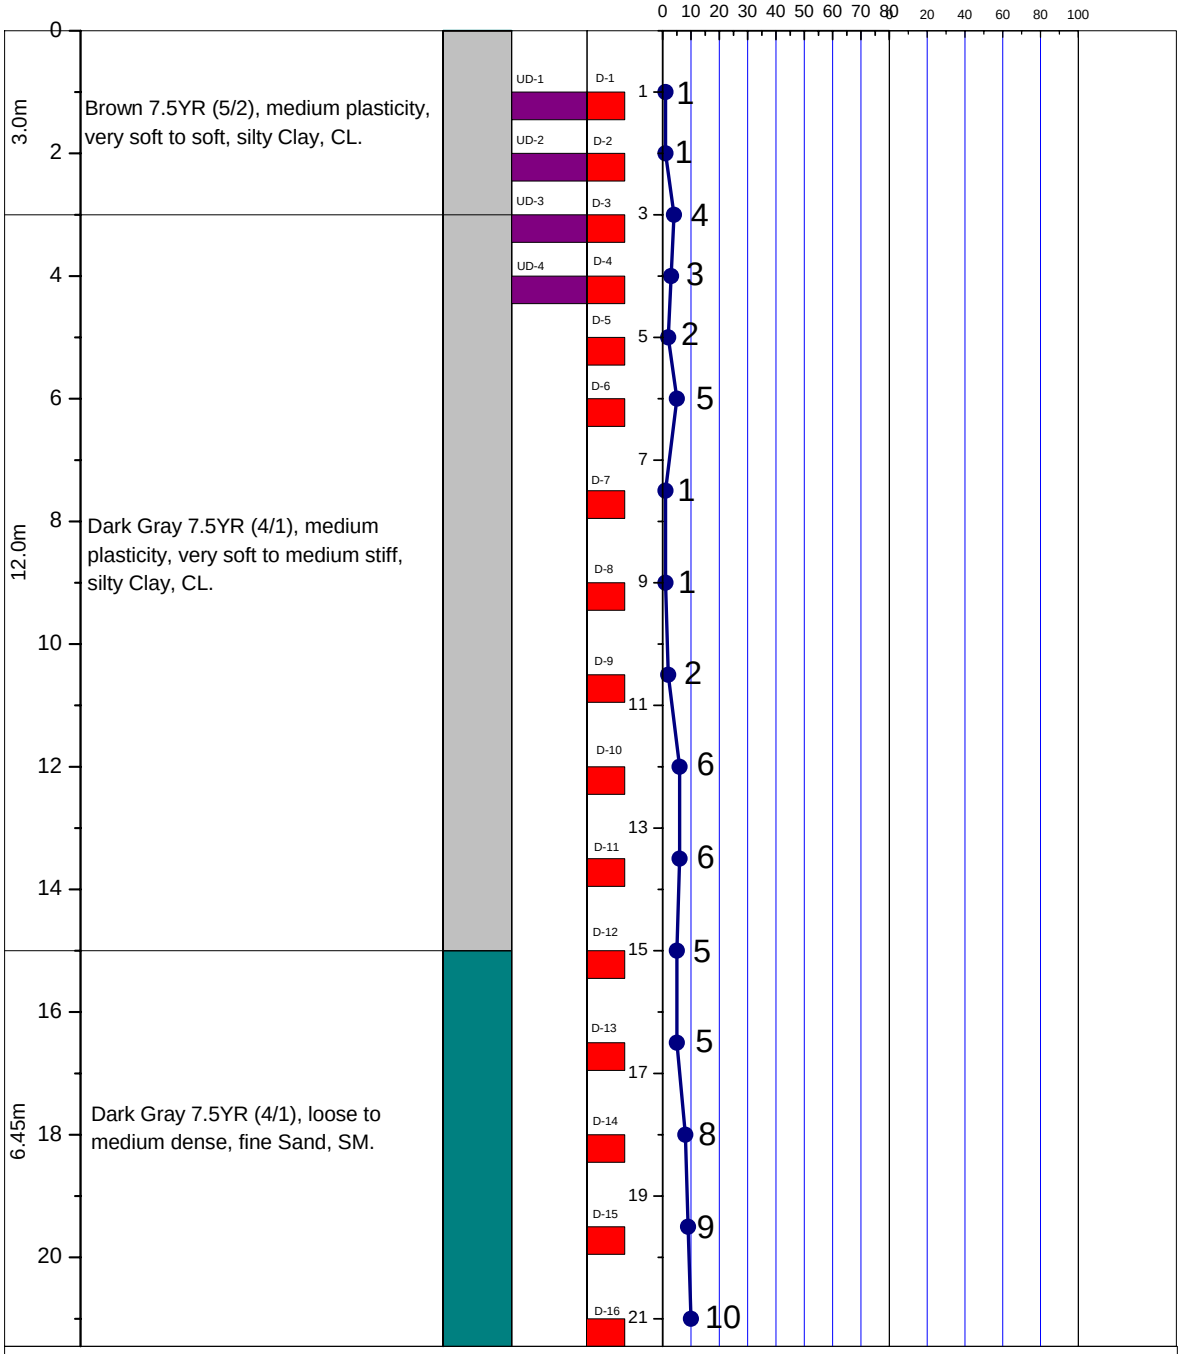

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SHALE	SILT	SAND
PEAT/HIGHLY ORGANIC SOIL	MICACEOUS FINE SAND/SILT	UNDISTURBED SAMPLE	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED

A2	PROSOIL	BOREHOLE NO: BH-3	
		LOCATION: Habispur, Doulatnagar, 4 No. Bahubal Union, Bahubal, Hobiganj.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING: 21.0m	R. L.: 0.66m below from Road Level.
CLIENT : Grameenphone Ltd.		DATE OF BORING: 08-05-2013.	G. W. T : 1.22m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration

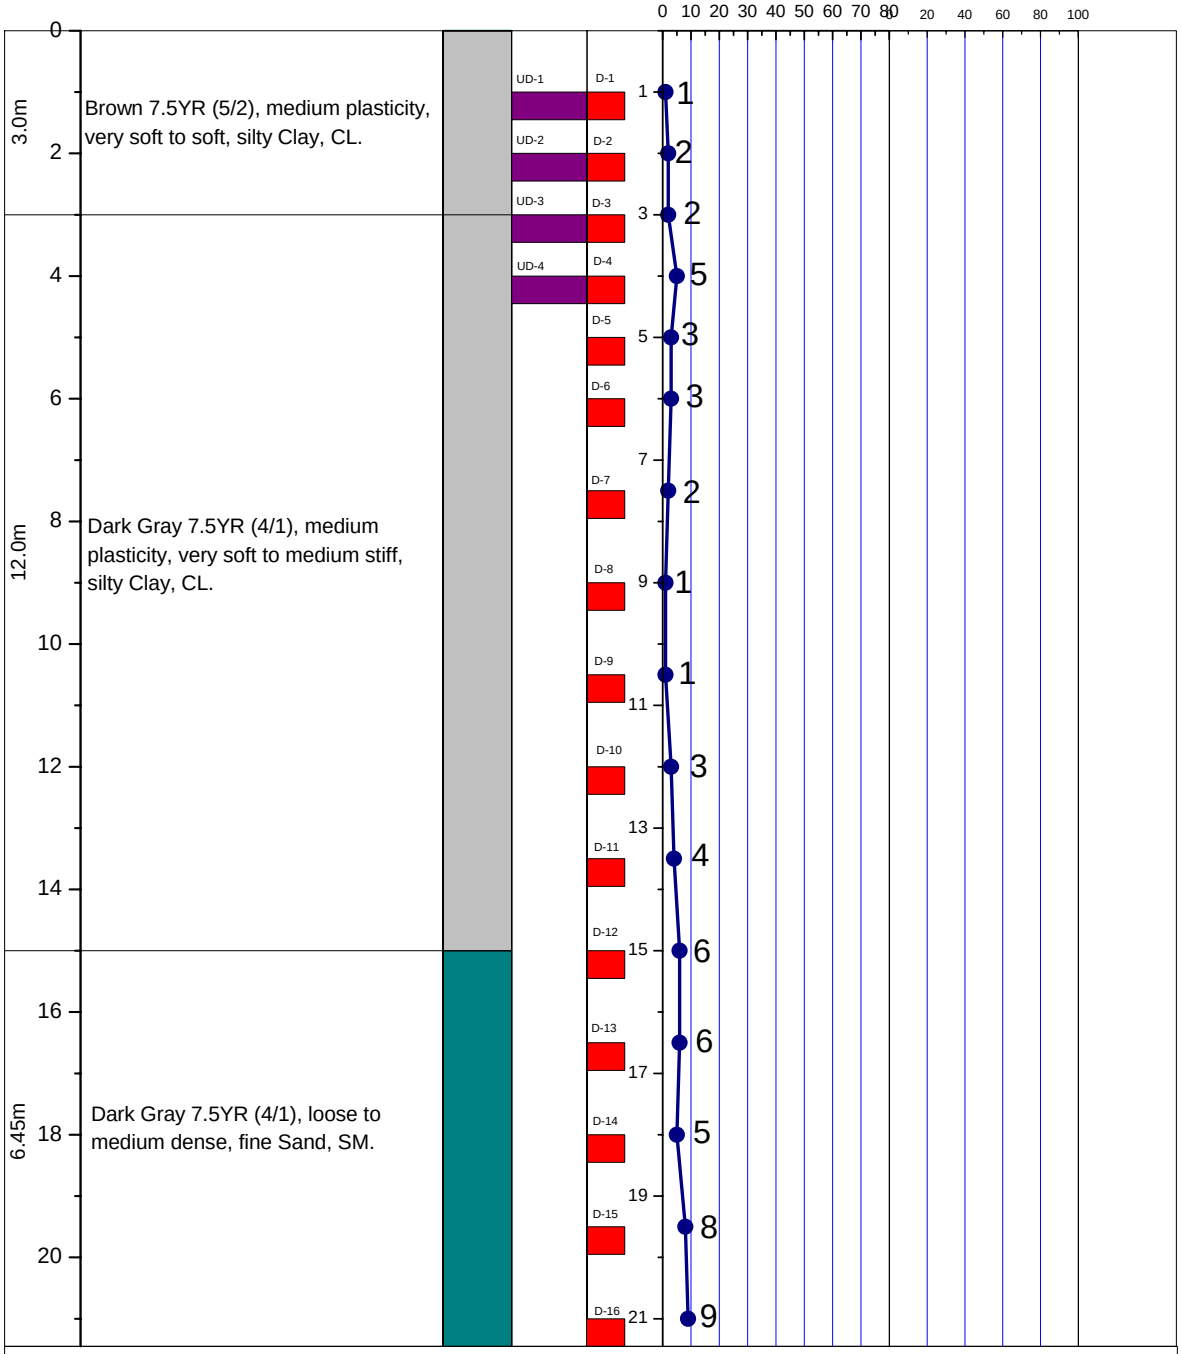

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY | SHALE | SILT | SAND

PEAT/HIGHLY ORGANIC SOIL | MICACEOUS FINE SAND/SILT | UNDISTURBED SAMPLE | DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
