A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION: Dhatir Hat, Sadar, Thakurgaon.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING: 12.0m	R. L.: 0.61m below from Road Level.
CLIENT : Grameenphone Ltd.		DATE OF BORING: 29-02-2012.	G. W. T : On E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
7.5m	Light Brown 7.5YR (6/4), loose to very dense, fine Sand, SM.			D-1 to D-6	10, 8, 7, 18, 8, 6		
4.95m	Light Gray 10YR (7/1), very dense, fine Sand with Quartz pebble and cobble grain, SM.			D-7 to D-10	41, 38, 38, 43		
	Boring was not possible due to very dense fine Sand with Quartz pebble and cobble grain.						

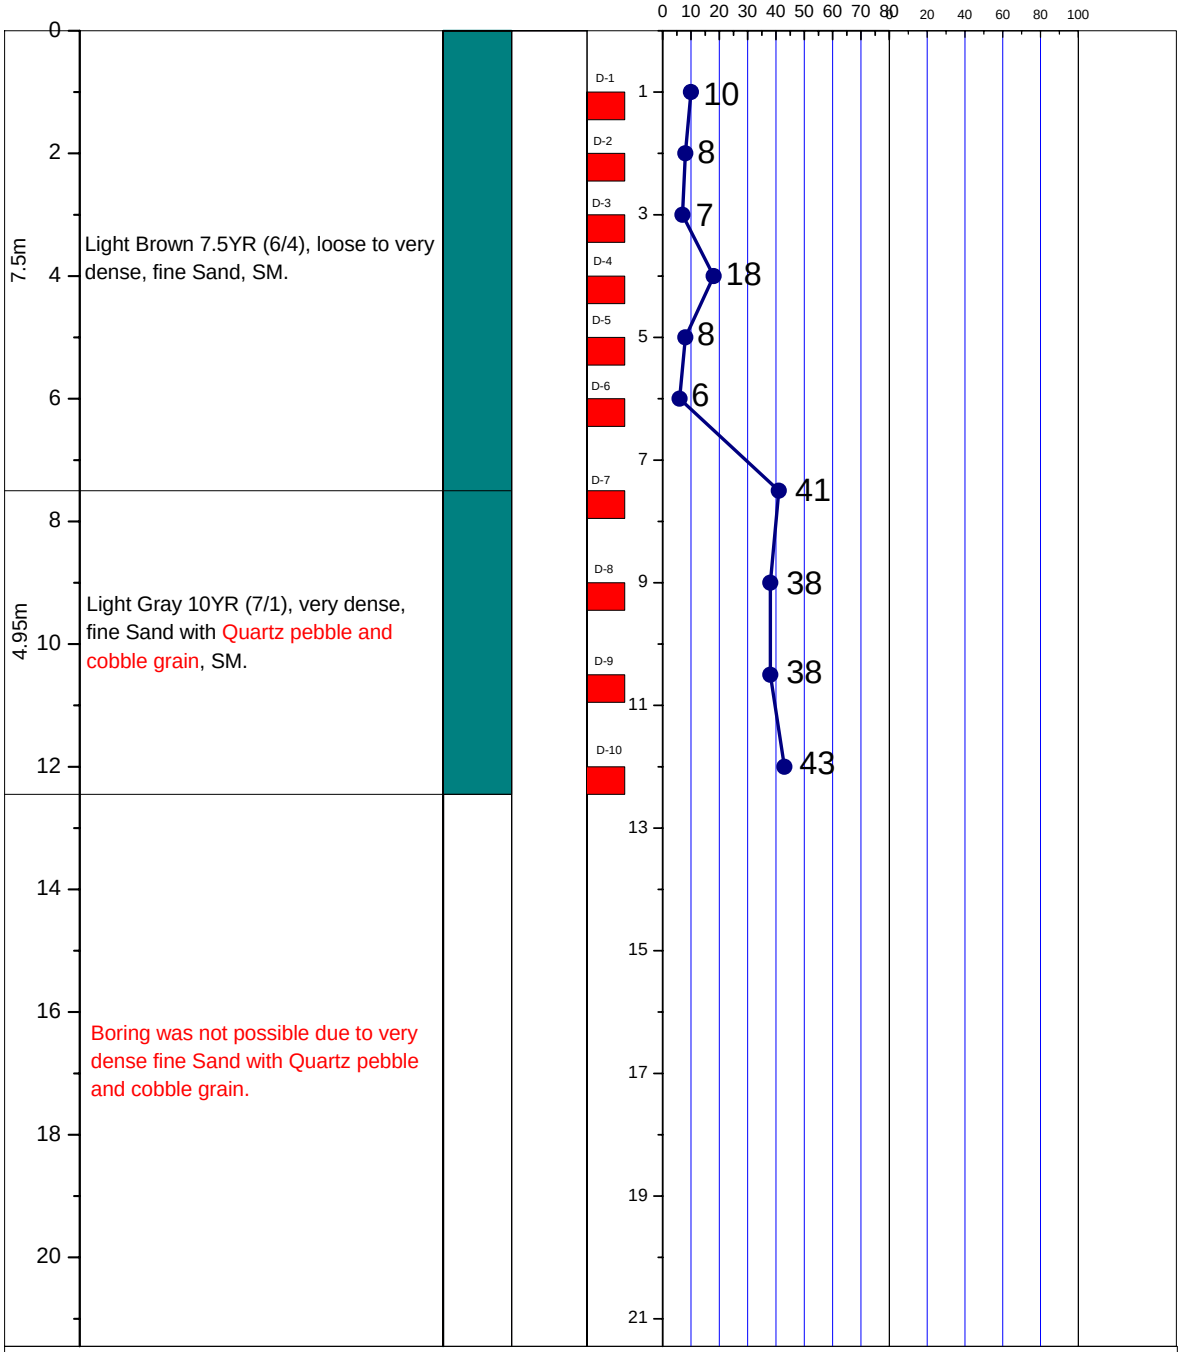

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY | SHALE | SILT | SAND

PEAT/HIGHLY ORGANIC SOIL | MICACEOUS FINE SAND/SILT | UNDISTURBED SAMPLE | DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
