| A2 | PROSOIL | BOREHOLE NO: BH-1 | |
|---|---|---|---|
| | | LOCATION : Kapna, Rotargaon, Bishwambarpur, 1 No. Shalokabad, Sunamganj. | |
| PROJECT : Telecommunication Tower. | | DEPTH OF BORING: 12.0m | R. L.: 0.15m below from Road Level. |
| CLIENT : Grameenphone Ltd. | | DATE OF BORING: 29-09-2012. | G. W. T : 3.66m below from E. G. L. |

| THICKNESS | SOIL STRATA | BORELOG | UNDISTURBED SAMPLE | DISTURBED SAMPLE | DEPTH (m) SPT VALUES ( BLOWS / 300mm ) | Grain Size Distribution, % Clay %, Silt %, Sand % | Max$^{m}$ Penetration |
|---|---|---|---|---|---|---|---|
| 2.0m | Light Gray 10YR (7/1), very loose, clayey Silt, ML. | | | D-1 | 1 | | |
| | | | | D-2 | 1 | | |
| 2.0m | Light Gray 10YR (7/1), very loose to medium dense, silty Sand, SM. | | | D-3 | 2 | | |
| | | | | D-4 | 14 | | |
| | | | | D-5 | 11 | | |
| 8.45m | Light Gray 10YR (7/1), medium dense to very dense, fine Sand (with pebble), SM. | | | D-6 | 12 | | |
| | | | | D-7 | 25 | | |
| | | | | D-8 | 31 | | |
| | | | | D-9 | 33 | | |
| | | | | D-10 | 30 | | |
| | Boring was terminated due to pebble. | | | | | | |

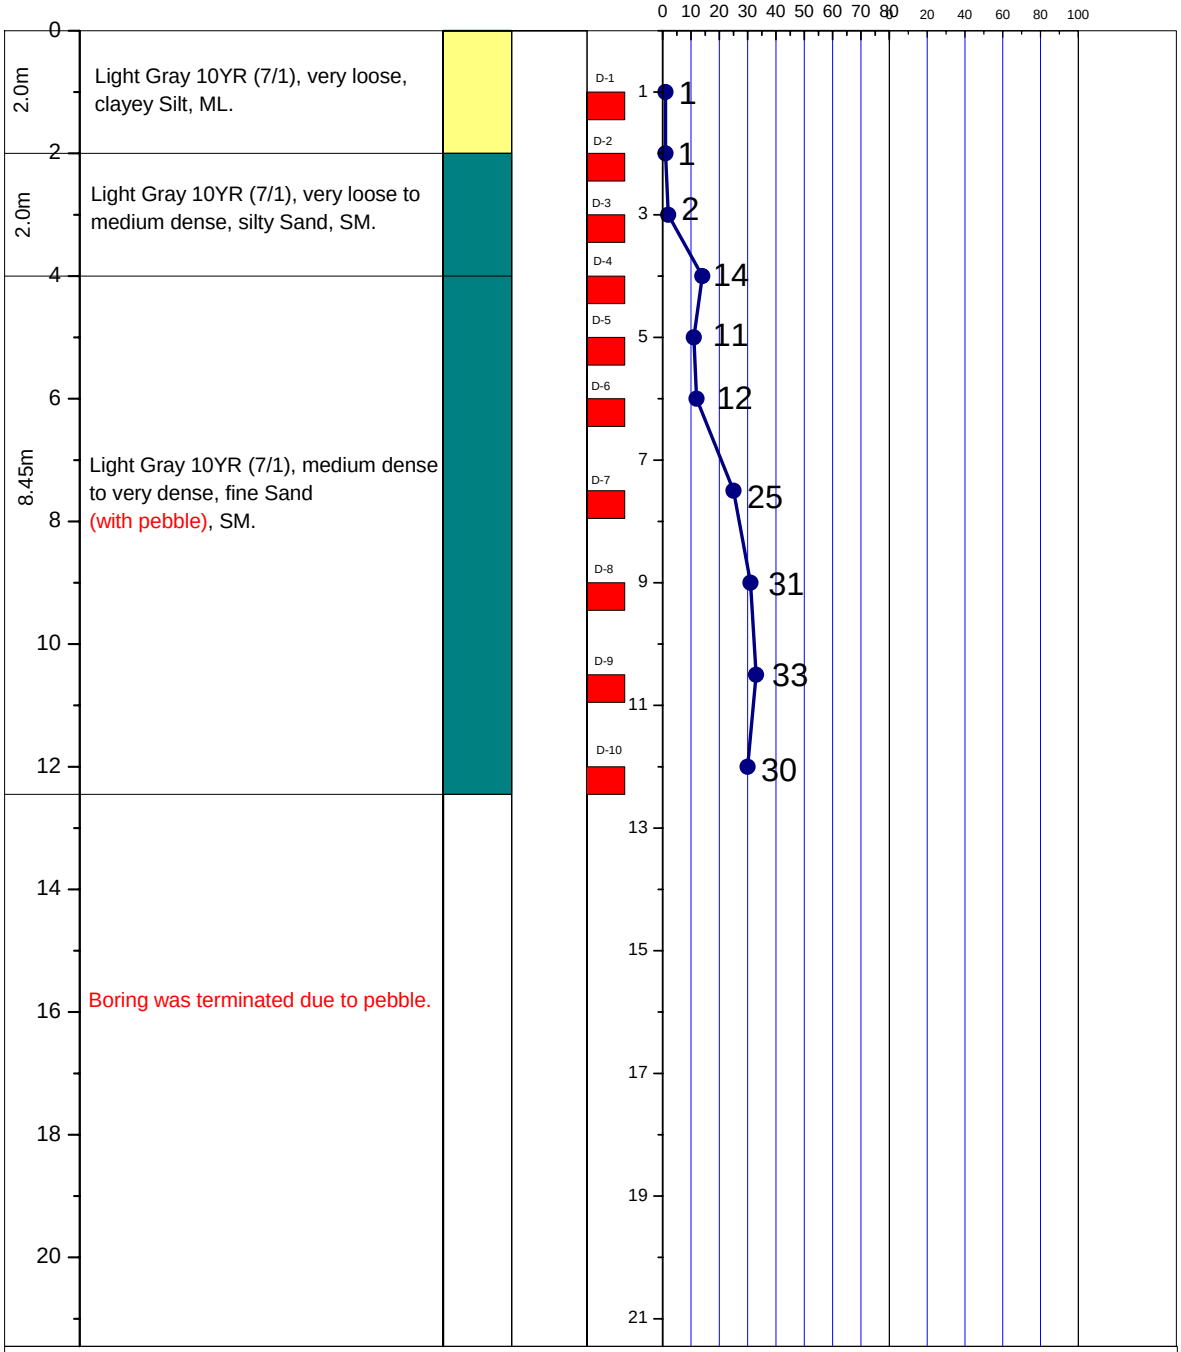


LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

| | | | |
|---|---|---|---|
| PLASTIC CLAY | SHALE | SILT | SAND |
| PEAT/HIGHLY ORGANIC SOIL | MICACEOUS FINE SAND/SILT | UNDISTURBED SAMPLE | DISTURBED SAMPLE |

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX$^{m}$ PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
