A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION: Bassainnadom Bazar, Vashannya Adam, Longudu, Rangamati.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING: 13.5m	R. L.: 0.46m above from Road Level.
CLIENT : AXIATA (Bangladesh) Ltd.		DATE OF BORING: 04-01-2013.	G. W. T : 1.83m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
5.0m	Red 2.5YR (5/6), medium dense to dense, Silt, ML.			D-1 to D-5	14, 15, 18, 18, 19		
4.0m	Yellow 10YR (7/8), dense to very dense, silty Sand, SM.			D-6 to D-8	20, 27, 35		
4.95m	Yellow 10YR (7/8), very dense, fine Sand, SM.			D-9 to D-12	43, 50, 50, 50		Over, Over, Over
	Boring was not possible due to very dense fine Sand.						

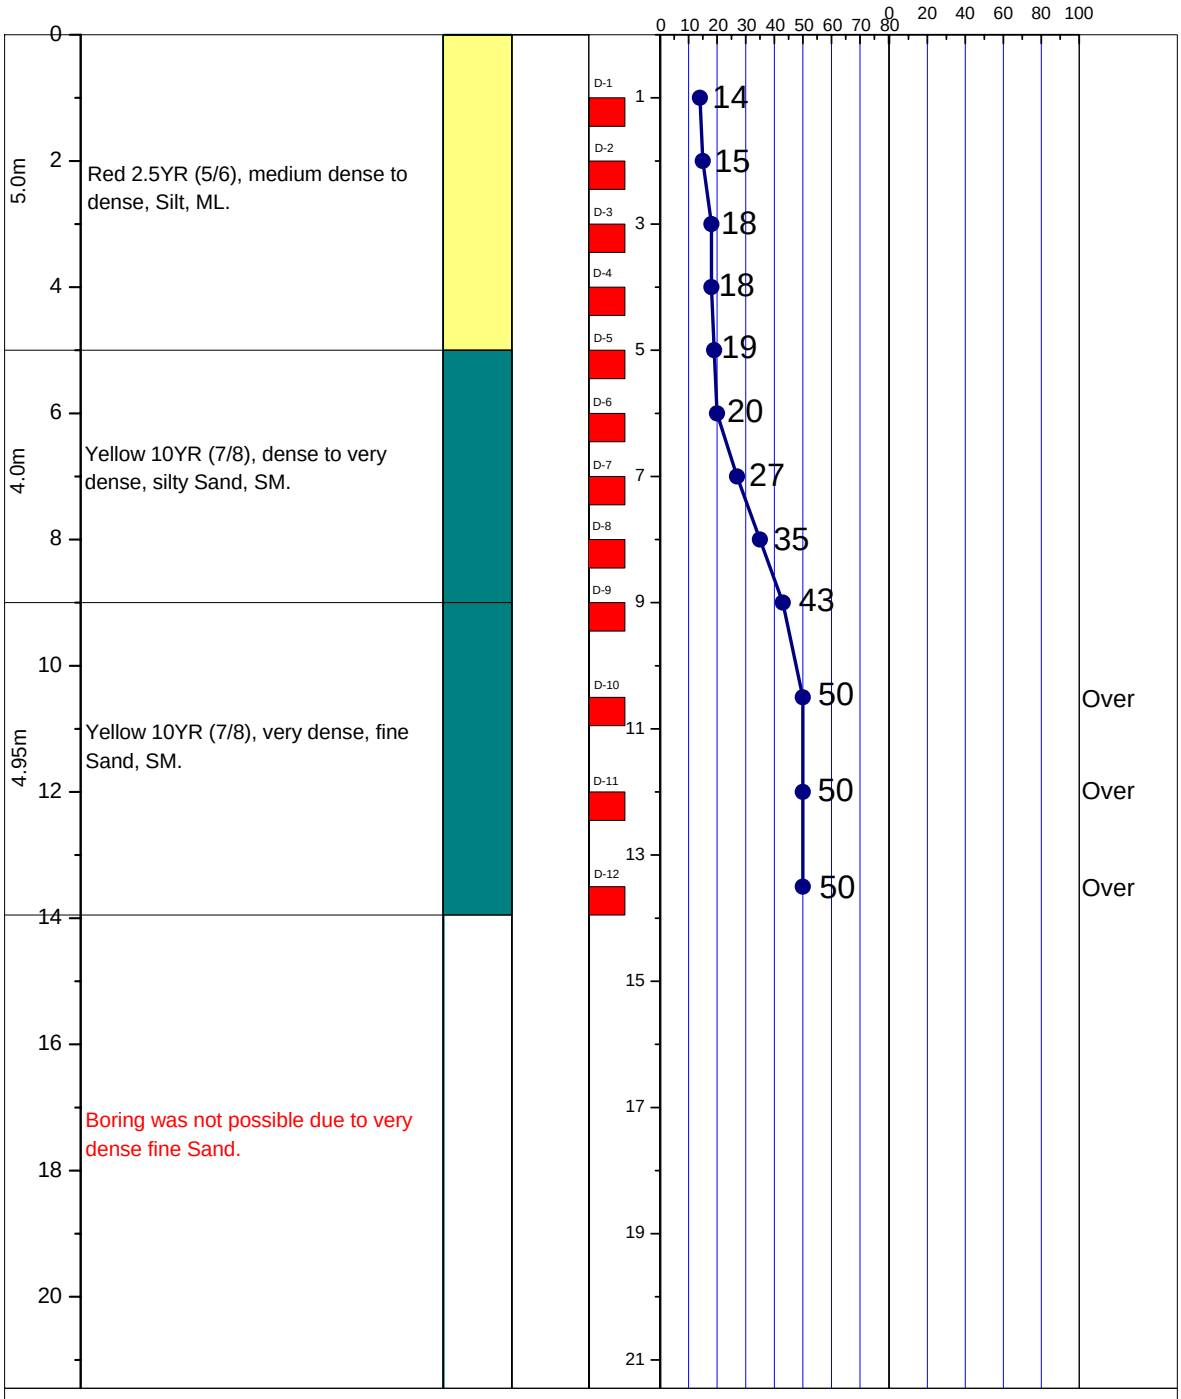

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SAND	SILT	SHALE
PEAT/HIGHLY ORGANIC SOIL	MICACEOUS FINE SAND/SILT	UNDISTURBED SAMPLE	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
