
A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION : Hatkhola, Daudkandi, Comilla.	
PROJECT : Proposed Duplex Building.		DEPTH OF BORING : 18.0m	R. L.: Road Level.
CLIENT : Mr. Anwar Faruque.		DATE OF BORING : 19-06-2009.	G. W. T : 4.27m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
2.0m	Pale brown 10YR (6/1), very loose to loose, cohesionless silt, SM.		UD-2	D-1, D-2	1, 3		
2.0m	Pale brown 10YR (6/1), medium plastic soft to medium stiff, silty Clay, CL.		UD-3	D-3	5		
1.0m	Gray 10YR (5/1), medium plastic, medium stiff to soft, silty Clay, CL.		UD-4	D-4	7		
5.5m	Gray 10YR (5/1), loose to medium dense, cohesionless silt, SM.			D-5, D-6, D-7, D-8	4, 5, 3, 5		
1.5m	Gray 10YR (5/1), medium plastic, medium stiff to very stiff, silty Clay, CL.			D-9	8		
6.45m	Gray 10YR (5/1), very dense to dense, fine sand, SM.			D-10, D-11, D-12, D-13, D-14	37, 44, 37, 30, 28		

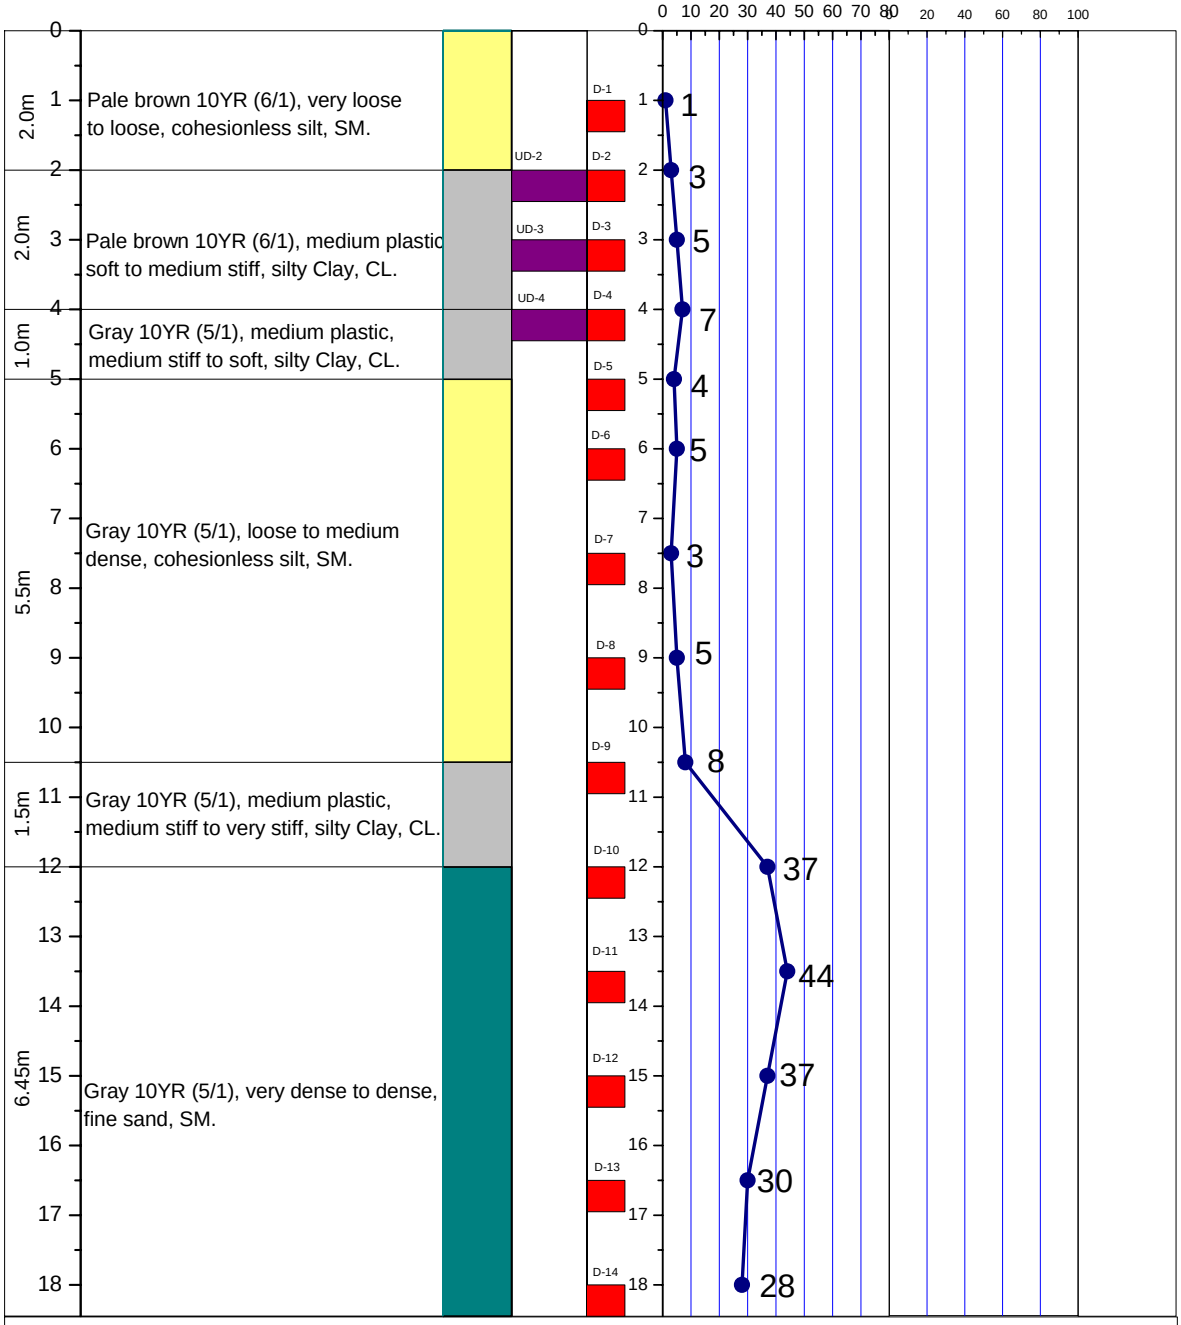

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
