A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION : Kumira Railway Station, Chittagong.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING : 16.5m	R. L.: 0.91m above from Road Level.
CLIENT : Grameen phone Ltd.	DATE OF BORING : 27-04-2005	G. W. T : 3.04m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Remarks
3.0m	Brown colour 10YR (5/3), non plastic loose, sandy Silt, SM.			D-1 to D-3	5, 3, 5		
2.0m	Light brownish gray colour 10YR (6/2), medium plastic, soft to medium stiff, silty Clay, CL.			D-4 to D-5	7, 8		
2.5m	Gray colour 10YR (5/1), medium dense, silty Sand, SM.			D-6 to D-7	10, 50		
9.0m	Gray colour (6/1), medium plastic, silty clay, CL. Clay shale with calcareous bands.			D-8 to D-13	50, 50, 50, 50, 50, 50		Over
4.95m	**Boring was not possible due to ground was too hard.**			D-14 to D-16			

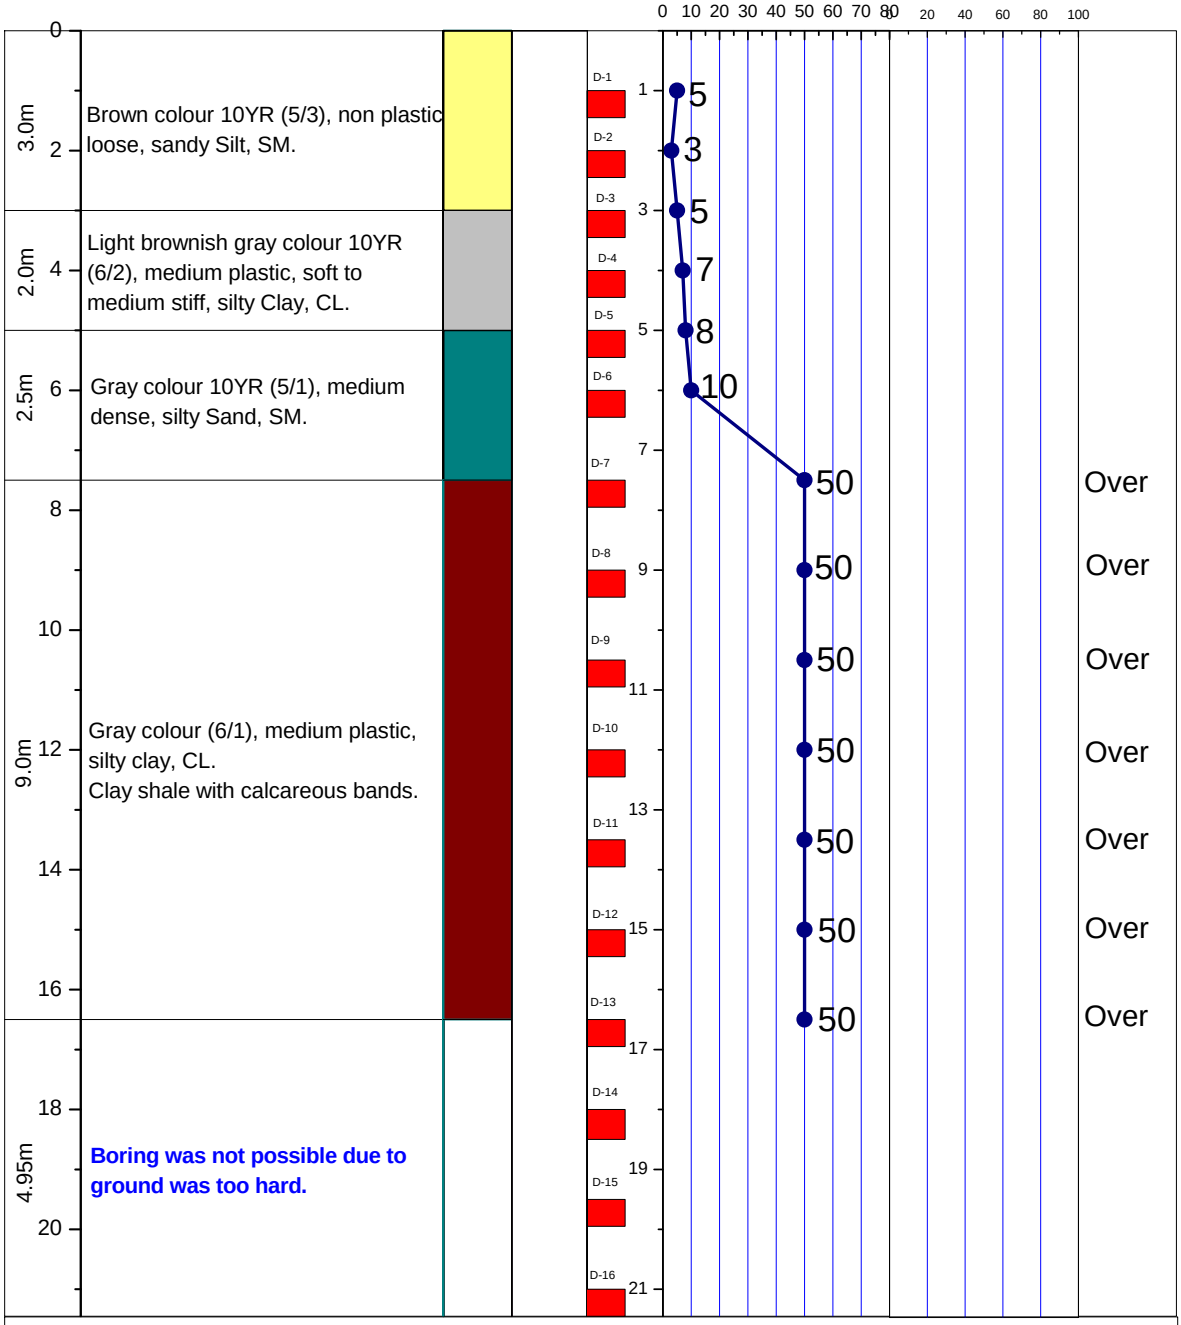

ID FOR BOREHOLE A RAIN SIZE DISTRIBU

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

UNDISTURBED SAMPLE

ORGANIC

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
