A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION : Ramchandrapur, Kaliakoir, Gazipur.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING : 21.0m	R. L.: 1.82m below from Road Level.
CLIENT : Grameenphone Ltd.	DATE OF BORING : 07-01-2008.	G. W. T : 1.21m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
21.45m	Very pale brown 10YR (7/3), medium plastic, medium stiff to very stiff, silty Clay, CL.		UD-1 to UD-4	D-1 to D-16	7, 10, 8, 11, 14, 16, 15, 22, 17, 21, 18, 20, 23, 25, 28, 27		

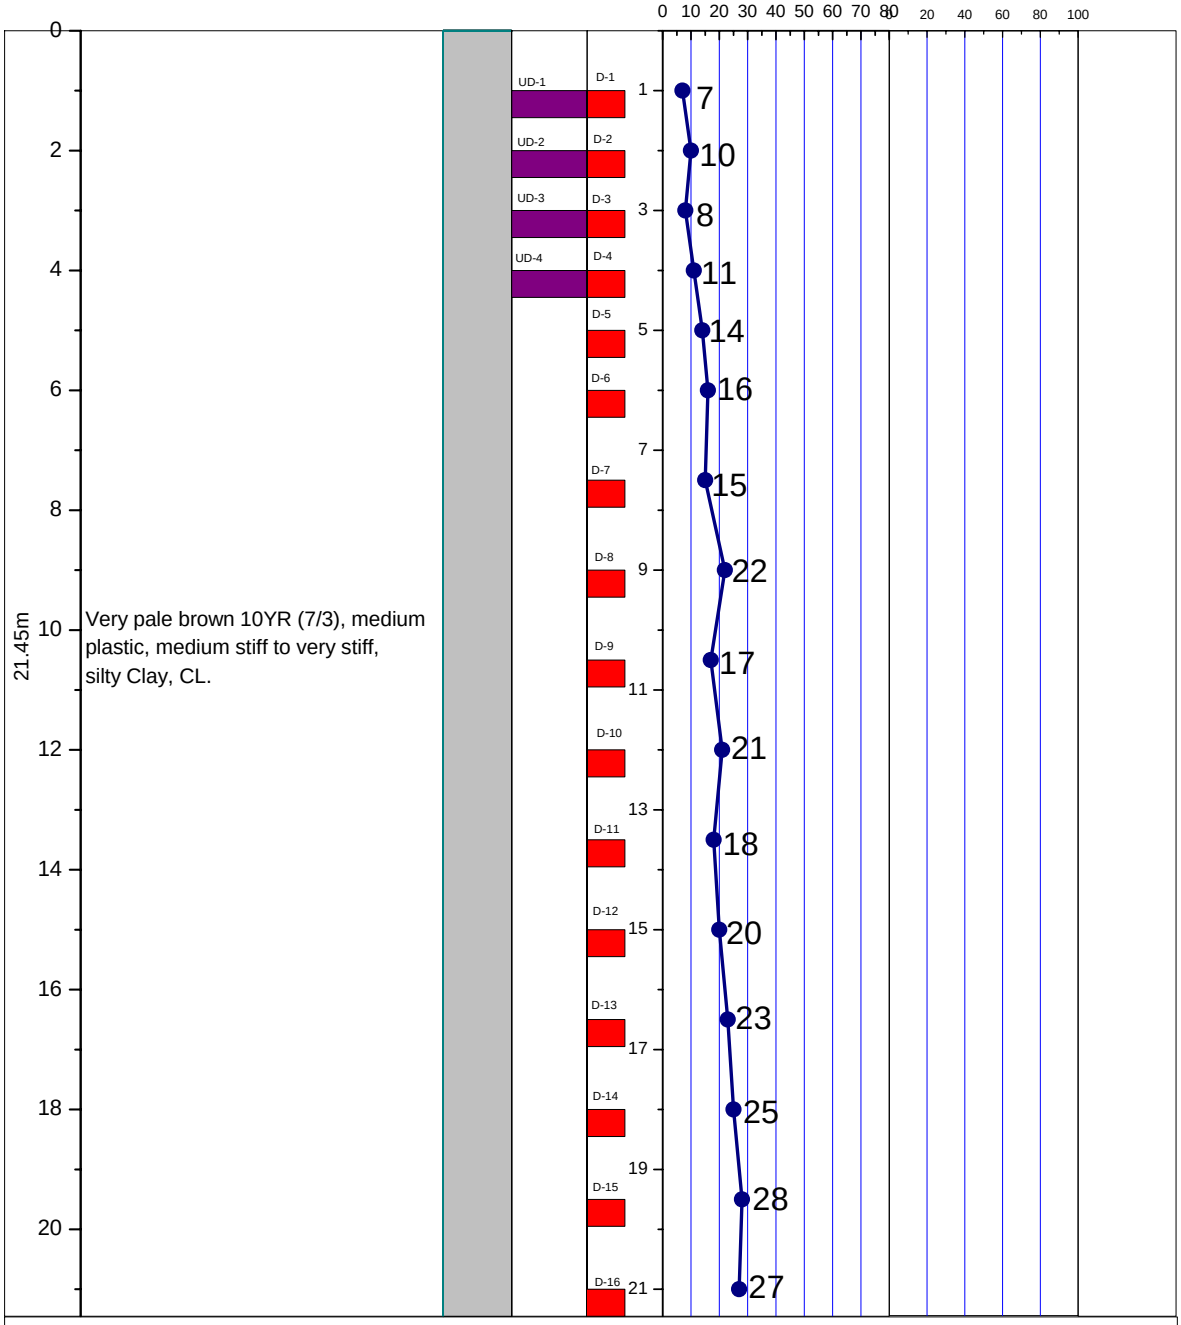

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
