A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION : Bashbaria, Bagatipara, Natore.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING : 21.0m	R. L.: 0.30m below from Road Level.
CLIENT : AXIATA (Bangladesh) Ltd.		DATE OF BORING : 06-08-2009.	G. W. T : 3.05m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
5.0m	Very pale brown 10YR (7/3), medium dense to loose, cohesionless silt, SM.			D-1 to D-5	7, 6, 4, 5, 6		
2.0m	Very pale brown 10YR (7/3), medium plastic, medium stiff to stiff, silty Clay, CL.			D-6 to D-7	6, 12		
3.5m	Very pale brown 10YR (7/3), medium dense, cohesionless silt, SM.			D-8 to D-10	8, 10, 7		
4.5m	Gray 10YR (6/1), medium plastic, medium stiff to stiff, silty Clay, CL.			D-11 to D-13	8, 14, 16		
3.0m	Very pale brown 10YR (7/3), dense to very dense, cohesionless silt, SM.			D-14 to D-15	16, 35		
3.45m	Very pale brown 10YR (7/3), very dense, fine sand, SM.			D-16 to D-17	27, 45		

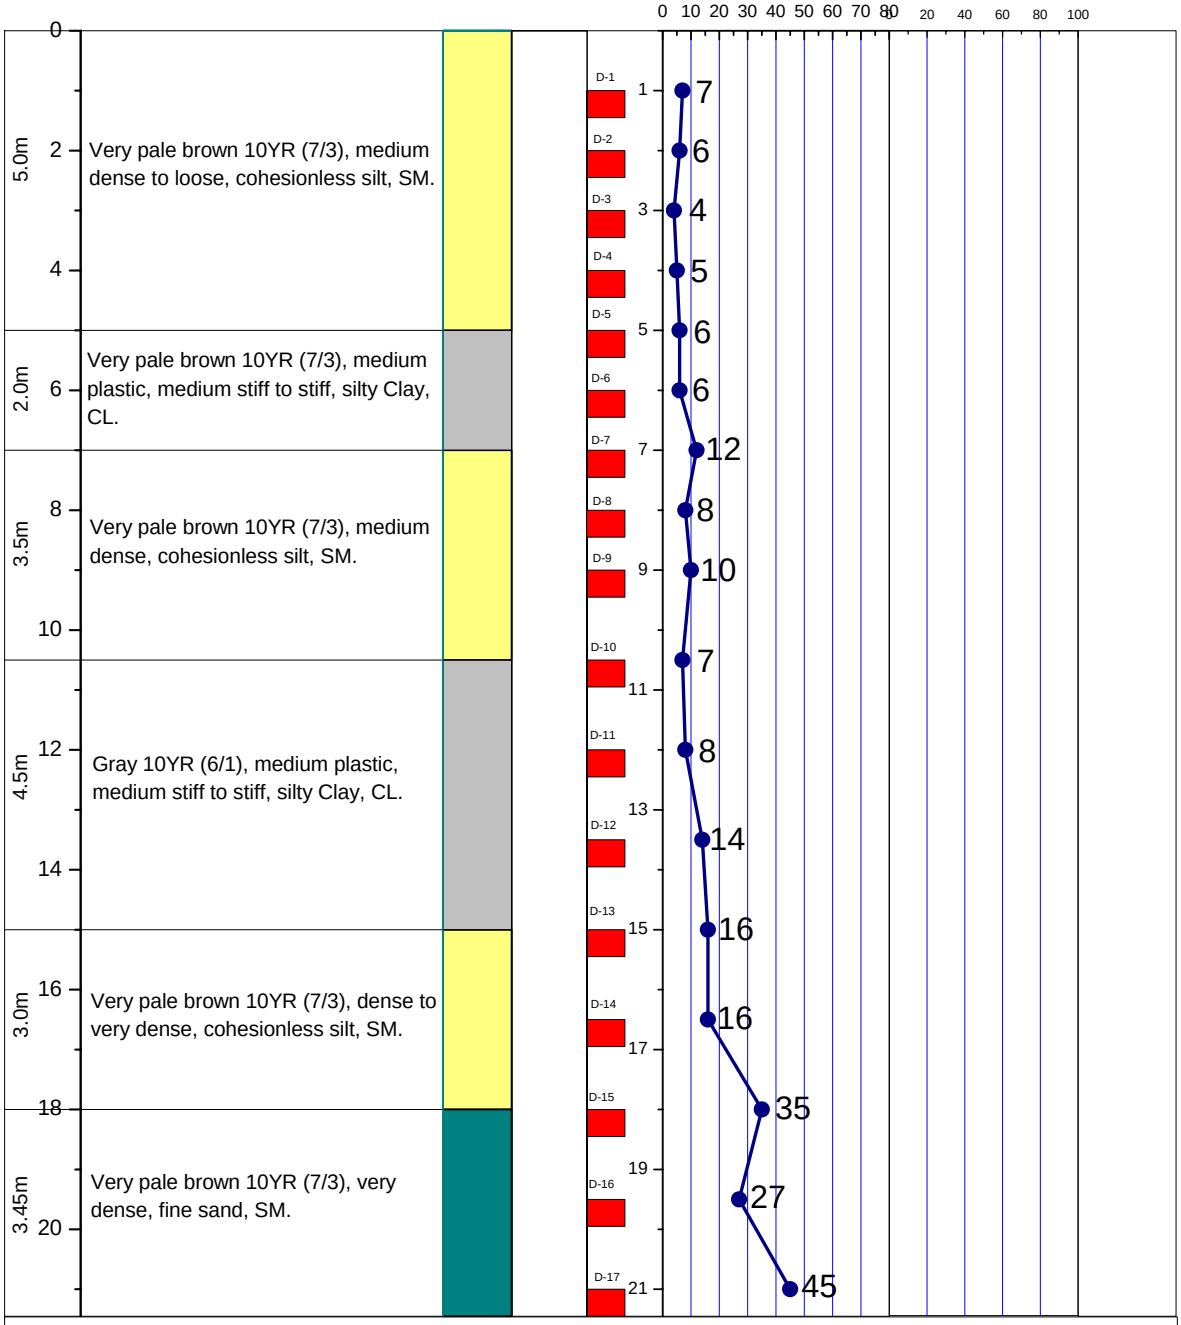

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
