A2 PROSOIL	BOREHOLE NO: BH-3	
	LOCATION : Gagla Bazar, Nageshwari, Kurigram.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING : 21.0m	R. L.: 0.91m below from Road Level.
CLIENT : Sheba Telecom (PVT.) Ltd.	DATE OF BORING : 17-12-2007.	G. W. T : 3.04m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
2.0m	Light brown 7.5YR (6/3), loose to medium dense, fine sand, SM.			D-1 to D-2	3, 9		
2.0m	Brown 7.5YR (4/3), medium dense to loose, silty Sand, SM.			D-3 to D-4	8, 6		
3.5m	Gray 7.5YR (6/1), loose to dense, fine sand, SM.			D-5 to D-8	18, 21, 22, 29		
13.95m	Gray 7.5YR (5/1), dense to very dense, fine sand, SM.			D-9 to D-16	32, 34, 36, 38, 40, 42, 44, 46		

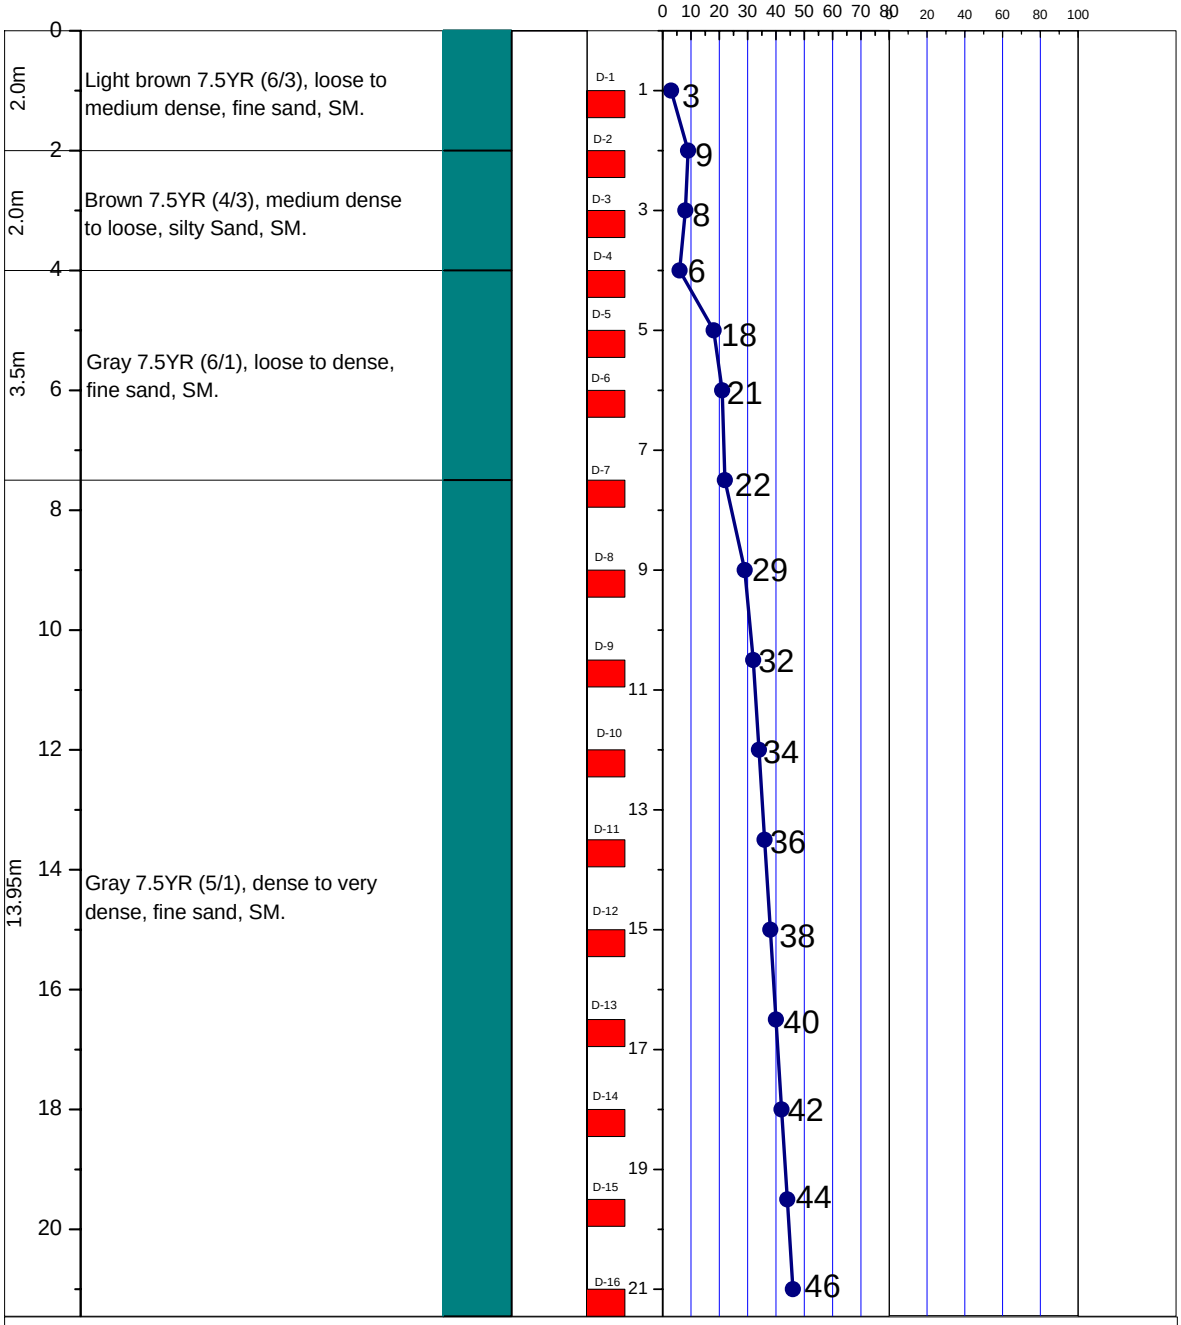

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
