A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION : Nagla Bazar, Haluaghat, Mymensingh.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING : 21.0m	R. L.: 0.76m below from Road Level.
CLIENT : Grameenphone Ltd.	DATE OF BORING : 02-07-2007.	G. W. T : 0.60m below from E.G.L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
2.0m	Brown 10YR (5/3), loose to medium dense, cohesionless silt, SM.			D-1 to D-2	4, 10		
1.0m	Light gray 10YR (7/2), medium dense, fine sand, SM.			D-2 to D-3	10, 13		
2.0m	Gray 10YR (6/1), medium dense, silty Sand, SM.			D-3 to D-4	13, 13		
2.5m	Gray 10YR (6/1), medium dense to loose, cohesionless silt, SM.			D-4 to D-6	13, 11, 10		
1.5m	Gray 10YR (6/1), medium plastic, soft to very stiff, silty Clay, CL.			D-6 to D-7	10, 3		
12.45m	Light gray 10YR (7/1), dense to very dense, fine sand, SM.			D-7 to D-16	3, 23, 27, 31, 35, 37, 40, 43, 46, 50		Over

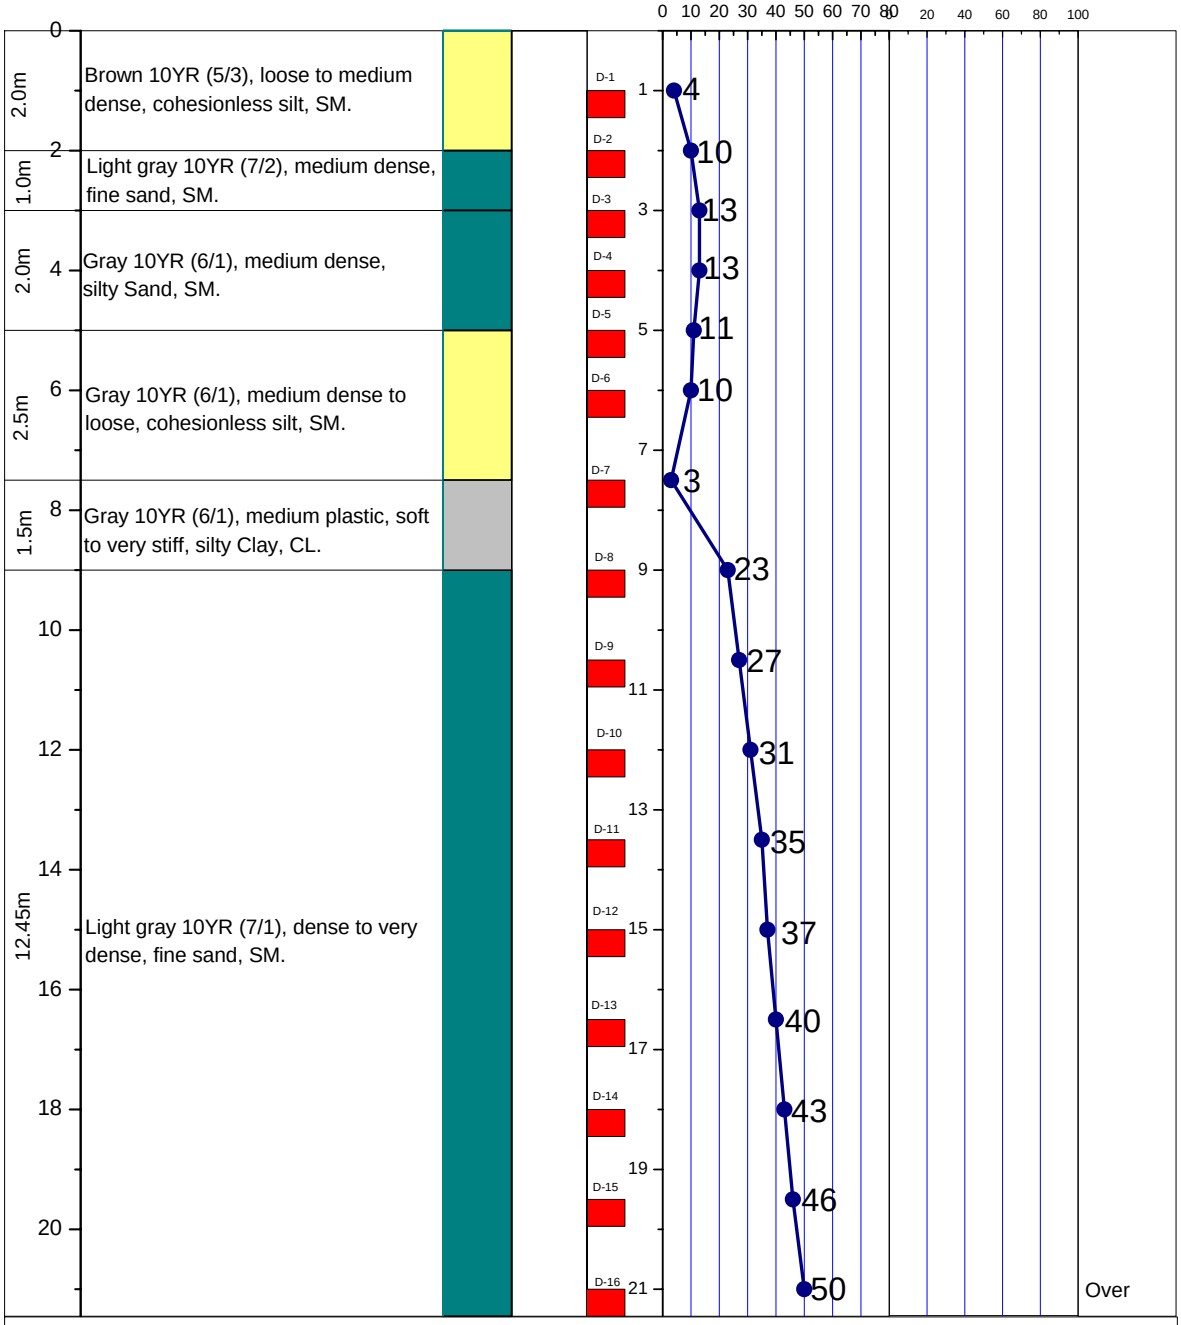

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
