A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION: Nakogaon, Charali Bazar, Nalitabari.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING: 21.0m	R. L.: 1.52m below from Road Level.
CLIENT : Orascom Telecom Bangladesh Limited.		DATE OF BORING : 07-03-2014.	B. W. T : 1.93m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
4.5m	Reddish Brown 2.5Y (4/5), very loose to loose, fine Sand, SM.			D-1 to D-4	1, 3, 2, 4		
6.0m	Light Reddish Brown 2.5Y (6/3), loose to medium dense, fine Sand, SM.			D-5 to D-8	3, 6, 10, 12		
5.5m	Yellowish Red 2.5Y (5/3), medium dense to dense, fine Sand, SM.			D-9 to D-12	15, 18, 17, 19		
2.0m	Yellowish Red 5Y (5/6), dense, fine Sand, SM.			D-13 to D-14	20, 24		
3.0m	brown 7.5Y (4/3), dense, fine Sand, SM.			D-15 to D-16	26, 36		
0.45m	Dark Gray 5Y (3/1), dense, fine Sand, SM.						

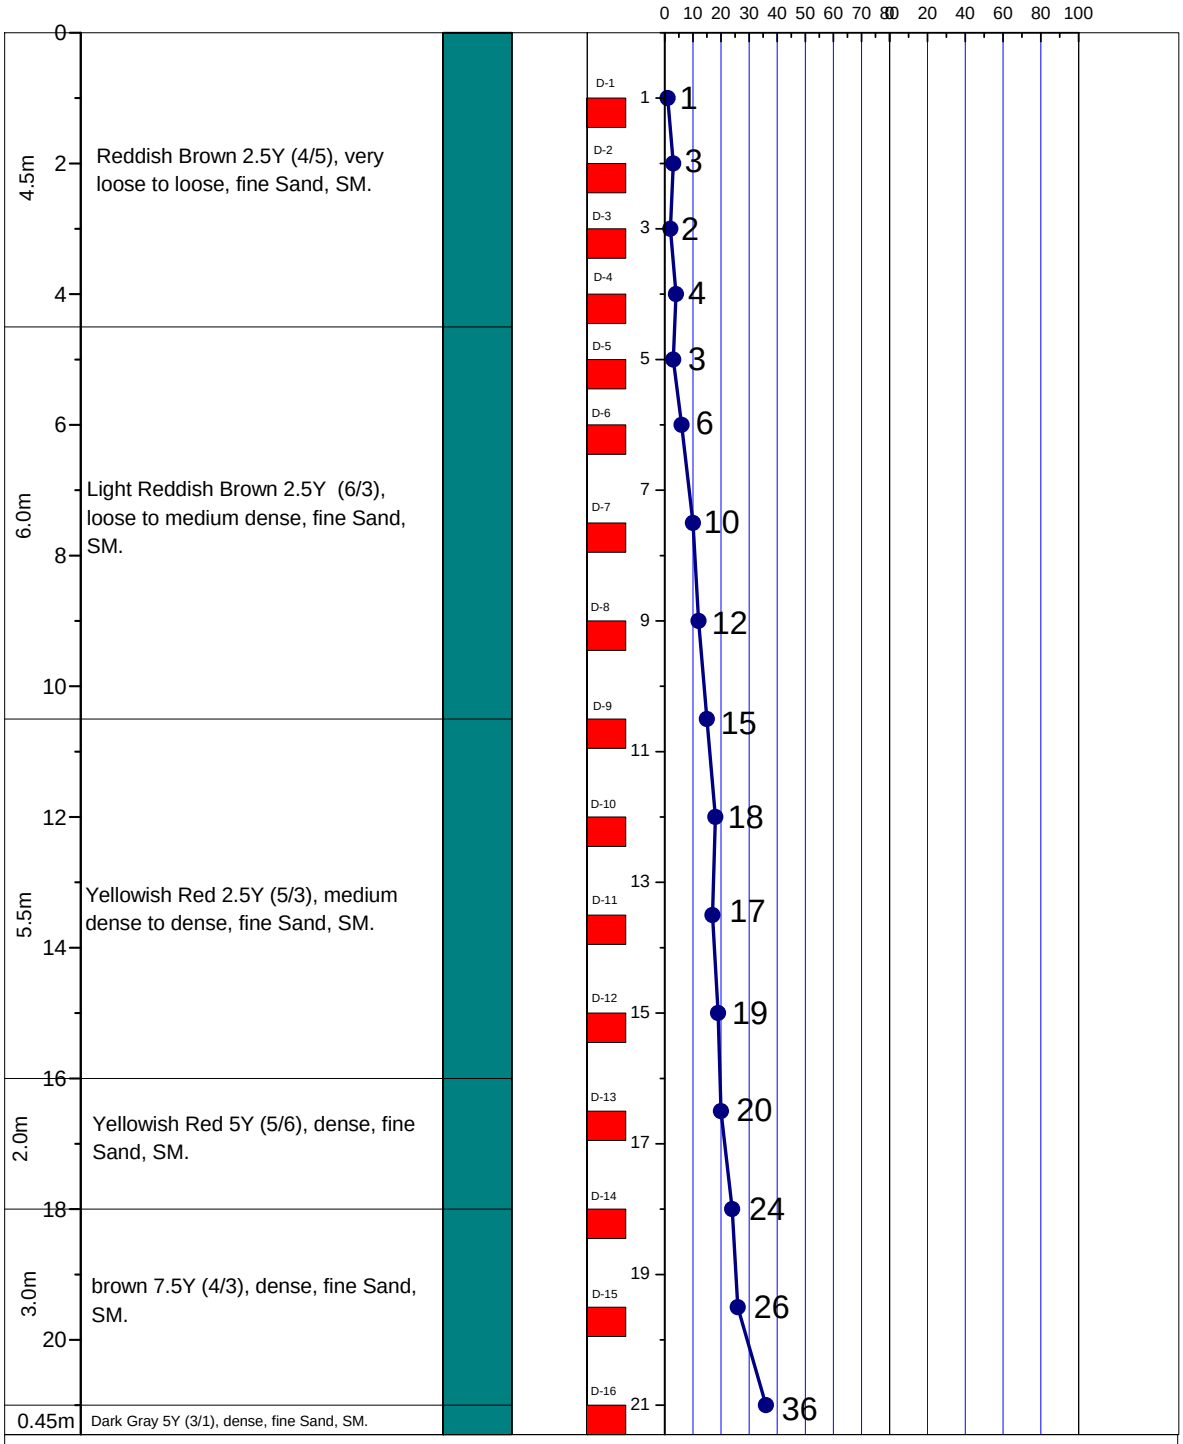

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SAND	SILT	SHALE
PEAT/HIGHLY ORGANIC SOIL	MICACEOUS FINE SAND/SILT	UNDISTURBED SAMPLE	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
