A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION : Dewhata, Mirzapur, Tangail.	
PROJECT : GSM1800 National Deployment.	DEPTH OF BORING : 21.0m	R. L.: 1.52m below from Road Level.
CLIENT : Warid Telecom.	DATE OF BORING : 12-10-2006	G. W. T : 0.91m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Dark reddish gray 10YR (4/1), organic soil.			D-1 to D-2	4, 4		
1.5m	Gray 10YR (5/1), loose, cohesionless silt, SM.			D-2 to D-3	4, 5		
6.0m	Dark gray 10YR (4/1), organic soil.			D-3 to D-6	5, 7, 6, 5		
1.5m	Gray 10YR (5/1), stiff, clayey Silt, ML.			D-6 to D-7	5, 10		
1.5m	Pale brown 10YR (6/3), medium plastic, stiff, silty Clay, CL.			D-7 to D-8	10, 12		
7.95m	Pale yellow 2.5Y (7/4), medium dense to very dense, fine sand, SM.			D-8 to D-14	12, 15, 18, 19, 24, 34, 42		

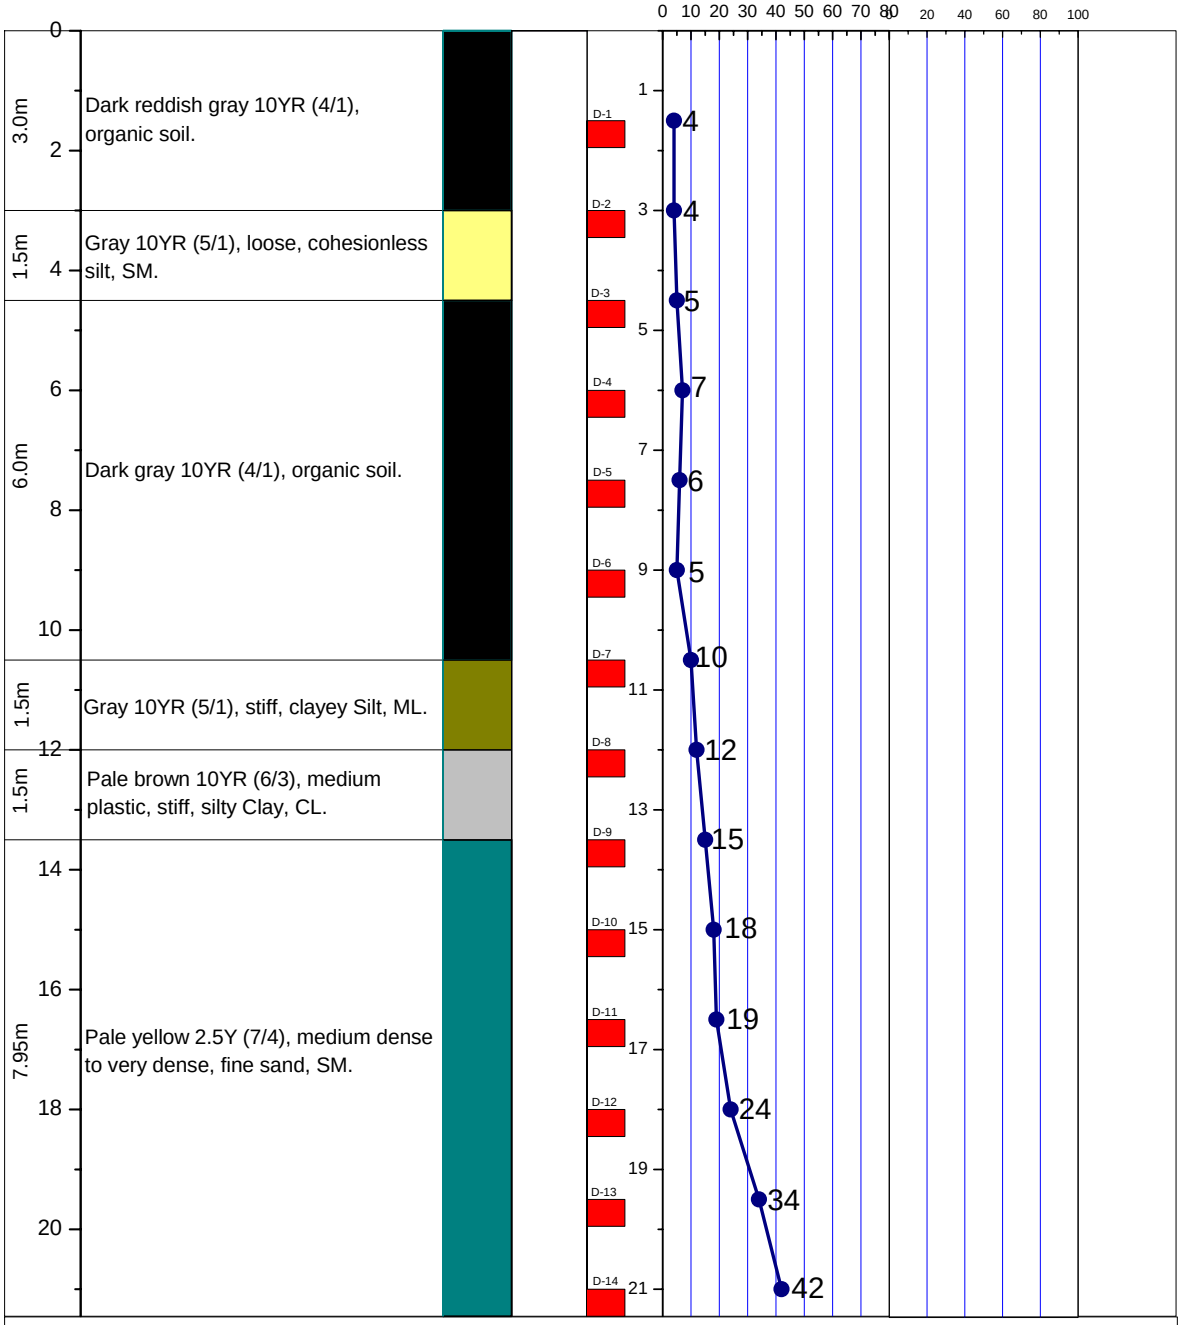

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY	NON PLASTIC SILT	ORGANIC	UNDISTURBED SAMPLE
LOW PLASTIC CLAYEY SILT	SAND	SHALE	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
