A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION: Dhunot, Bogra.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING: 16.5m	R. L.: 1.52m below from Road Level.
CLIENT : Orascom Telecom Bangladesh Limited.		DATE OF BORING : 22-05-2010.	G. W. T : 6.09m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
4.0m	Light 10YR (7/C), medium dense Silt, MH.			D-1 to D-3	6, 7, 11		
1.0m	Light gray 10YR (7/C), medium dense fine Sand, SW.			D-4 to D-5	15, 10		
10.0m	Gray 10YR (7/C), medium dense to dense, fine Sand, SW.			D-6 to D-11	11, 25, 29, 30, 32, 50		Over
1.95m	Dark gray 10YR (4/1), highly Organic Soil, Pt.			D-12	50		Over
4.95m	**Boring was not possible due to** highly organic Soil.			D-13	50		Over

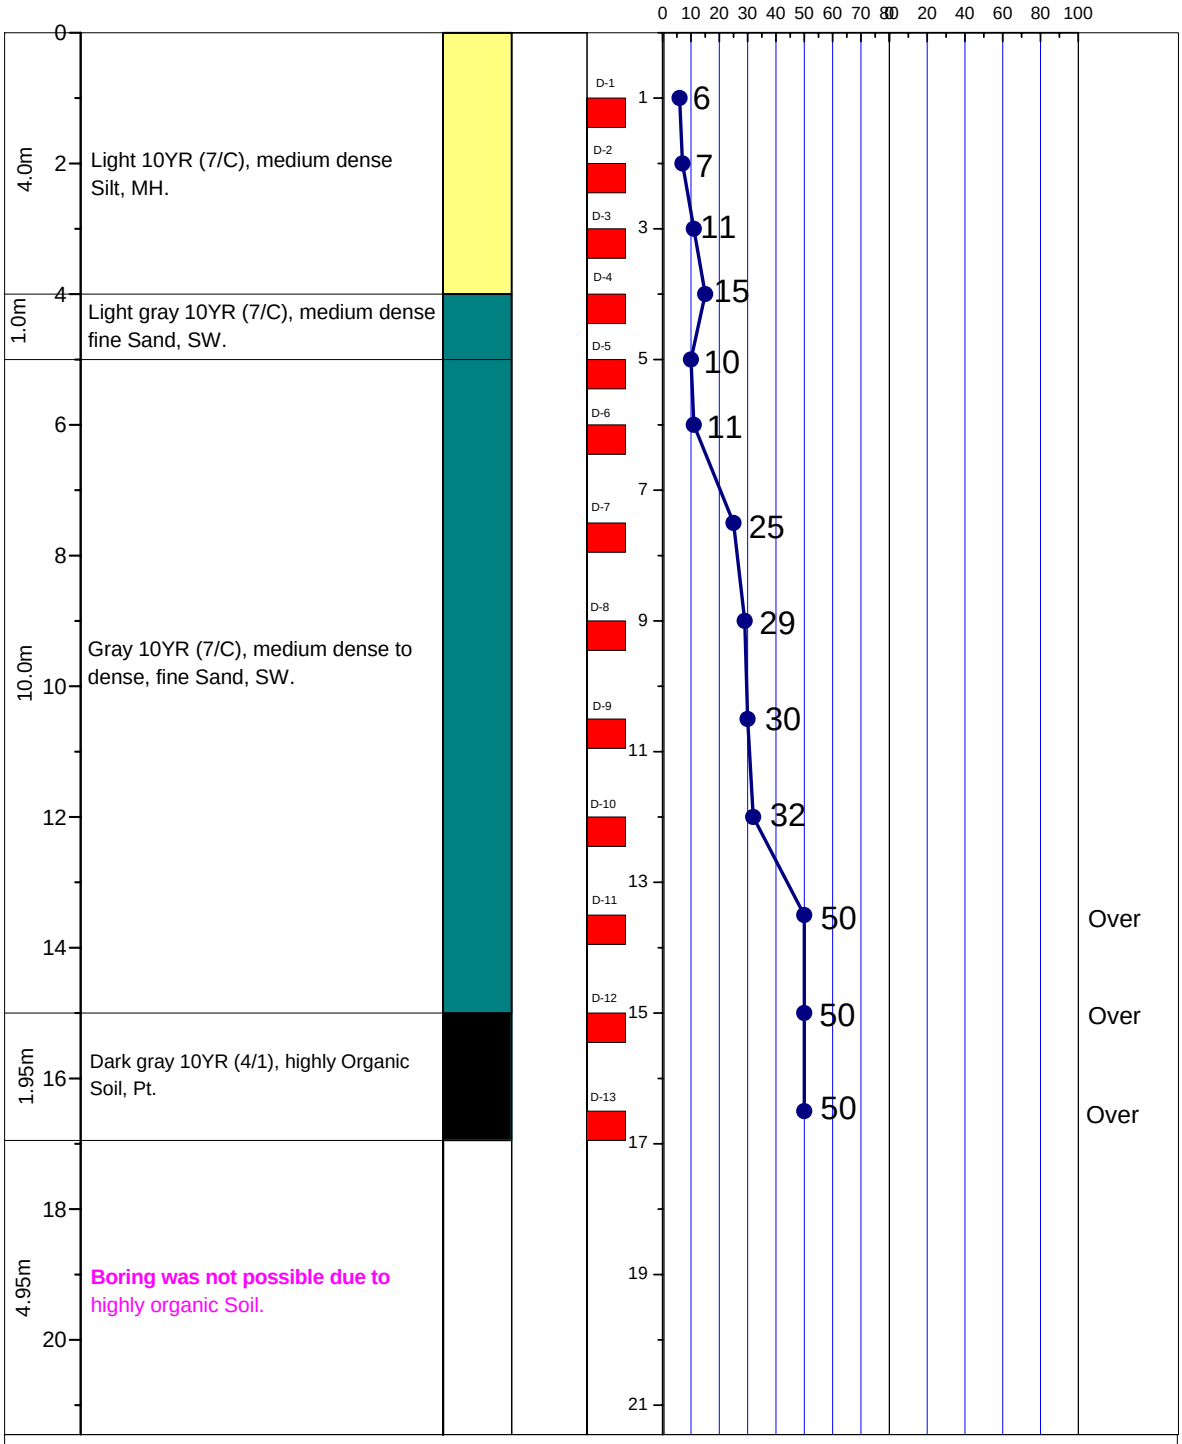

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SAND	SILT	SHALE
PEAT/HIGHLY ORGANIC SOIL	MICACEOUS FINE SAND/SILT	UNDISTURBED SAMPLE	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS
AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
