A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION: Ranirhat 2, Uttar Ghagra, Thanda Chorry, Rangunia, Chittagong.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING: 21.0m	R. L.: 0.61m below from Road Level.
CLIENT : AXIATA (Bangladesh) Ltd.		DATE OF BORING: 17-12-2012.	G. W. T : 1.83m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
5.0m	Brown 7.5YR (4/6), medium plasticity, very soft to stiff, silty Clay, CL.		UD-1, UD-2, UD-3, UD-4	D-1, D-2, D-3, D-4, D-5	2, 3, 6, 6, 5		
3.0m	Dark Gray 7.5YR (4/1), medium plasticity, soft to stiff, silty Clay, CL.			D-6, D-7	3, 4		
2.5m	Dark Gray 7.5YR (4/1), medium dense, silty Sand, SM.			D-8, D-9	13, 14		
7.5m	Dark Gray 7.5YR (4/1), medium plasticity, medium stiff to very stiff, silty Clay, CL.			D-10, D-11, D-12, D-13, D-14	7, 6, 6, 6, 8		
3.45m	Light Gray 10YR (7/1), very dense, coarse to medium Sand, SP.			D-15, D-16, D-17	35, 41, 45		

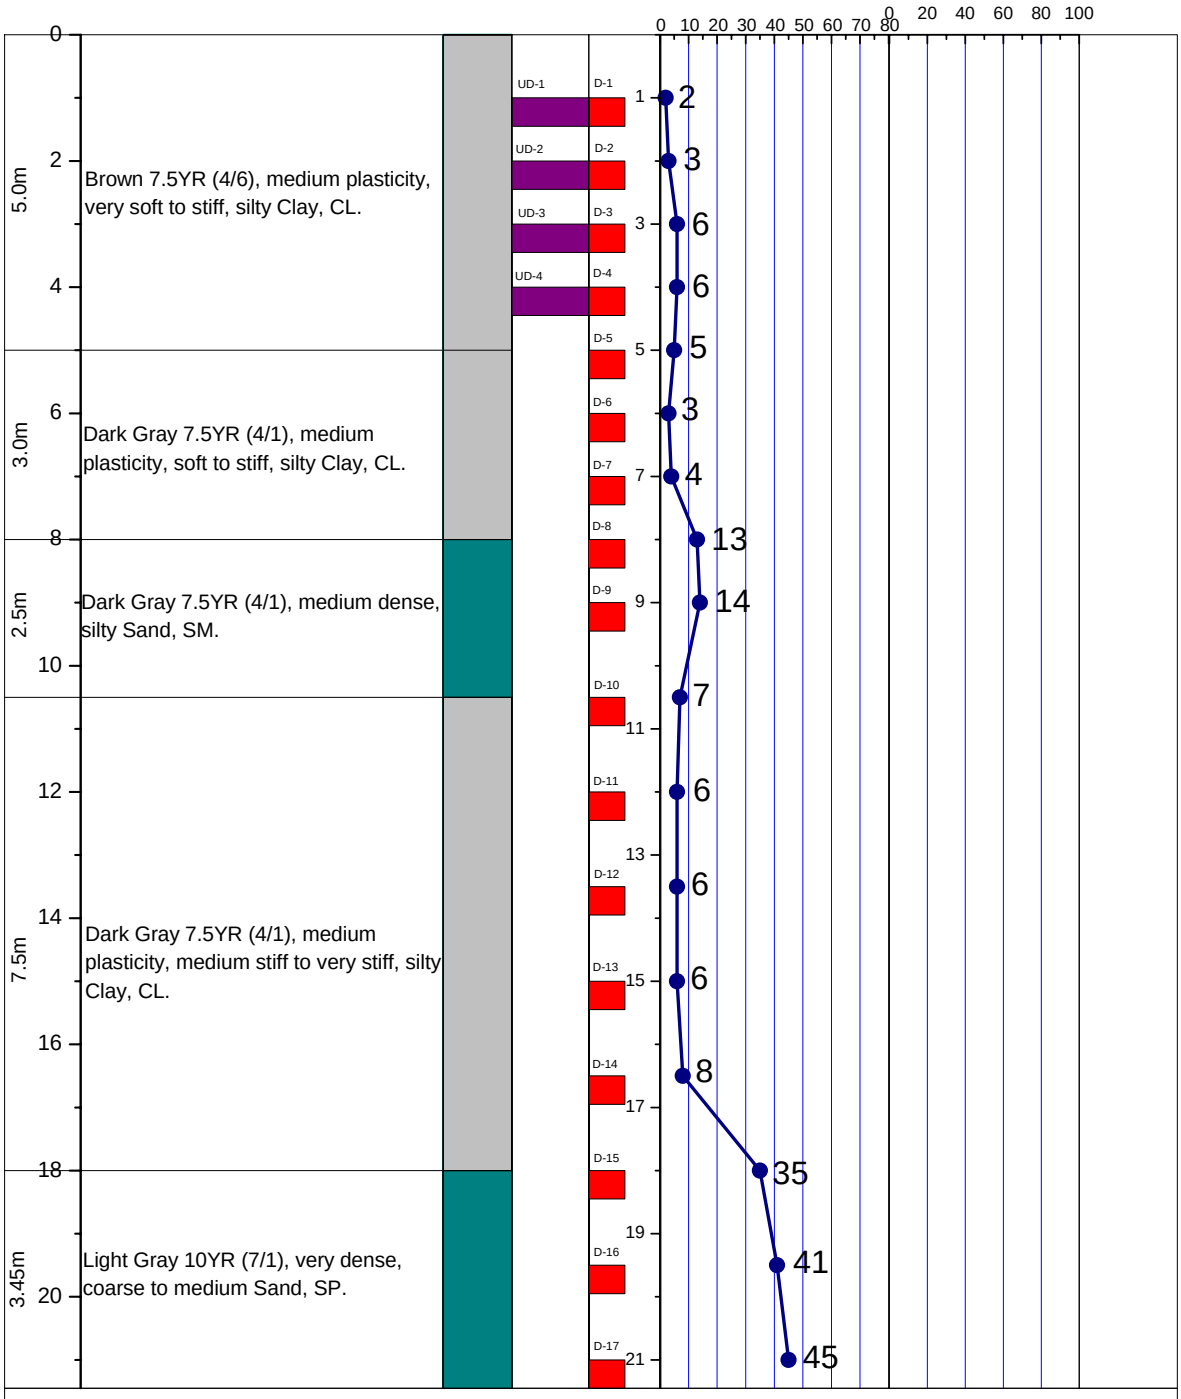

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SAND	SILT	SHALE
PEAT/HIGHLY ORGANIC SOIL	MICACEOUS FINE SAND/SILT	UNDISTURBED SAMPLE	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
