A2	PROSOIL	BOREHOLE NO: BH-A	
		LOCATION : UCEP Technical School, Dharmadas, Rangpur.	
PROJECT : Proposed UCEP TECHNICAL School.		DEPTH OF BORING : 15.0m	R. L.: 1.52m below from Road Level.
CLIENT : UCEP-BANGLADESH		DATE OF BORING : 12-06-2009.	G. W. T : 0.30m above from E. G. L. (Rain water).

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Very pale brown 10YR (7/3), loose, cohesionless silt, SM.			D-1 to D-3	4, 4, 4		
3.0m	Gray 10YR (6/1), loose to medium dense, cohesionless silt, SM.			D-4 to D-6	5, 5, 9		
4.5m	Gray 10YR (6/1), medium dense to dense, fine sand, SM.			D-7 to D-9	17, 20, 30		
4.95m	Very pale brown 10YR (7/3), dense to very dense, fine sand, SM.			D-10 to D-12	31, 37, 41		

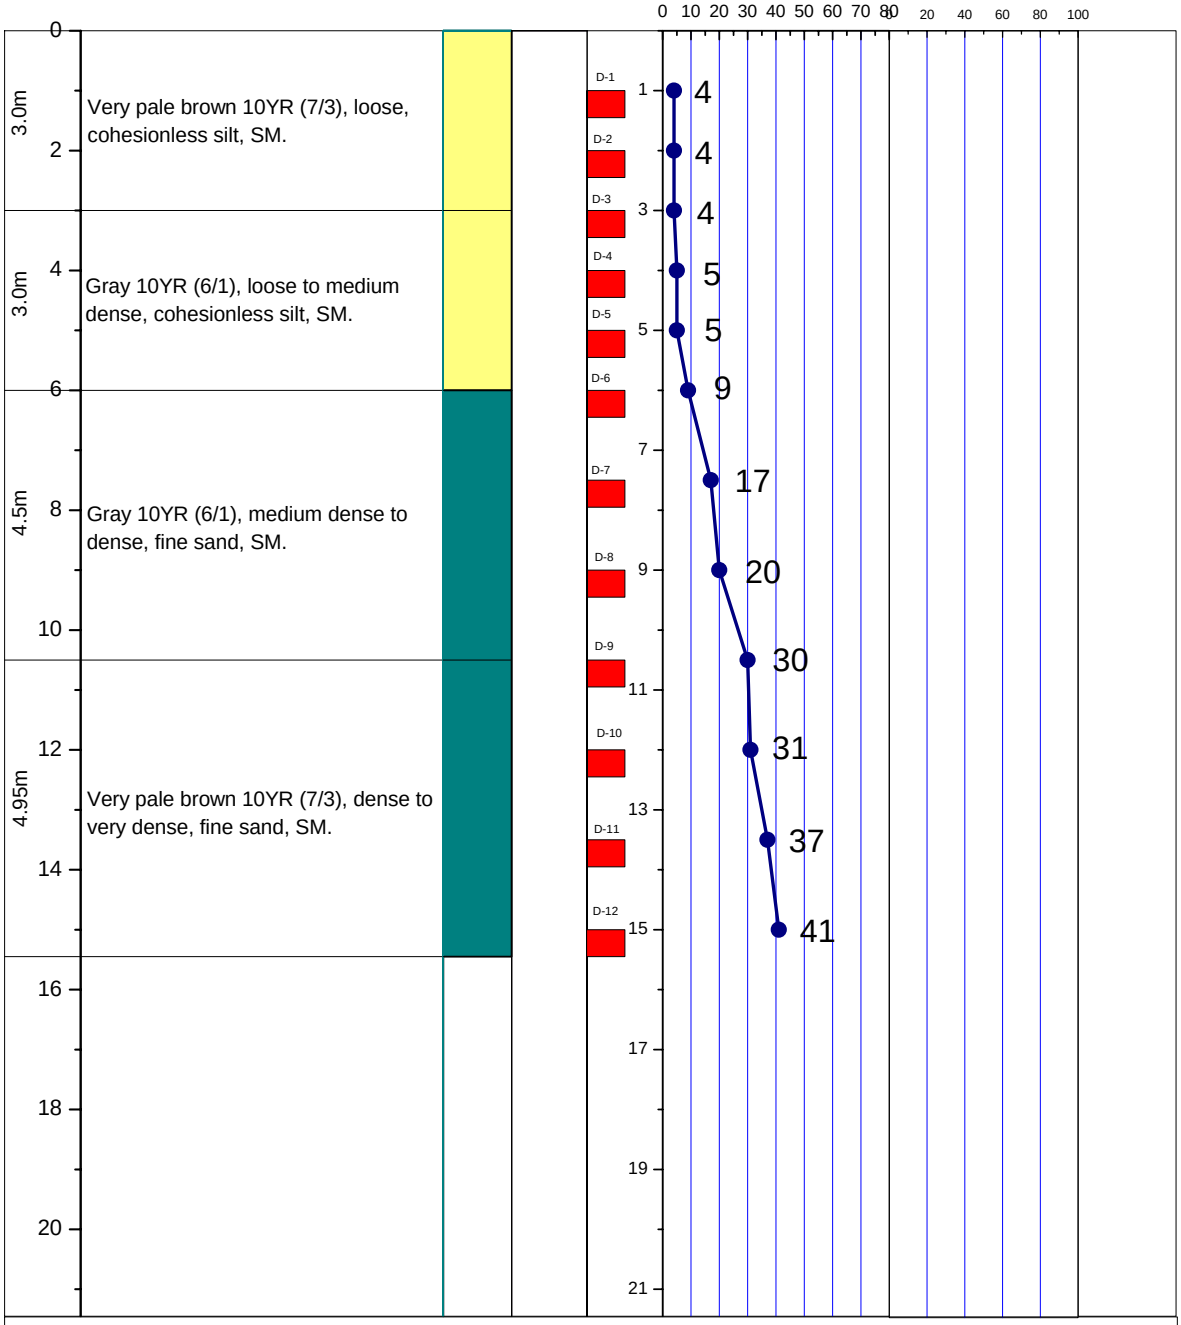

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

- PLASTIC SILTY CLAY
- LOW PLASTIC CLAYEY SILT
- NON PLASTIC SILT
- SAND
- ORGANIC
- UNDISTURBED SAMPLE
- DISTURBED SAMPLE
- SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
