A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION: Gopalpur, Comilla.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING: 21.0m	R. L.: On Road Level.
CLIENT : AXIATA (Bangladesh) Ltd.	DATE OF BORING: 19-03-2010.	G. W. T : 6.10m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Pale Brown 10YR (8/2), medium plasticity, medium stiff, silty Clay, CL.		UD-1, UD-2	D-1, D-2, D-3	7, 5, 3		
3.0m	Very pale Brown 10YR (8/3), loose to very loose Silt, ML.			D-4, D-5, D-6	2, 2, 1		
2.0m	Very pale Brown 10YR (8/3), medium plasticity, very soft Clay, CL.			D-7, D-8	1, 2		
13.45m	Light bluish Gray Gley2 (7/1), very loose to very dense, fine Sand, SW.			D-9, D-10, D-11, D-12, D-13, D-14, D-15, D-16, D-17	3, 6, 10, 12, 14, 28, 38, 36, 40		

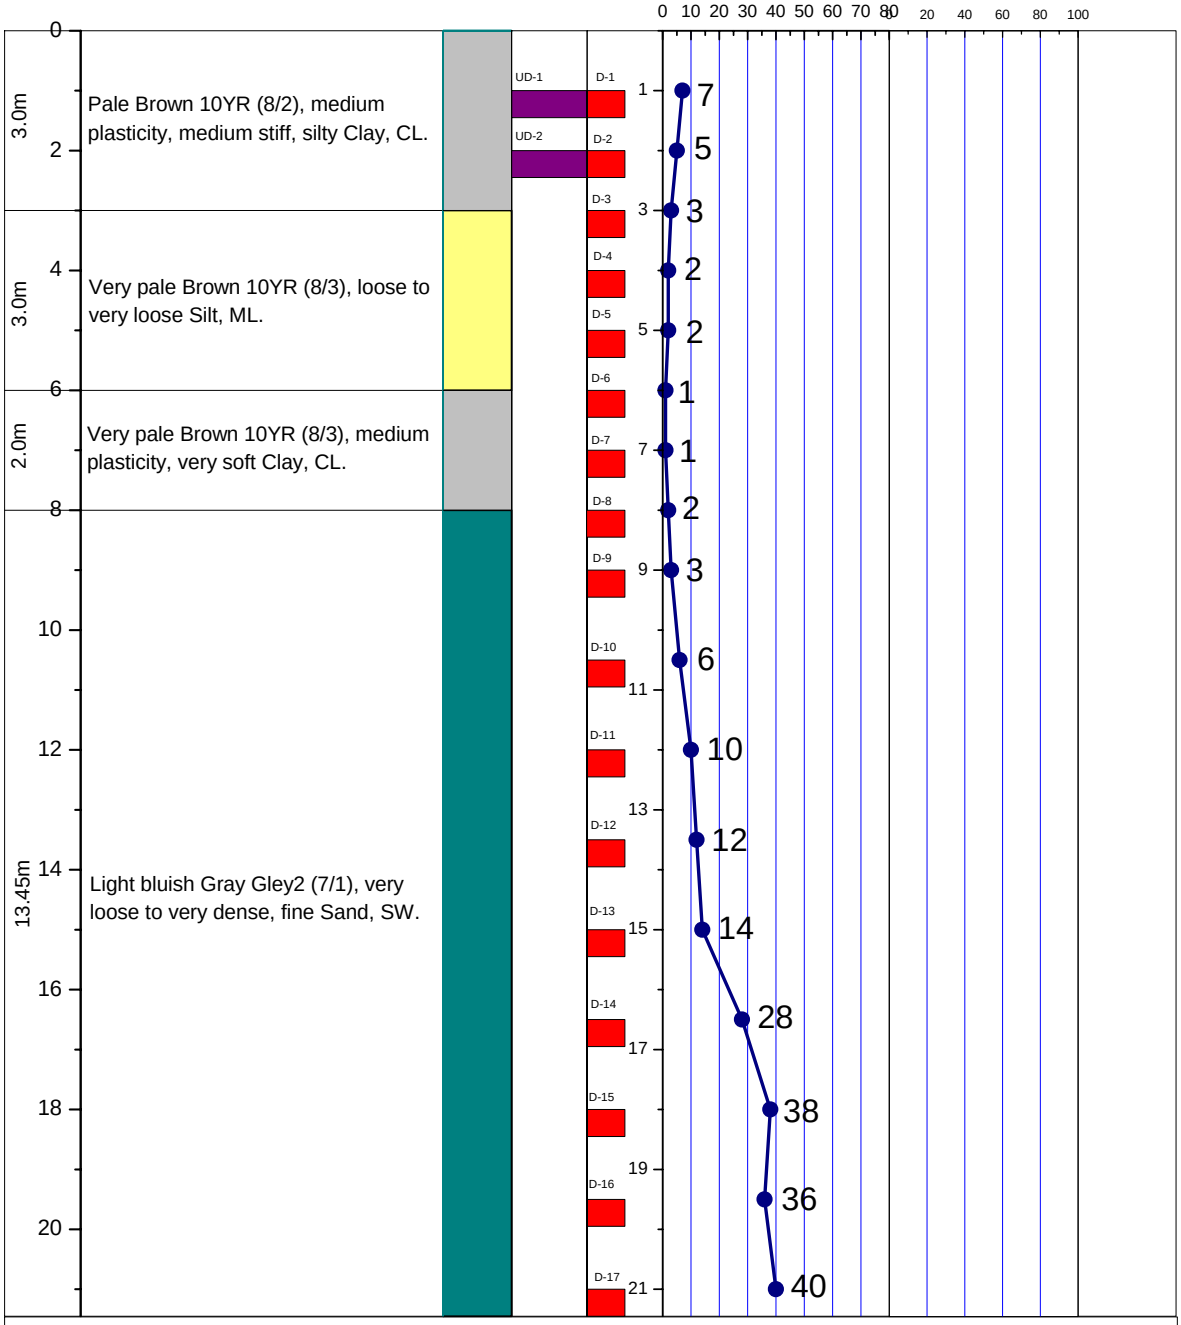

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY | SAND | SILT | SHALE

PEAT/HIGHLY ORGANIC SOIL | MICACEOUS FINE SAND/SILT | UNDISTURBED SAMPLE | DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
