A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION: Hodgara Doxin (Askamta), Comilla.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING: 15.0m	R. L.: 0.91m below from Road Level.
CLIENT : AXIATA (Bangladesh) Ltd.	DATE OF BORING: 08-06-2010.	G. W. T : 0.61m above from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
4.0m	Grayish Brown 2.5YR (5/2), medium dense to dense, Silt, ML.			D-1 to D-4	12, 19, 17, 20		
11.45m	Gray Gley1 (5/1), dense to very dense, silty Sand, SM.			D-5 to D-11	22, 34, 36, 42, 50, 50, 50, 50		Over
6.0m	Boring was not possible due to very dense fine Sand.			D-12, D-13	50, 50		Over

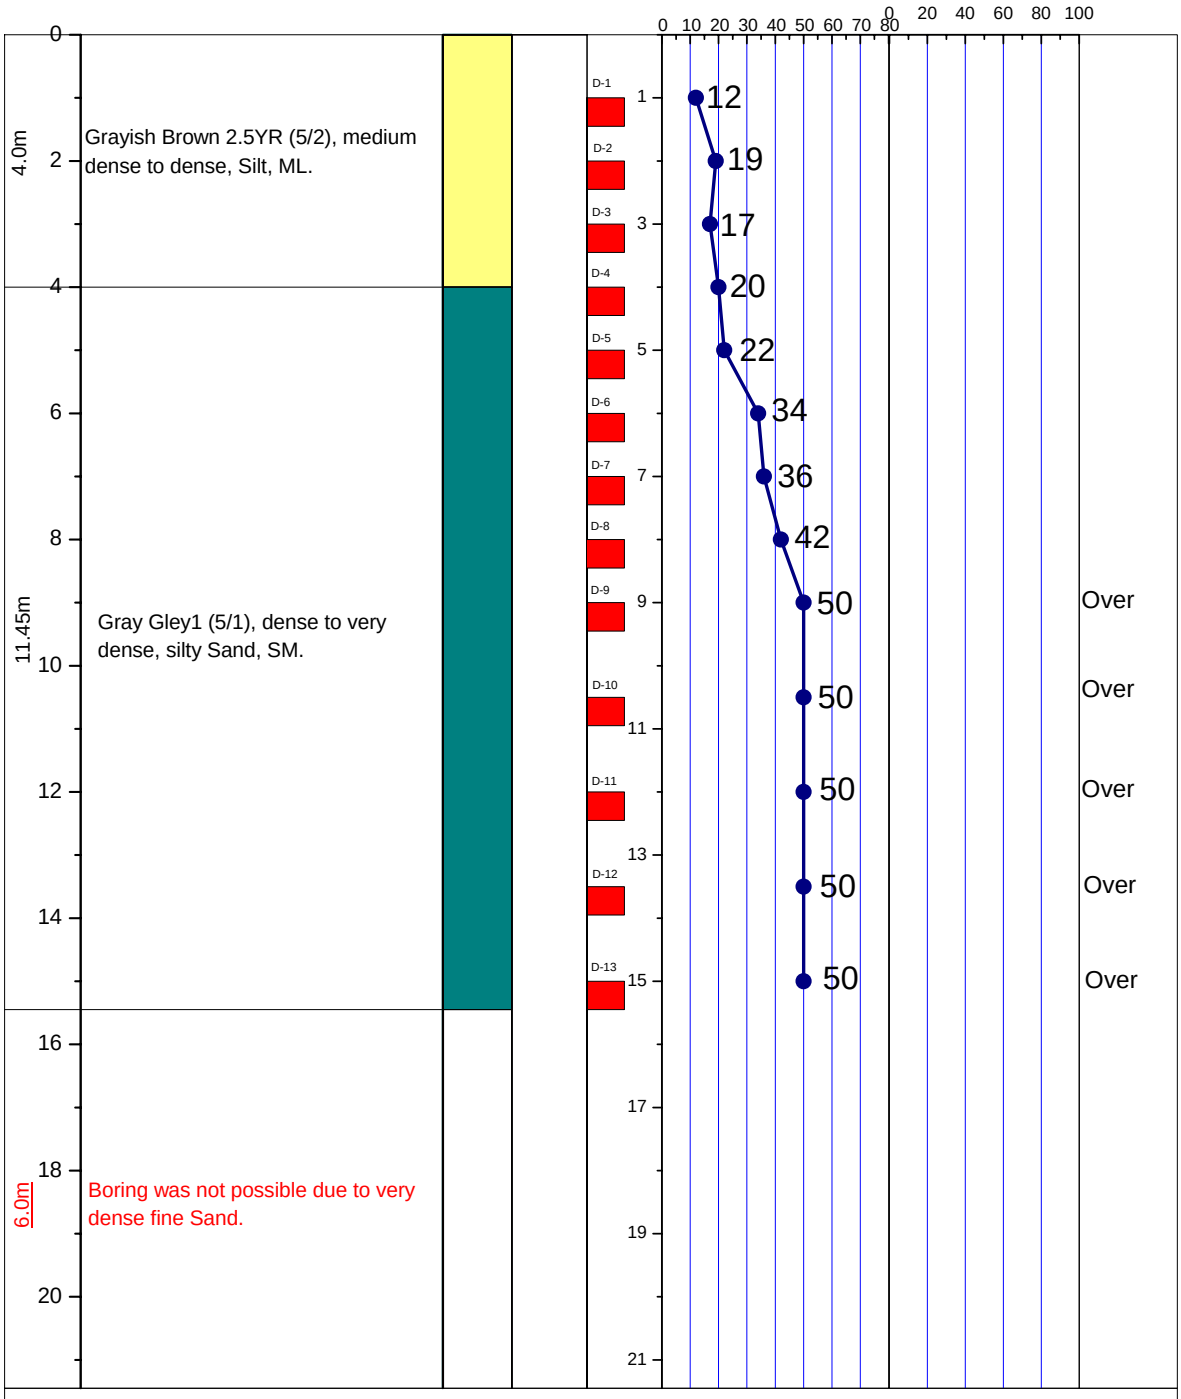

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SAND	SILT	SHALE
PEAT/HIGHLY ORGANIC SOIL	MICACEOUS FINE SAND/SILT	UNDISTURBED SAMPLE	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
