A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION: Maulana Vasani University, Tangail.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING: 21.0m	R. L.: On Road Level.
CLIENT : Grameenphone Ltd.		DATE OF BORING: 27-05-2012.	G. W. T : 0.60m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Rubbish.			D-3 to D-6	9, 10, 9, 14		
4.5m	Brown 7.5YR (5/4), medium dense to dense, Silt, ML.			D-7 to D-8	21, 26		
6.0m	Pale Brown 10YR (6/3), medium dense to very dense, fine Sand, SM.			D-9 to D-11	34, 35, 42		
7.95m	Light Brownish Gray 10YR (6/2), very dense, fine Sand, SM.			D-12 to D-16	44, 49, 50, 50, 50		Over, Over, Over

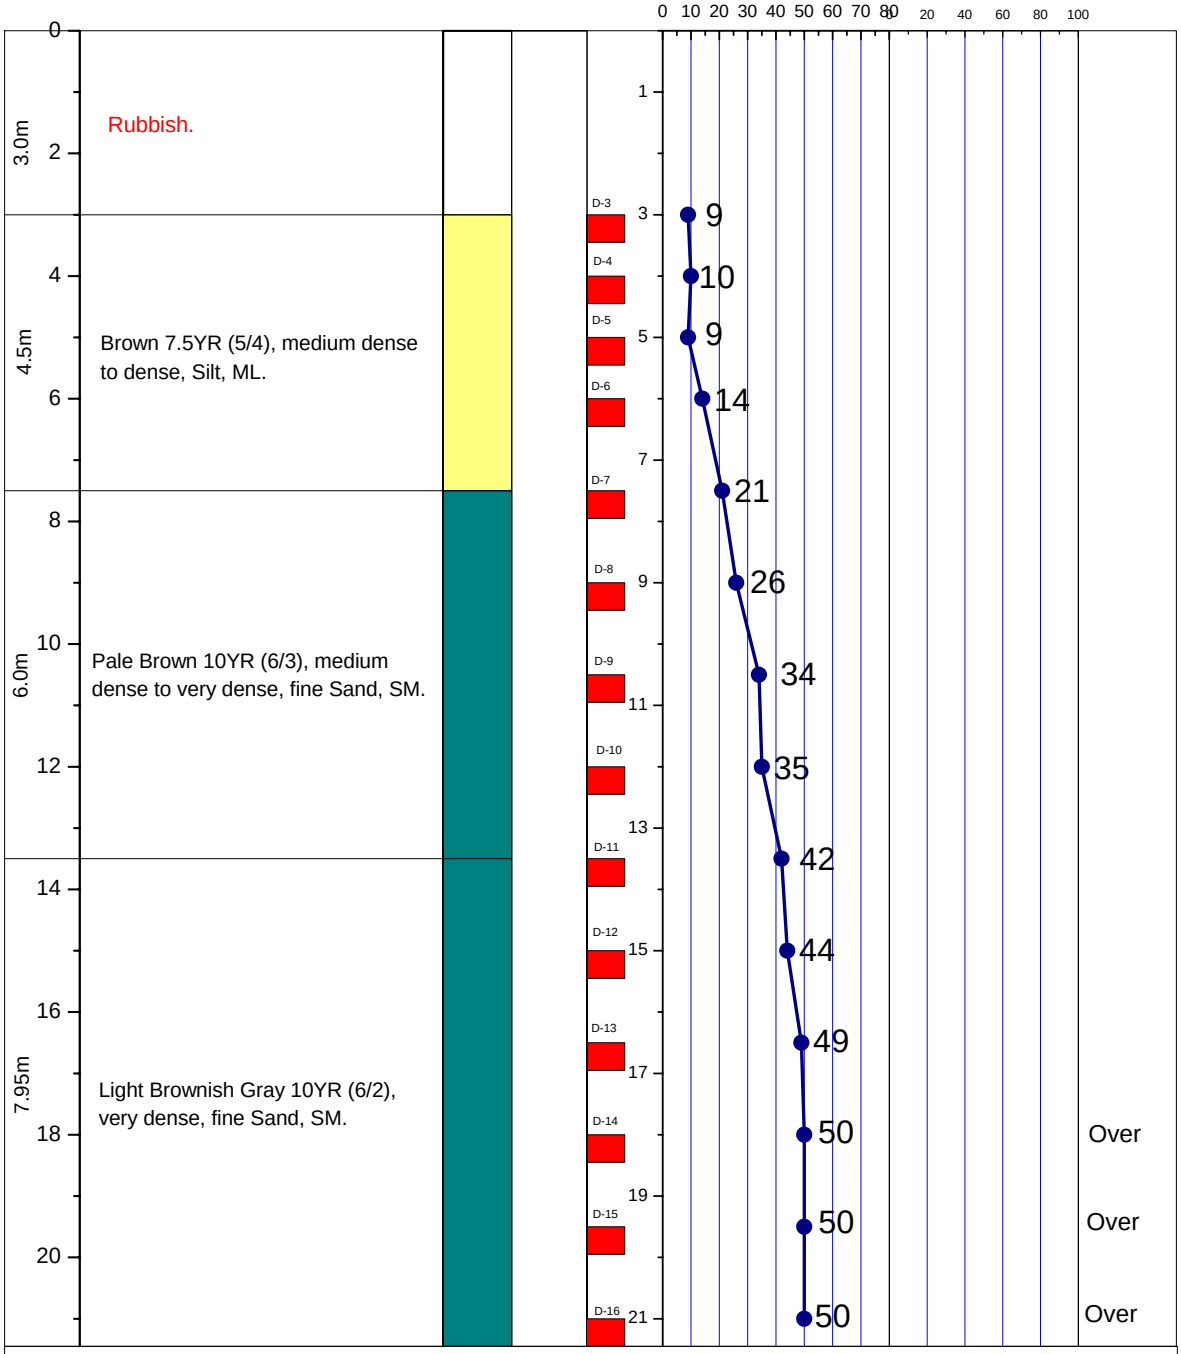

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY | SHALE | SILT | SAND

PEAT/HIGHLY ORGANIC SOIL | MICACEOUS FINE SAND/SILT | UNDISTURBED SAMPLE | DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
