A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION: West Ladua, Rampur Bazar , Hajiganj, Chandpur.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING: 21.0m	R. L.: 0.46m below from Road Level.
CLIENT : AXIATA (Bangladesh) Ltd.		DATE OF BORING: 17-01-2013.	G. W. T : 2.44m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Brown 7.5YR (5/2), loose, Silt, ML.			D-1 to D-3	4, 3, 4		
4.0m	Dark Gray 10YR (4/3), medium plasticity, very soft to medium stiff, Clay, CL.			D-3 to D-6	2, 3, 3		
14.45m	Gray 10YR (5/1), medium dense to very dense, fine Sand, SM.			D-6 to D-17	6, 9, 16, 19, 24, 24, 25, 28, 35, 39, 42		

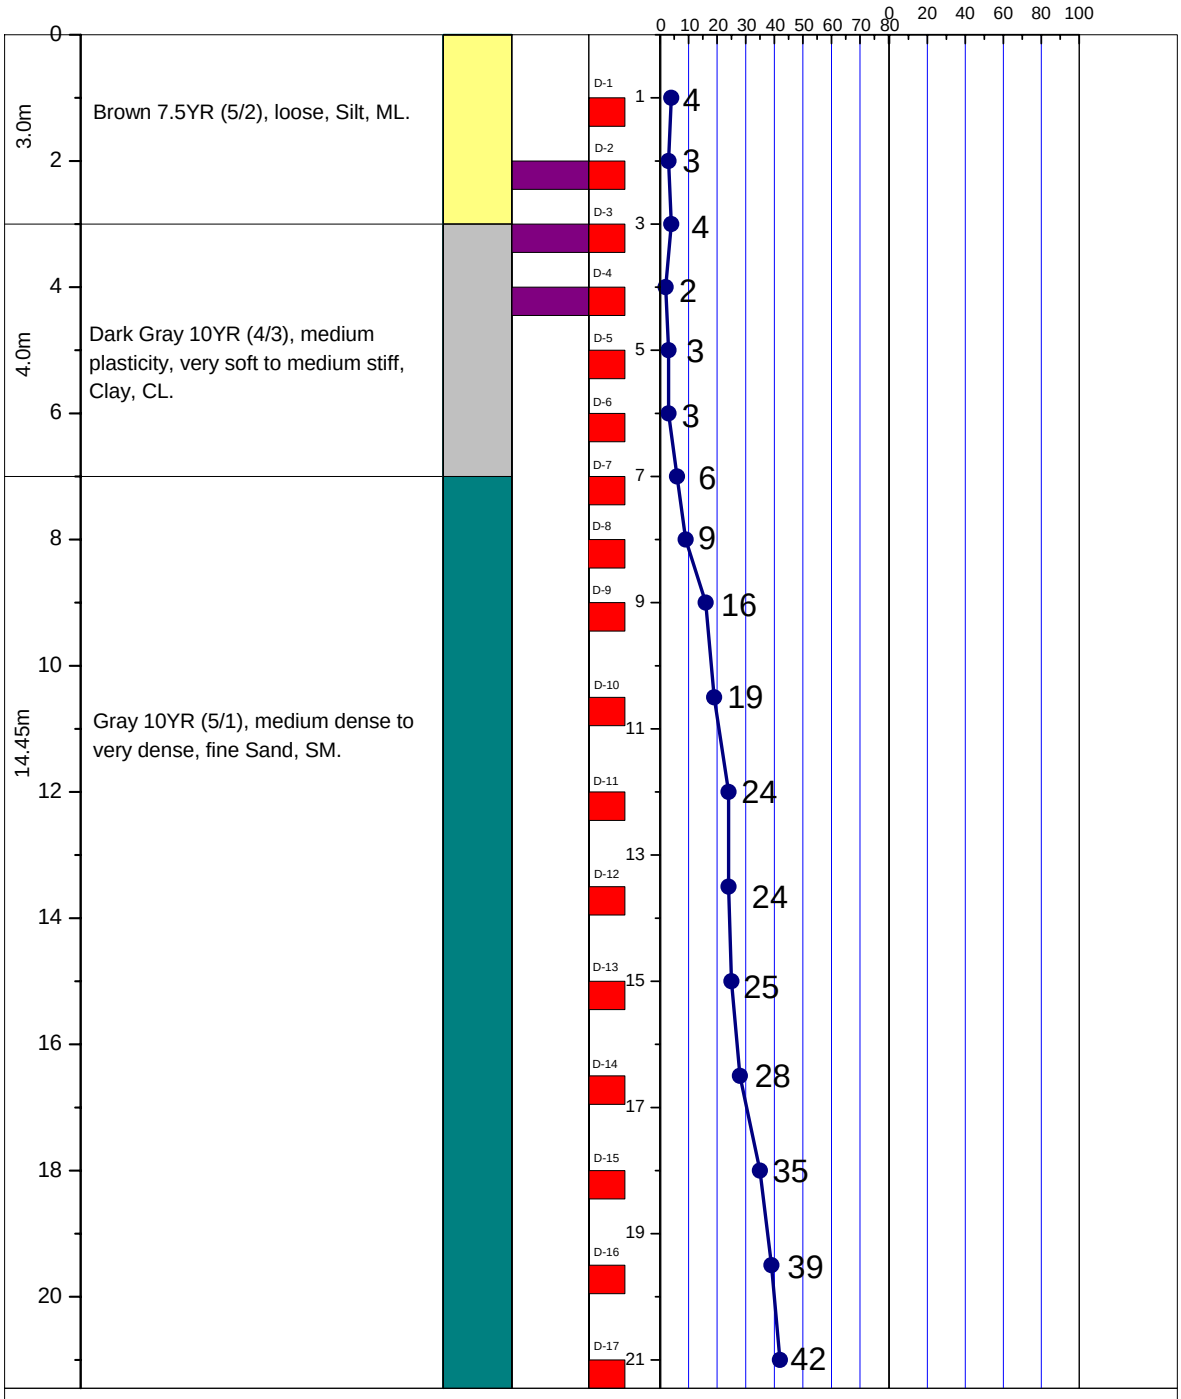

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SAND	SILT	SHALE
PEAT/HIGHLY ORGANIC SOIL	MICACEOUS FINE SAND/SILT	UNDISTURBED SAMPLE	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
