| A2 | PROSOIL | BOREHOLE NO: BH-1 | |
|---|---|---|---|
| | | LOCATION: Goalbatan, Rumchondopur, Sharikndi, Bogura. | |
| PROJECT : Telecommunication Tower. | | DEPTH OF BORING: 21.0m | R. L.: 0.61m below from Road Level. |
| CLIENT : Grameenphone Ltd. | | DATE OF BORING: 18-12-2014. | G. W. T : 1.52m below from E. G. L. |

| THICKNESS | SOIL STRATA | BORELOG | UNDISTURBED SAMPLE | DISTURBED SAMPLE | DEPTH (m) SPT VALUES ( BLOWS / 300mm ) | Grain Size Distribution, % Clay %, Silt %, Sand % | Max$^{m}$ Penetration |
|---|---|---|---|---|---|---|---|
| 3.0m | Brown 7.5YR (5/3), very loose to medium dense, silty Sand, SM. | | | D-1 to D-3 | 1, 2, 8 | | |
| 18.45m | Gray 7.5YR (5/1), medium dense to very dense, fine Sand, SM. | | | D-4 to D-16 | 9, 11, 14, 18, 19, 28, 32, 33, 37, 43, 44, 46, 48 | | |

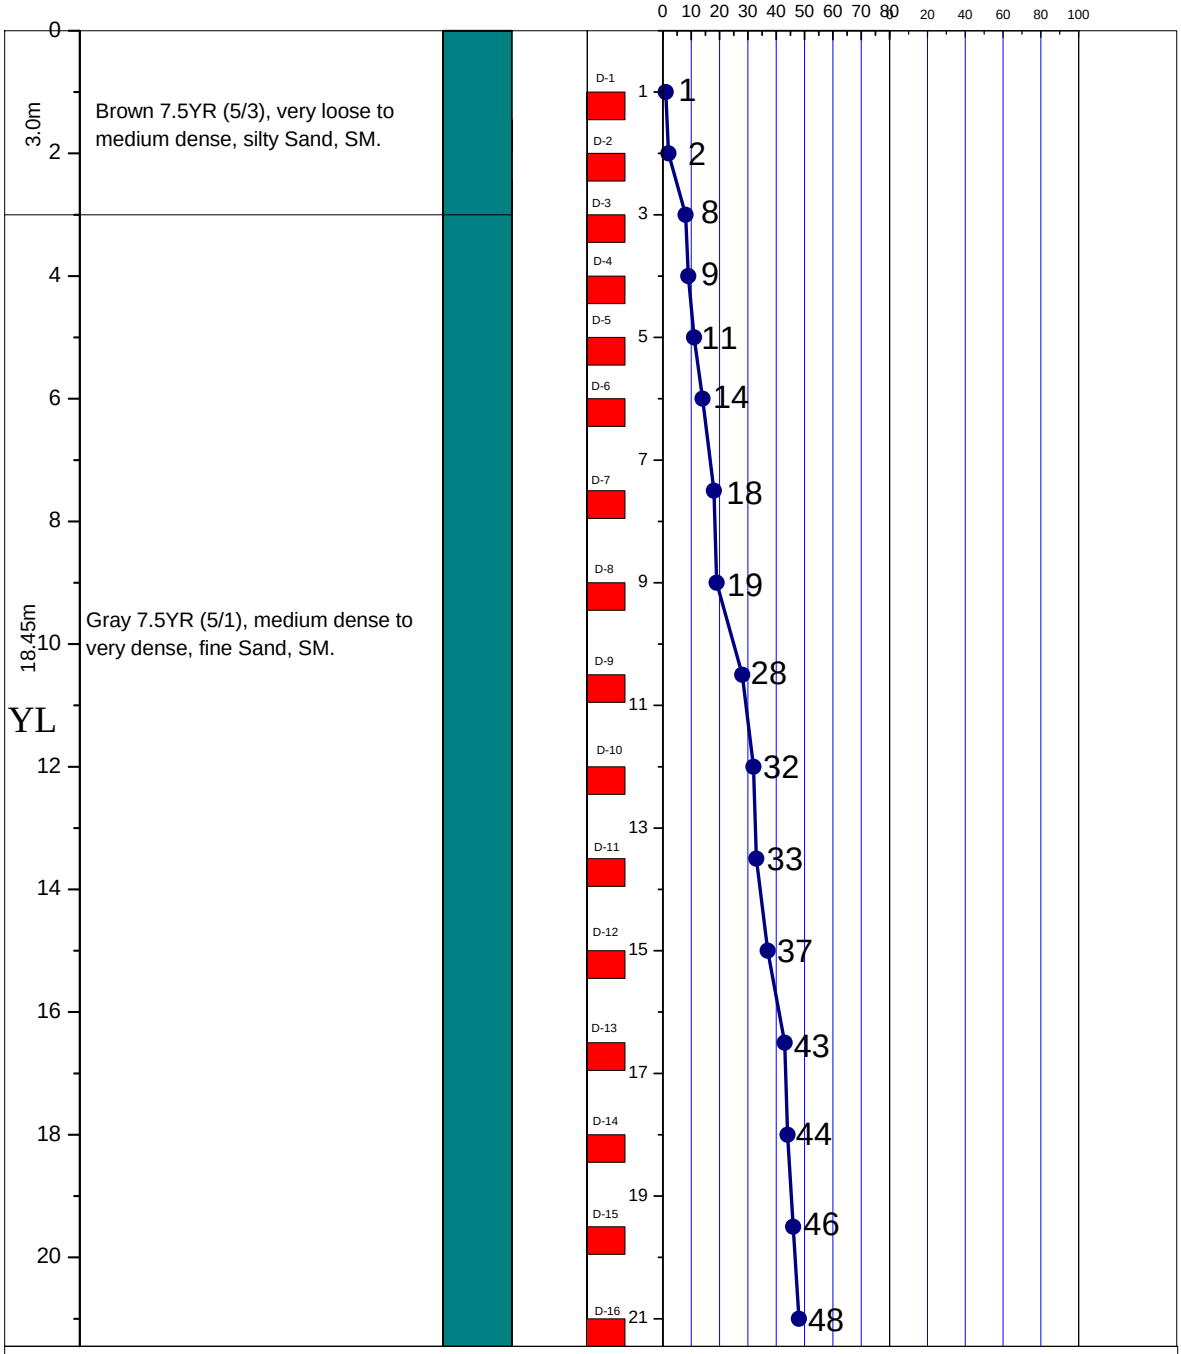


LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY | SHALE | SILT | SAND

PEAT/HIGHLY ORGANIC SOIL | MICACEOUS FINE SAND/SILT | UNDISTURBED SAMPLE | DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX$^{m}$ PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
