A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION : Vaukshar, Barura, Comilla.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING : 15.45m	R. L.: 1.50m below from Road Level.
CLIENT : Warid Telecom International Ltd.		DATE OF BORING: 27-10-2010.	G. W. T : 0.61m below from E.G.L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Dark grayish Brown 10YR (4/2), mediur dense to loose, Silt, ML.			D-1, D-2, D-3	8, 5, 11		
6.0m	Dark Gray 2.5YR (4/1), Loose to very dense , Silt, ML.			D-4, D-5, D-6	37, 40, 50		
6.45m	Dark grayish Brown 10YR (4/2), very dense, silty Sand, SM.			D-7, D-8, D-9, D-10	50, 50, 50, 50		Over, Over, Over, Over, Over

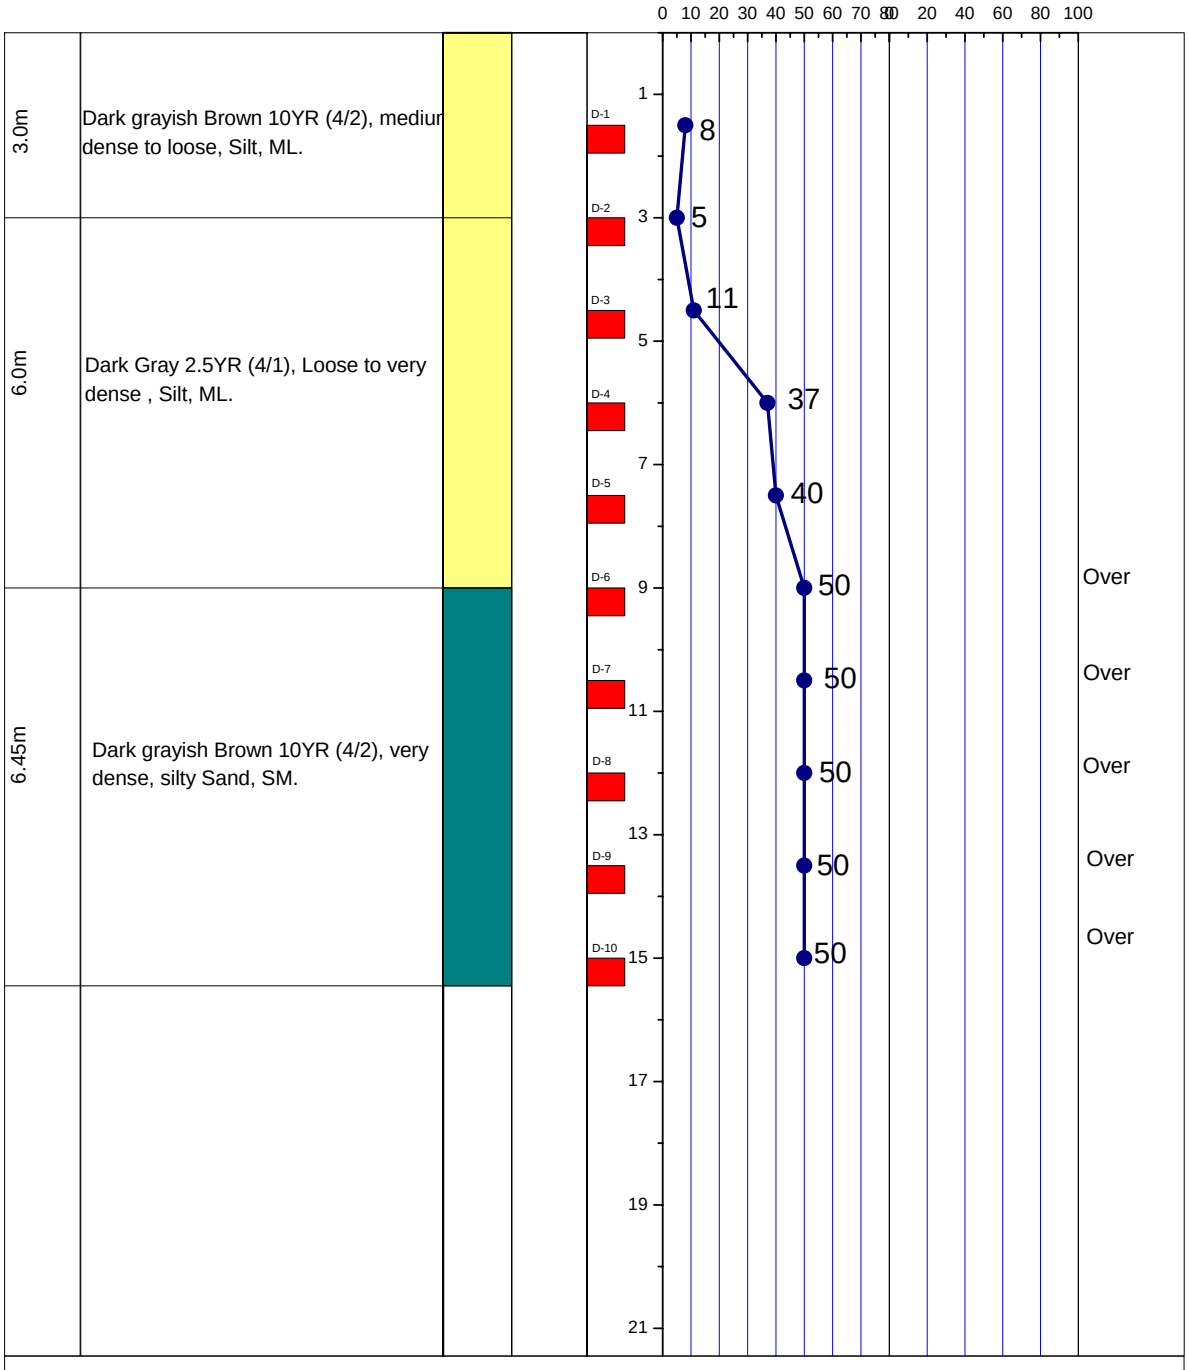

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SAND	SHALE	UNDISTURBED SAMPLE
MICACEOUS FINE SAND/SILT	SILT	PEAT/HIGHLY ORGANIC SOIL	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
