A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION : Roygorth, Golabganj, Sylhet. (24°48'53.7904"N, 92°02'59.1873"E).	
PROJECT : Roygorth GPS, (Multi-purpose Cyclone Shelter/Govt. Primary School)		DEPTH OF BORING : 10.5m	R. L.: On Road Level.
CLIENT : US Army Corps of Engr, Alaska District. THROUGH : AUSPICIOUS, QA Contractor.		DATE OF BORING : 18-04-2013.	G. W. T : 5.18m below from E.G.L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
7.5m	Gray 7.5YR (5/1), very loose to very dense, fine Sand, SM.			D-1 to D-4	2, 6, 4, 5		
3.45m	Gray 7.5YR (5/1), very dense, pebble and cobble grain Sand, SP.			D-5 to D-7	50, 50, 50		85, 58, 85

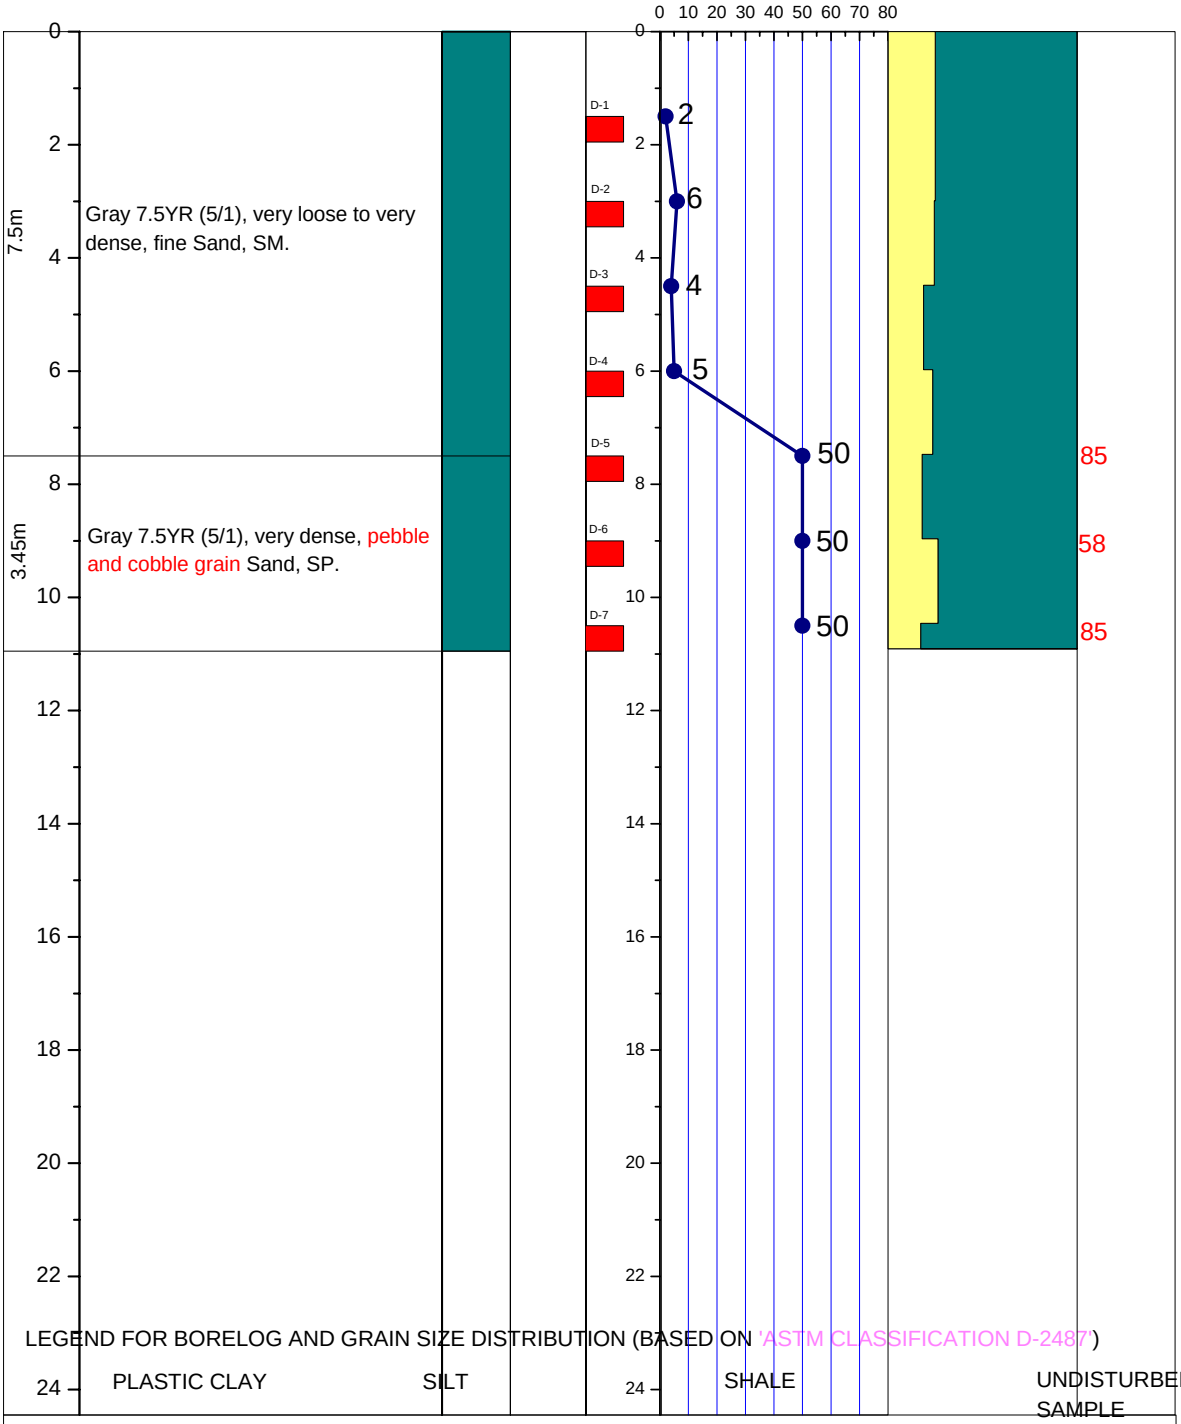

LEGEND FOR BOREHOLE AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY

SILT

SHALE

UNDISTURBED SAMPLE

MICACEOUS FINE SAND/SILT

SAND

PEAT/HIGHLY ORGANIC SOIL

DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS AFTER 50 BLOWS PENETRATION WERE MEASURED

A6	PROSOIL	BOREHOLE NO: BH-1 (SETTLEMENT CALCULATION)
		LOCATION : Roygorth, Golabganj, Sylhet. (24°48'53.7904"N, 92°02'59.1873"E).
PROJECT : Roygorth GPS, (Multi-purpose Cyclone Shelter/Govt. Primary School)		**SHALLOW FOOTING:** B: 0.6m, L=0.9m, P=100kpa
CLIENT : US Army Corps of Engr, Alaska District. THROUGH : AUSPICIOUS, QA Contractor.		**Shear failure Safety Factor=0.3**

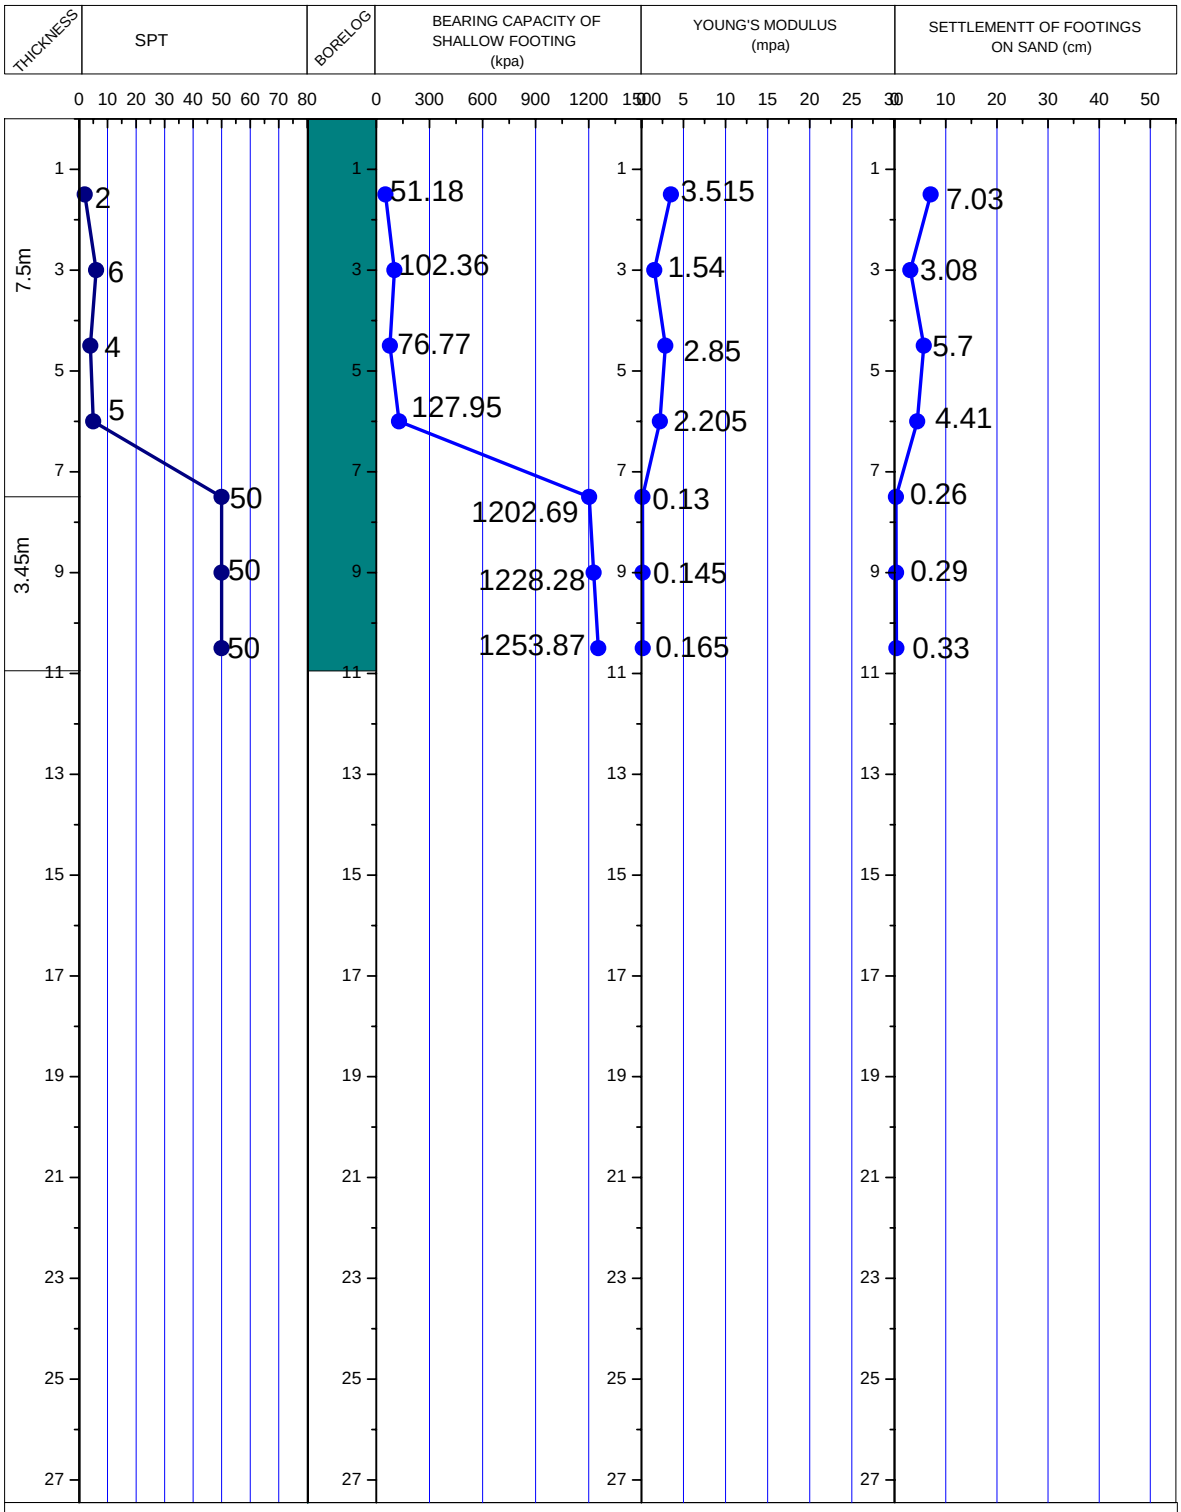

LEGEND FOR BOREHOLE AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

- PLASTIC CLAY
- SILT
- SHALE
- UNDISTURBED SAMPLE
- MICACEOUS FINE SAND/SILT
- SAND
- PEAT/HIGHLY ORGANIC SOIL

SETTLEMENT CALCULATION BY SOFTWARE: **NOVO SPT CORRELATION PROGRAM.**
