A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION: Amduar, Azgora, Laksham, Comilla.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING: 21.0m	R. L.: 1.22m below from Road Level.
CLIENT : AXIATA (Bangladesh) Ltd.		DATE OF BORING: 05-01-2013.	G. W. T : 0.76m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
2.0m	Very pale Brown 10YR (8/3), loose to medium dense, silty Sand, SM.			D-1 to D-3	5, 8, 10		
19.45m	Gray 10YR (6/1), medium dense to very dense, fine Sand, SM.			D-4 to D-17	17, 20, 22, 37, 36, 38, 38, 42, 44, 45, 48, 50, 50, 50		Over, Over, Over

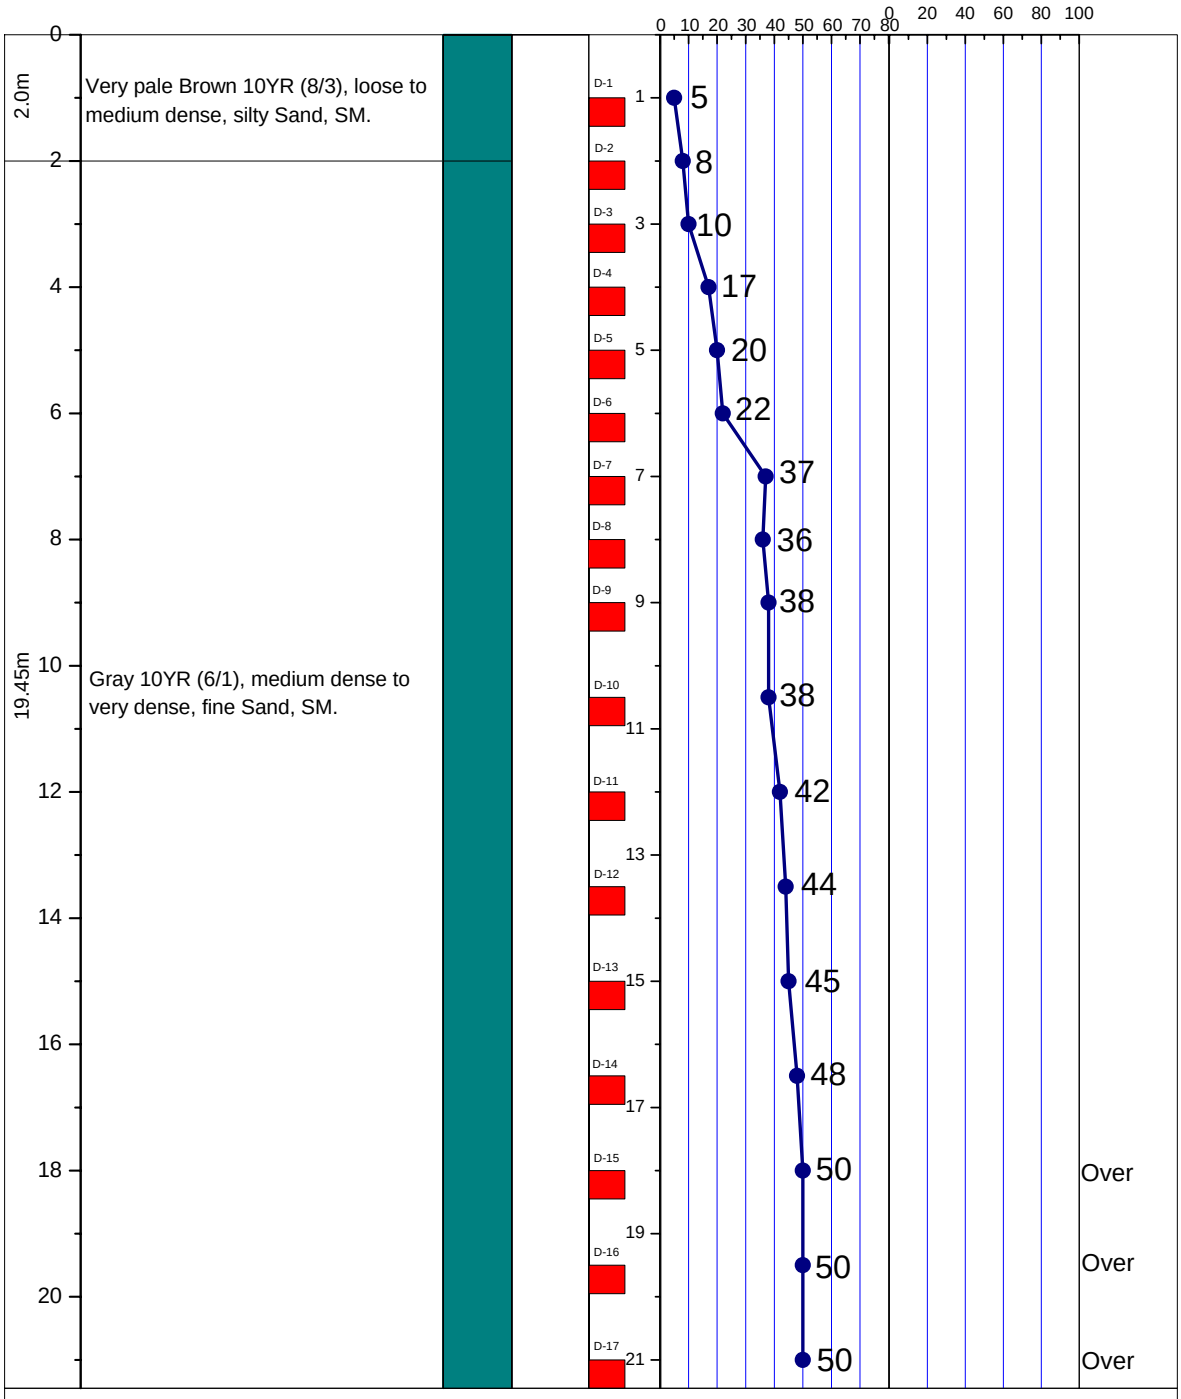

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SAND	SILT	SHALE
PEAT/HIGHLY ORGANIC SOIL	MICACEOUS FINE SAND/SILT	UNDISTURBED SAMPLE	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
