A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION: Vill: Sen Bhanga Bari, P. O: Sen Bhanga Bari, P. S: Belkuchi, Dist: Sirajganj.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING: 21.0m	R. L.: 1.52m below from Road Level.
CLIENT : AXIATA (Bangladesh) Ltd.		DATE OF BORING: 22-02-2015.	B. W. T : 2.43m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Brown 7.5YR (5/3), very loose to loose, silty sand, SM.			D-1 to D-3	2, 3, 4		
2.0m	Gray 7.5YR (5/1), loose to medium dense, silty sand, SM.			D-4 to D-5	6, 12		
16.45m	Light Gray 10YR (7/1), medium dense to very dense, fine sand, SM.			D-6 to D-17	20, 24, 26, 30, 35, 37, 39, 40, 42, 44, 46, 48		

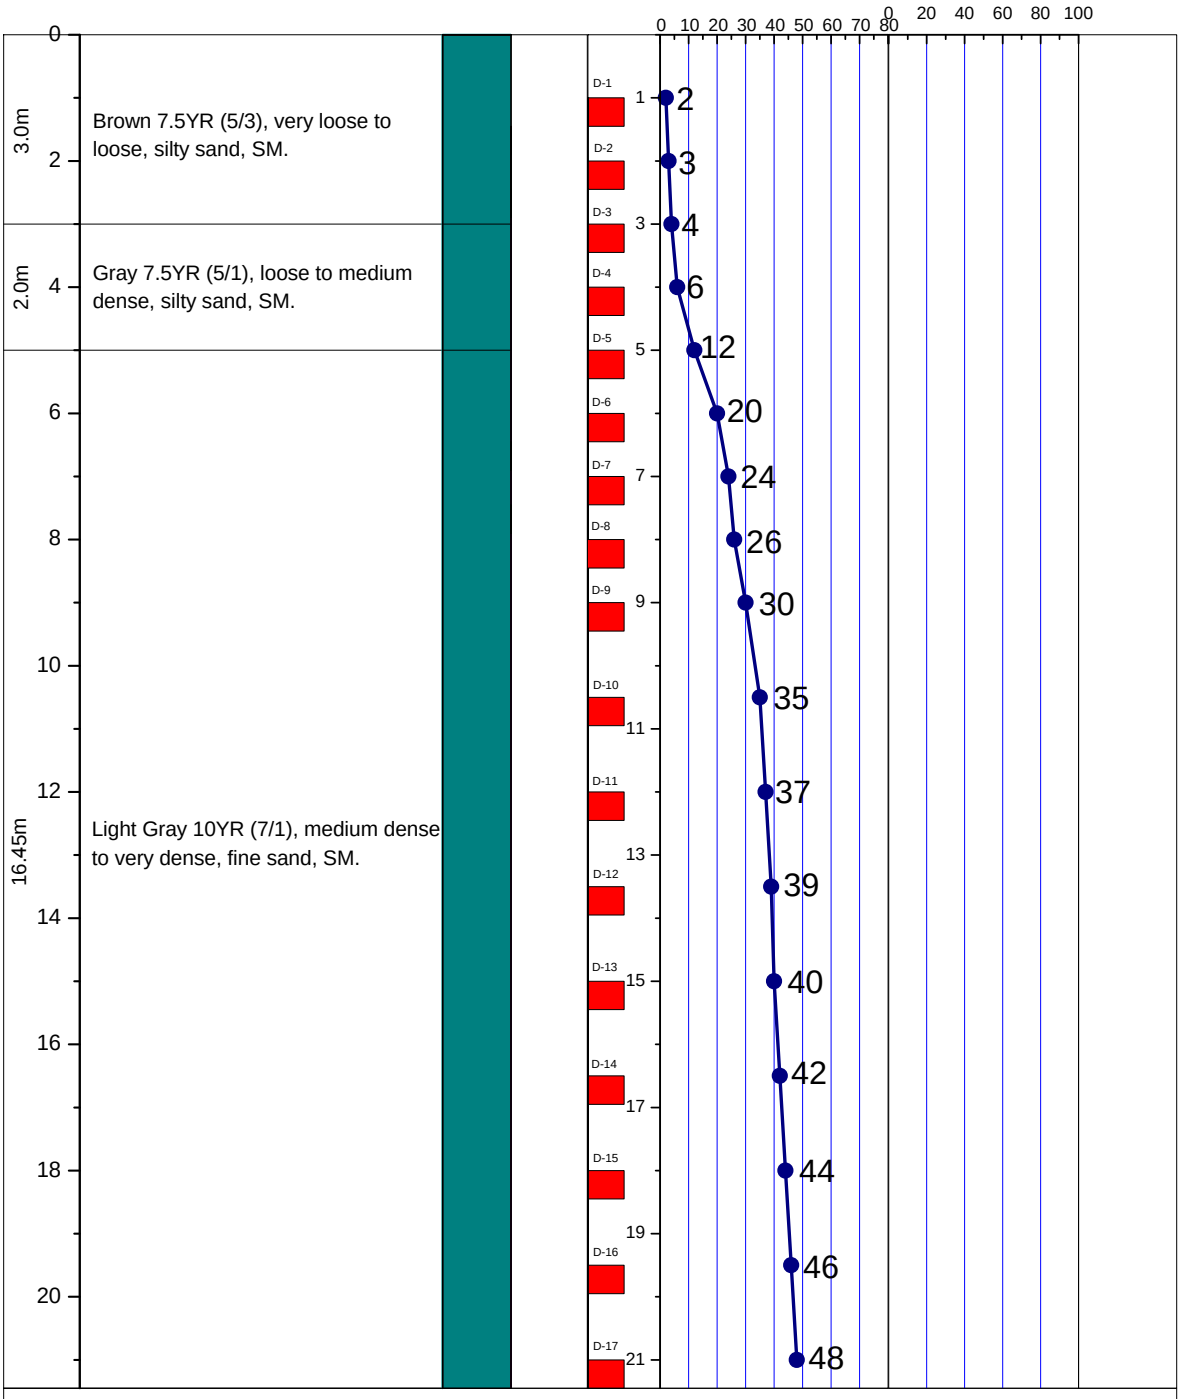

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SAND	SILT	SHALE
PEAT/HIGHLY ORGANIC SOIL	MICACEOUS FINE SAND/SILT	UNDISTURBED SAMPLE	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED

XB

PROSOIL FOUNDATION CONSULTANT DHAKA-1205 69/B, INDIRA ROAD

Md. Shamsul Islam

(Engr. Md. Shamsul Islam)
B. Sc. Engg. (Civil, BUET),
M. Engg. (Geotech), MCSD, FIEB, CCPE
Chief Executive
Prosoil Foundation Consultant
