A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION: Dorjimoti, Tinchati, Jingrabari, Kanaighat, Sylhet.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING: 21.0m	R. L.: 0.60m below from Road Level.
CLIENT : Grameenphone Ltd.		DATE OF BORING: 26-05-2012.	G. W. T : 2.06m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
2.0m	Brown 7.5YR (5/4), medium plasticity, soft to very soft, silty Clay, CL.		UD-1, UD-2	D-1, D-2	3, 2		
8.5m	Very dark Gray 7.5YR (3/1), medium plasticity, very soft to soft, silty Clay, CL.		UD-3, UD-4	D-3, D-4, D-5, D-6, D-7, D-8, D-9	1, 5, 5, 5, 5, 6, 5		
1.5m	Black 7.5YR (2.5/1), medium plasticity, soft to medium stiff, organic Clay, CL.			D-10	9		
3.0m	Dark Gray 7.5YR (4/1), medium dense to very dense, Silt, ML.			D-11, D-12, D-13	11, 30, 29		
6.45m	Light Gray 10YR (7/1), dense to very dense, fine Sand, SM.			D-14, D-15, D-16	29, 32, 34		

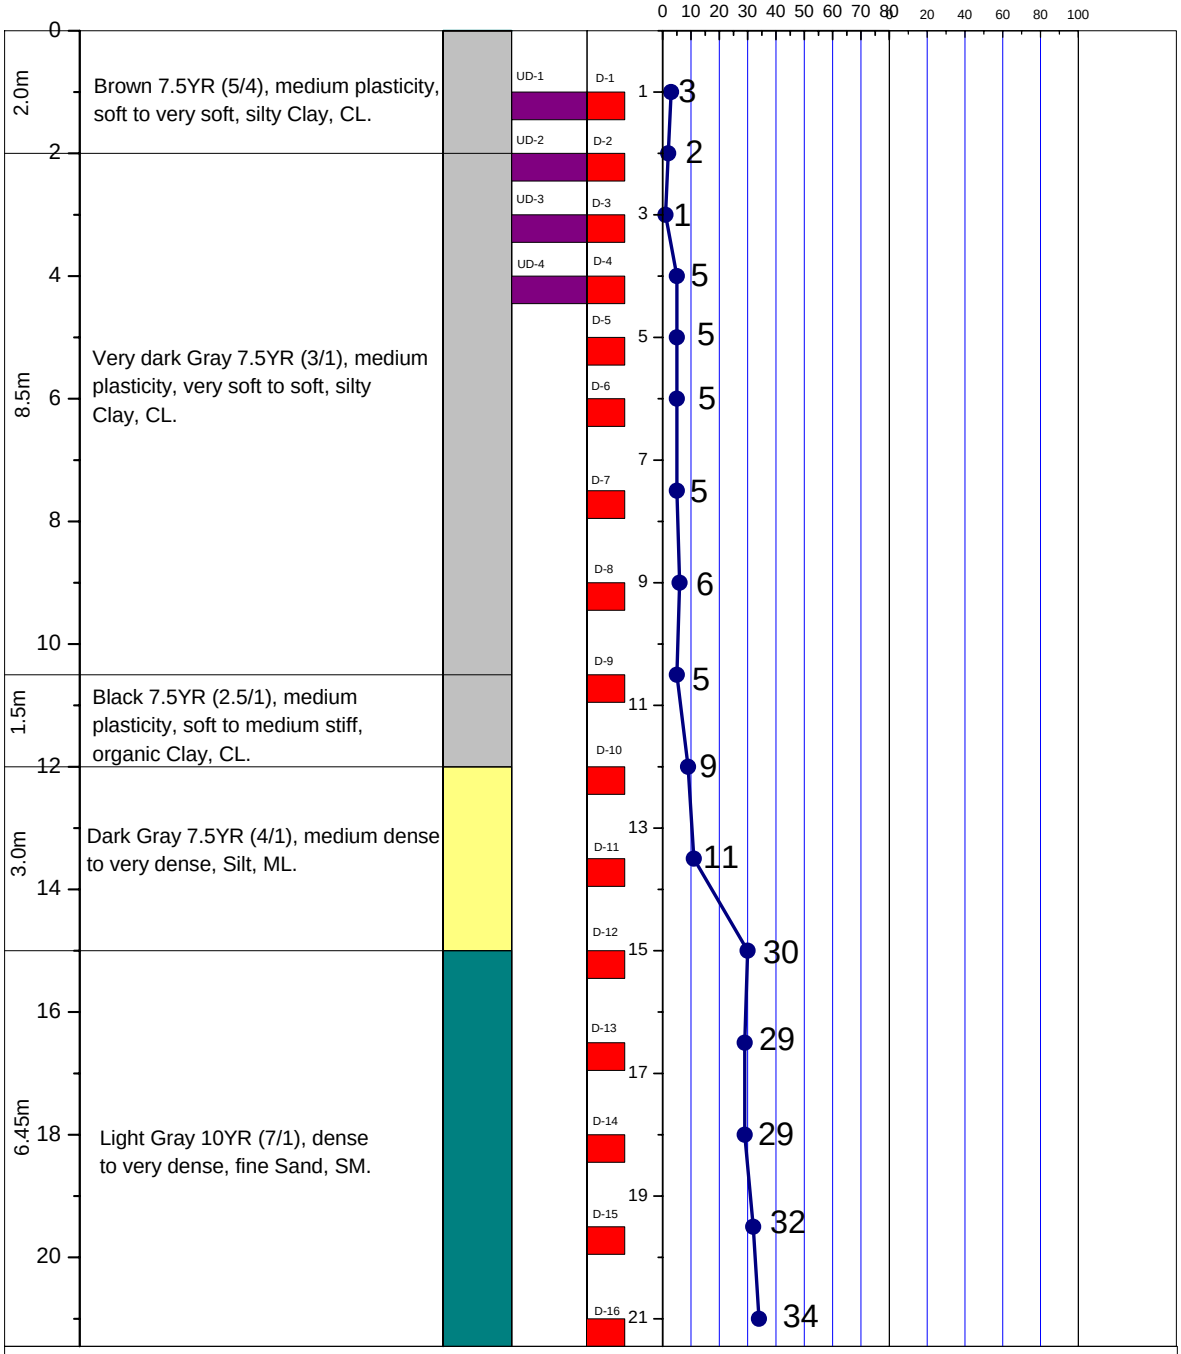

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY | SHALE | SILT | SAND

PEAT/HIGHLY ORGANIC SOIL | MICACEOUS FINE SAND/SILT | UNDISTURBED SAMPLE | DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
