A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION : Badiakhali, Gaibandha.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING : 21.0m	R. L.: 1.37m below from Road Level.
CLIENT : AXIATA (Bangladesh) Ltd.		DATE OF BORING : 07-03-2010.	G. W. T : 4.57m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Pale brown 10YR (6/3), loose, cohesionless Silt, SM.			D-1 to D-3	4, 4, 3		
1.0m	Gray 10YR (5/1), loose to medium dense, cohesionless Silt, SM.			D-4	10		
1.0m	Gray 10YR (5/1), medium dense to loose, fine Sand, SM.			D-5	4		
1.0m	Gray 10YR (5/1), loose to medium dense, cohesionless Silt, SM.			D-6	10		
1.0m	Gray 10YR (5/1), medium dense to dense, fine Sand, SM.			D-7	21		
5.0m	Brown 7.5YR (5/1), dense to very dense, fine Sand, SM.			D-8 to D-11	23, 27, 29, 27		
9.45m	Gray 7.5YR (5/1), very dense, fine Sand, SM.			D-12 to D-17	30, 29, 34, 33, 35, 37		

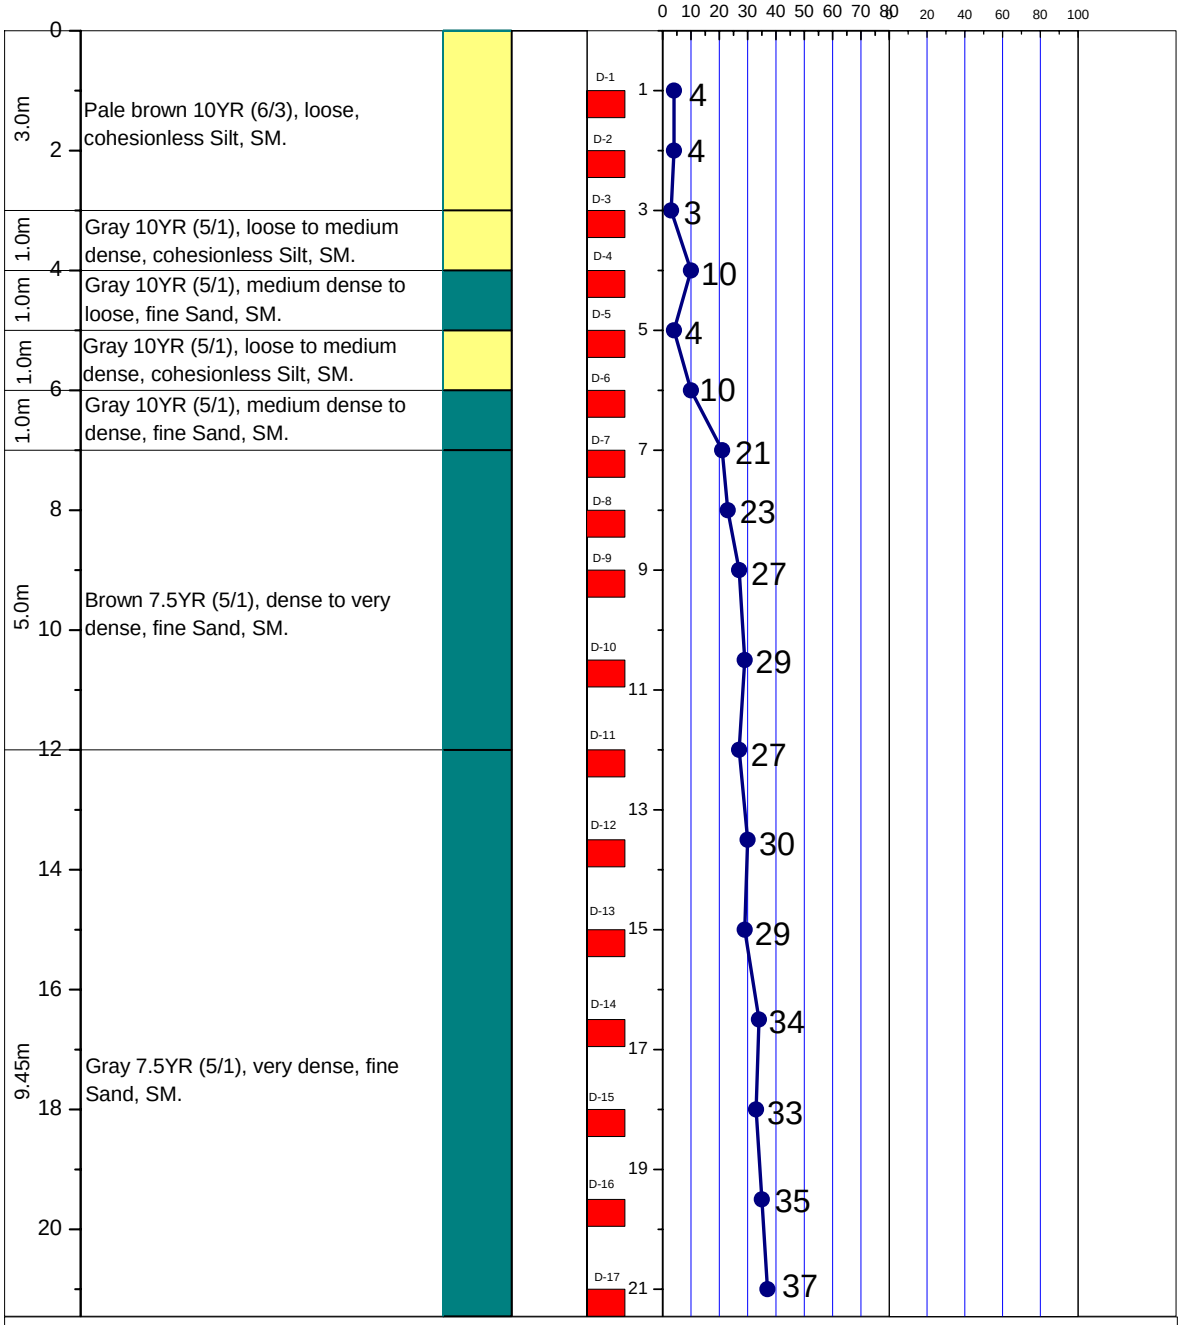

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY | SAND | SILT | SHALE

ORGANIC SOIL | MICACEOUS FINE SAND/SILT | UNDISTURBED SAMPLE | DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
