A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION: Dhaksin Gobindapur, Dharmaghar, Mdhabpur, Habiganj.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING: 21.0m	R. L.: 1.37m below from Road Level.
CLIENT : Grameenphone Ltd.	DATE OF BORING: 31-12-2010.	G. W. T : 0.91m below from E. G. L.

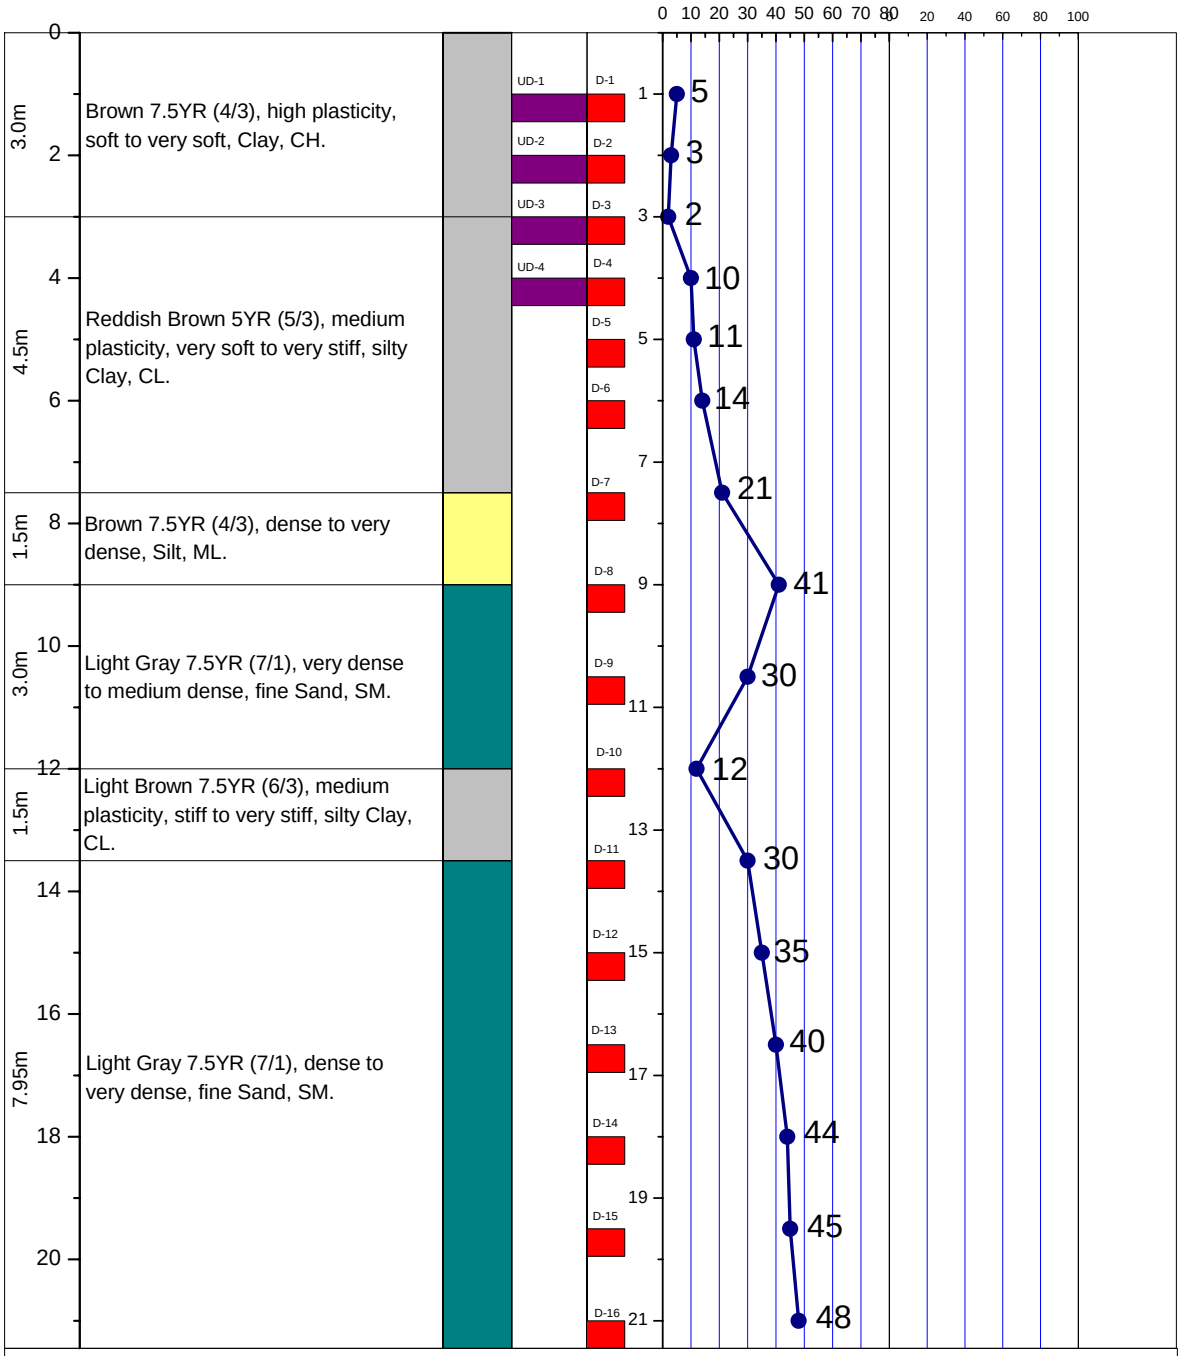

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY | SHALE | SILT | SAND

PEAT/HIGHLY ORGANIC SOIL | MICACEOUS FINE SAND/SILT | UNDISTURBED SAMPLE | DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED

A2 PROSOIL	BOREHOLE NO: BH-2	
	LOCATION: Dhaksin Gobindapur, Dharmaghar, Mdhabpur, Habiganj.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING: 21.0m	R. L.: 1.37m below from Road Level.
CLIENT : Grameenphone Ltd.	DATE OF BORING: 01-01-2011.	G. W. T : 0.91m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Brown 7.5YR (4/3), high plasticity, soft to very soft, Clay, CH.		UD-1, UD-2, UD-3	D-1, D-2, D-3	4, 4, 2		
4.5m	Reddish Brown 5YR (5/3), medium plasticity, very soft to very stiff, silty Clay, CL.		UD-3, UD-4	D-3, D-4, D-5, D-6, D-7	11, 13, 15, 23		
1.5m	Brown 7.5YR (4/3), dense to very dense, Silt, ML.			D-7, D-8	40		
3.0m	Light Gray 7.5YR (7/1), very dense to medium dense, fine Sand, SM.			D-8, D-9, D-10	32, 13		
1.5m	Light Brown 7.5YR (6/3), medium plasticity, stiff to very stiff, silty Clay, CL.			D-10, D-11	29		
7.95m	Light Gray 7.5YR (7/1), dense to very dense, fine Sand, SM.			D-11, D-12, D-13, D-14, D-15, D-16	34, 42, 45, 46, 47		

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY | SHALE | SILT | SAND

PEAT/HIGHLY ORGANIC SOIL | MICACEOUS FINE SAND/SILT | UNDISTURBED SAMPLE | DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED

A2 PROSOIL	BOREHOLE NO: BH-3	
	LOCATION: Dhaksin Gobindapur, Dharmaghar, Mdhabpur, Habiganj.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING: 21.0m	R. L.: 1.37m below from Road Level.
CLIENT : Grameenphone Ltd.	DATE OF BORING: 01-01-2011.	G. W. T : 0.91m below from E. G. L.

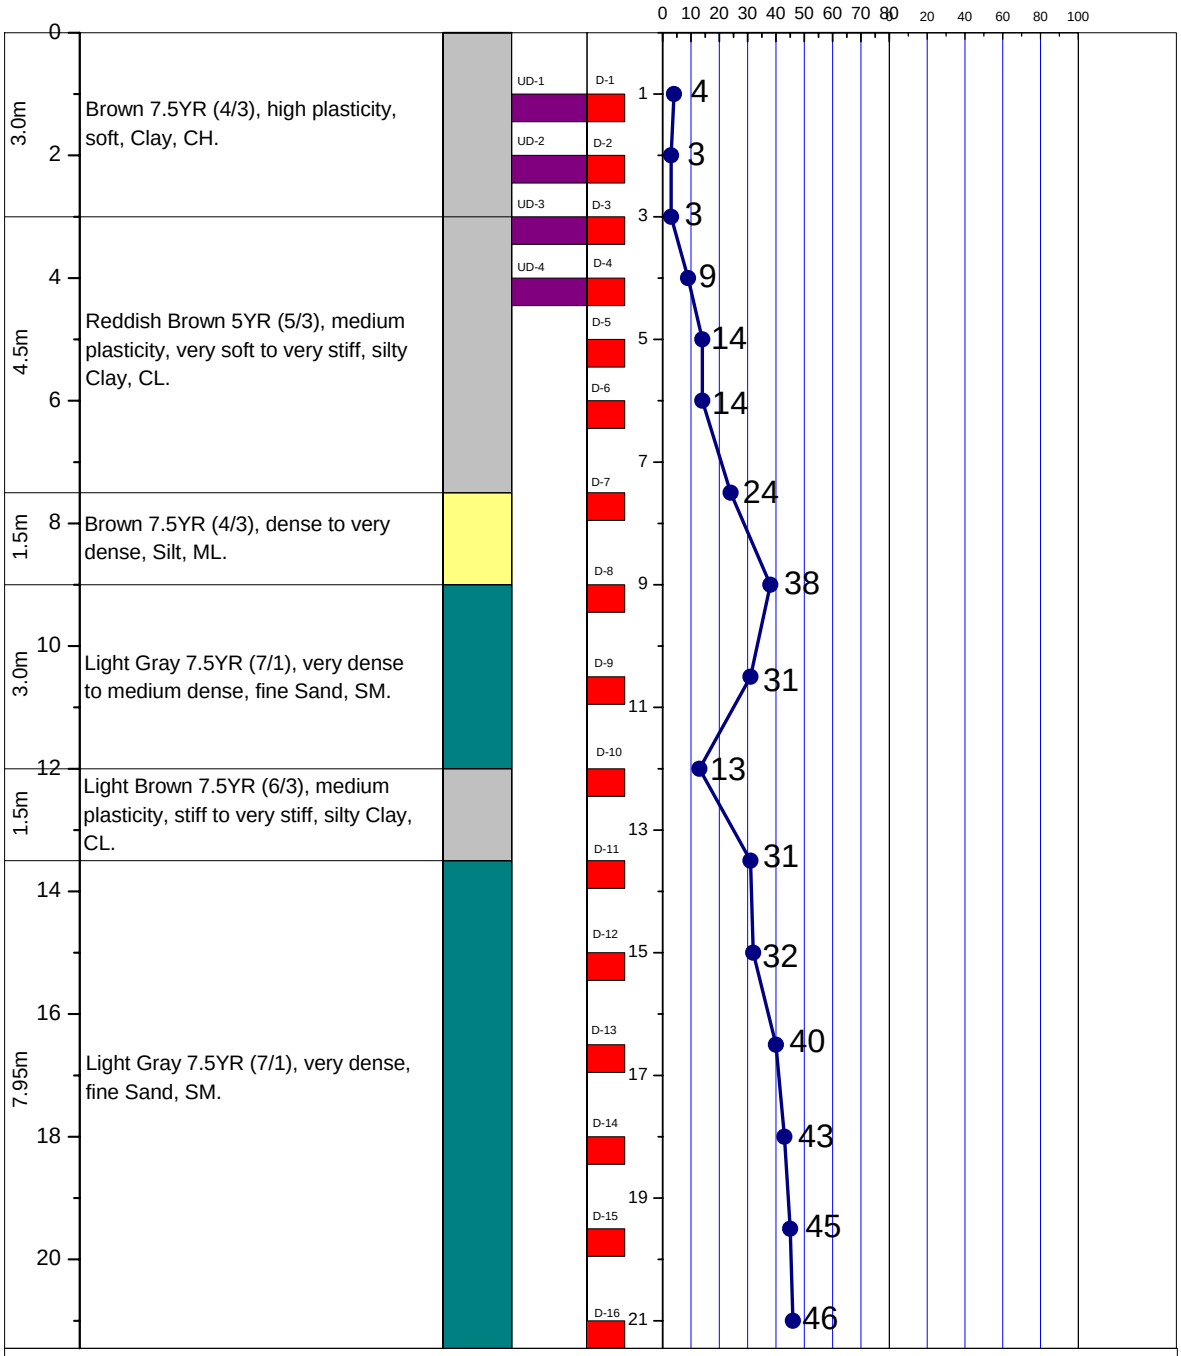

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY | SHALE | SILT | SAND

PEAT/HIGHLY ORGANIC SOIL | MICACEOUS FINE SAND/SILT | UNDISTURBED SAMPLE | DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
