A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION: Barthi, Gournadi, Barisal.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING: 21.0m	R. L.: 0.20m above from Road Level.
CLIENT : AXIATA (Bangladesh) Ltd.		DATE OF BORING: 30-09-2010.	G. W. T : o.91m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
2.0m	Brown 7.5YR (5/3), medium plasticity, soft, silty Clay, CL.		UD-1, UD-2	D-1, D-2	4, 5		
2.0m	Grayish Brown 10YR (5/2), medium plasticity, soft to stiff, silty Clay, CL.		UD-3, UD-4	D-3, D-4, D-5, D-6, D-7, D-8	5, 10, 6, 8, 5, 5		
9.5m	Gray 7.5YR (5/1), medium plasticity, soft to very stiff, silty Clay, CL.			D-9, D-10, D-11	6, 3, 4		
7.95m	Gray 7.5YR (5/1), dense to very dense, silty Sand, SM.			D-12, D-13, D-14, D-15, D-16, D-17	19, 24, 25, 28, 29, 34		

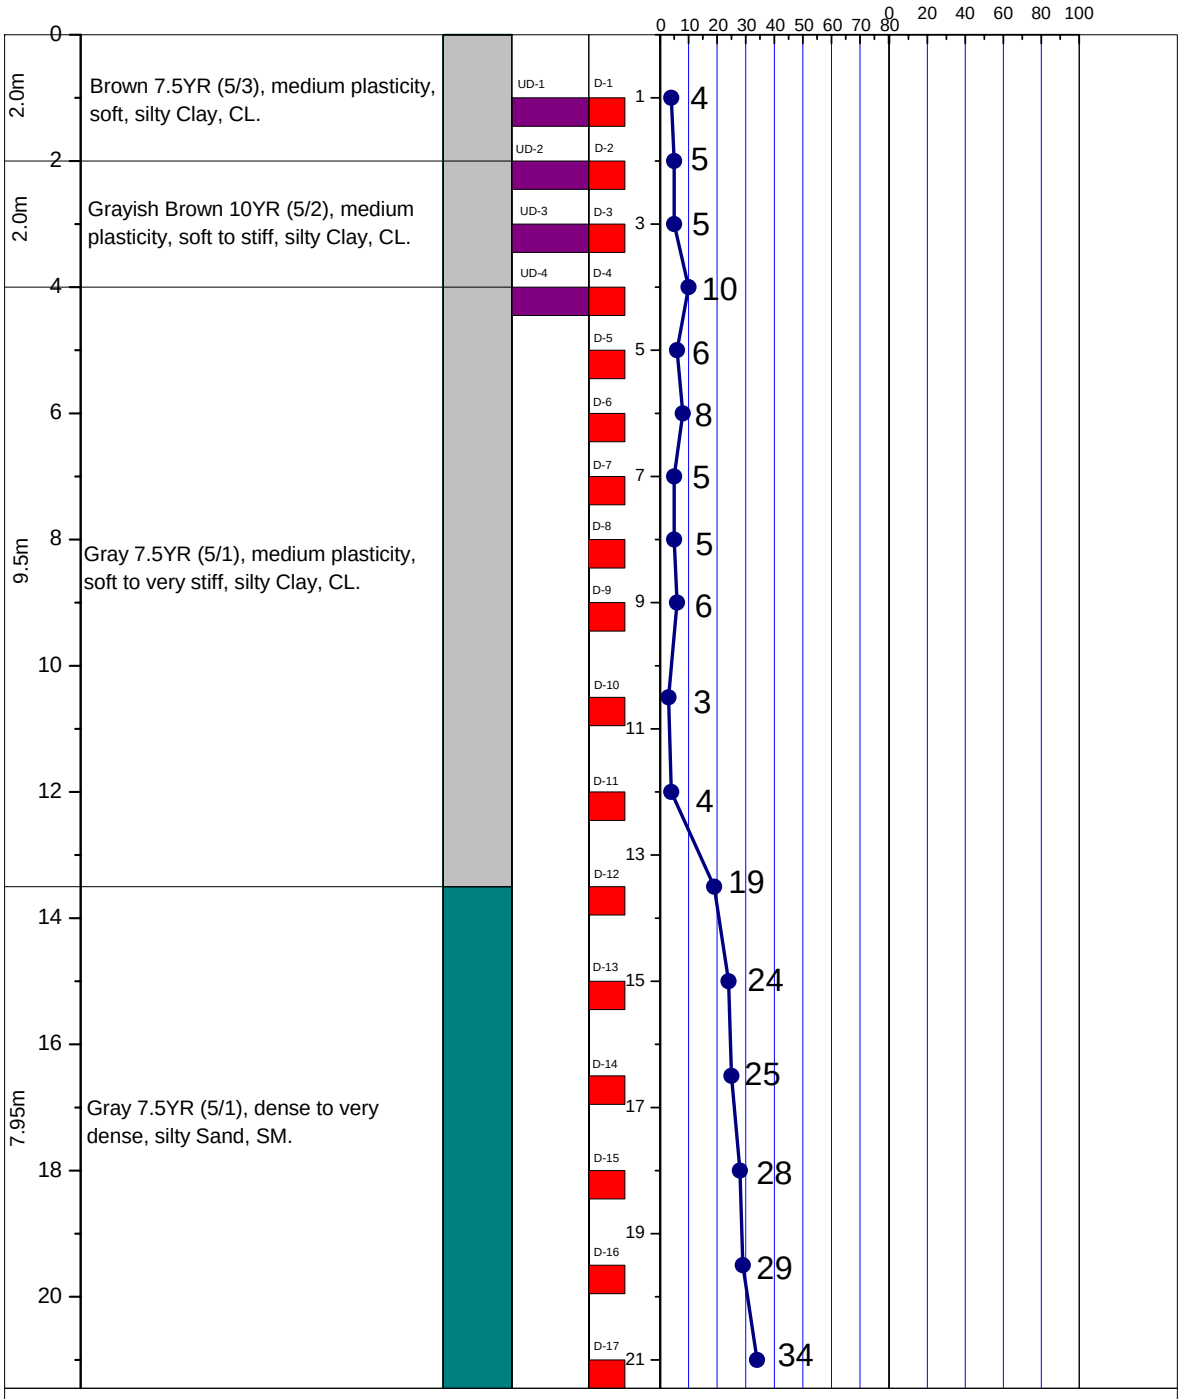

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY | SAND | SILT | SHALE

PEAT/HIGHLY ORGANIC SOIL | MICACEOUS FINE SAND/SILT | UNDISTURBED SAMPLE | DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
