A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION: Chilpara, Sangirshor, Chaddogram, Comilla.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING: 12.0m	R. L.: 1.52m below from Road Level.
CLIENT : AXIATA (Bangladesh) Ltd.		DATE OF BORING: 21-09-2010.	G. W. T : 0.91m above from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Bluish Gray Gley2 (5/1), medium dense to dense, Silt, ML.			D-1 to D-3	7, 10, 17		
9.45m	Light bluish Gray Gley2 (7/1), dense to very dense, fine Sand, SM.			D-4 to D-10	27, 41, 42, 44, 50, 50, 50		Over
9.0m	Boring was not possible due to very dense fine Sand.			D-11	50		Over

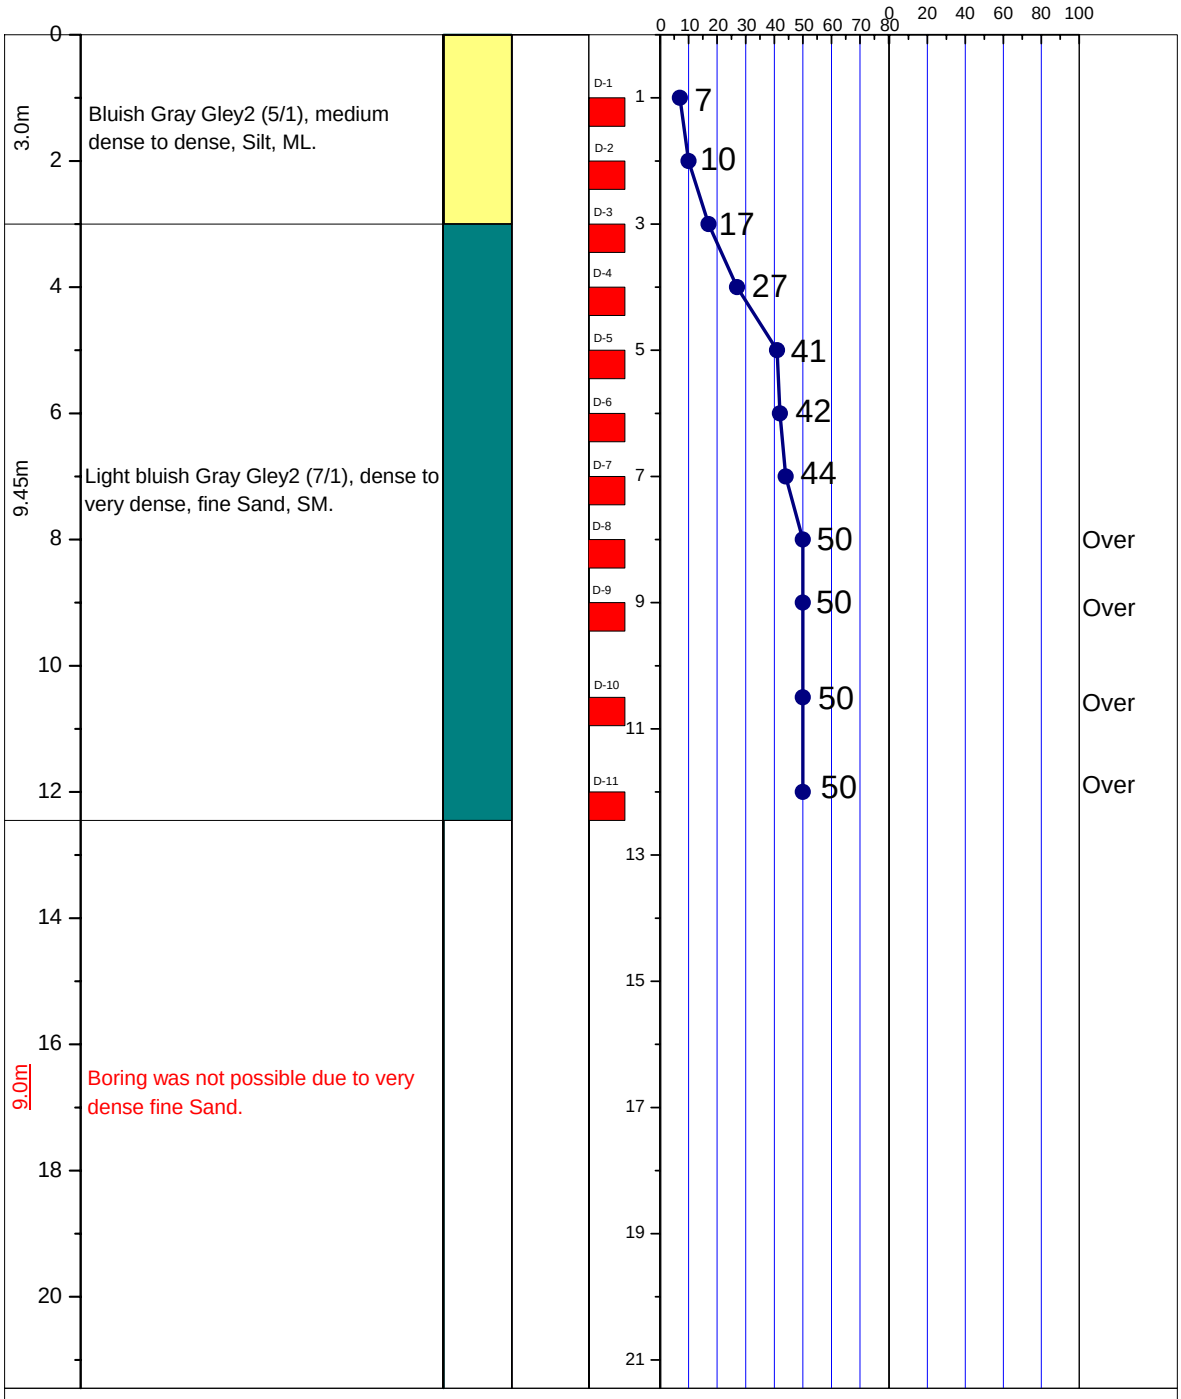

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SAND	SILT	SHALE
PEAT/HIGHLY ORGANIC SOIL	MICACEOUS FINE SAND/SILT	UNDISTURBED SAMPLE	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
