A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION: Daya, Shahjadpur, Sirajganj.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING: 21.0m	R. L.: 0.66m below from Road Level.
CLIENT : Grameenphone Ltd.		DATE OF BORING: 07-03-2014.	B. W. T : 4.57m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Pale Brown 10YR (8/2), very loose to medium dense, silty Sand, SM.			D-1 to D-3	2, 5, 8		
3.0m	Pale Brown 10YR (8/2), medium plasticity, very soft to medium stiff, silty Clay, CL.		UD-1, UD-2	D-4 to D-6	4, 5, 2		
9.0m	Gray 7.5YR (5/2), medium plasticity soft to stiff, silty Clay, CL.			D-7 to D-11	4, 5, 4, 5, 31		
6.45m	Gray 10YR (6/1), dense to very dense, silty Sand, SM.			D-12 to D-16	32, 36, 34, 35, 39		

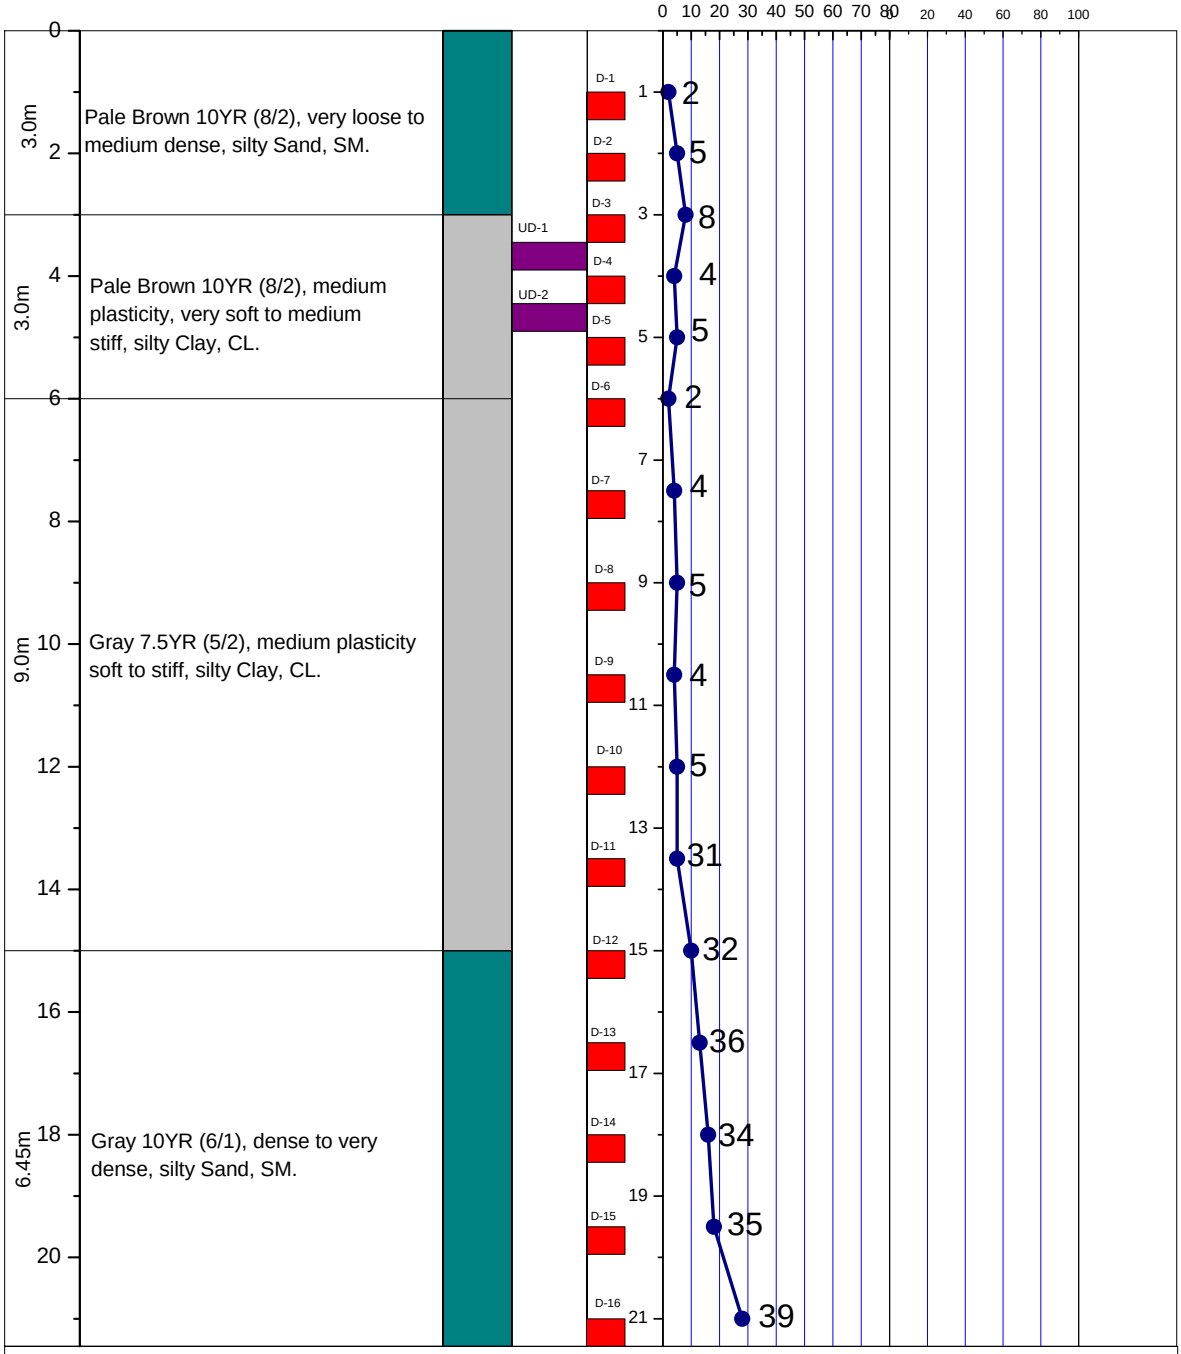

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY | SHALE | SILT | SAND

PEAT/HIGHLY ORGANIC SOIL | MICACEOUS FINE SAND/SILT | UNDISTURBED SAMPLE | DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
