A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION : Isachari, Chokoria, Cox's Bazar.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING : 21.0m	R. L.: 2.43m below from Road Level.
CLIENT : TM International, Bangladesh Ltd.	DATE OF BORING : 27-04-2007	G. W. T : 3.65m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
4.0m	Very Pale Brown 10YR (7/3), Medium Plastic, Medium stiff, silty Clay, CL.			D-1 to D-4	6, 7, 5, 7		
1.0m	Light gray 10YR (7/2), Medium plastic, Medium stiff, silty Clay, CL.			D-5	21		
4.0m	Very pale brown, 10YR (7/3), Dense, Fine sand, SM.			D-6 to D-8	31, 26, 23		
1.5m	Gray 10YR (6/1), Dense, Cohesion-less silt, SM.			D-9	18		
1.5m	Very pale brown 10YR (7/3), Dense, Fine sand, SM.			D-10	29		
9.45m	Light gray 10YR (7/2), Very dense, Fine sand, SM.			D-11 to D-17	38, 39, 41, 43, 46, 46, 49		

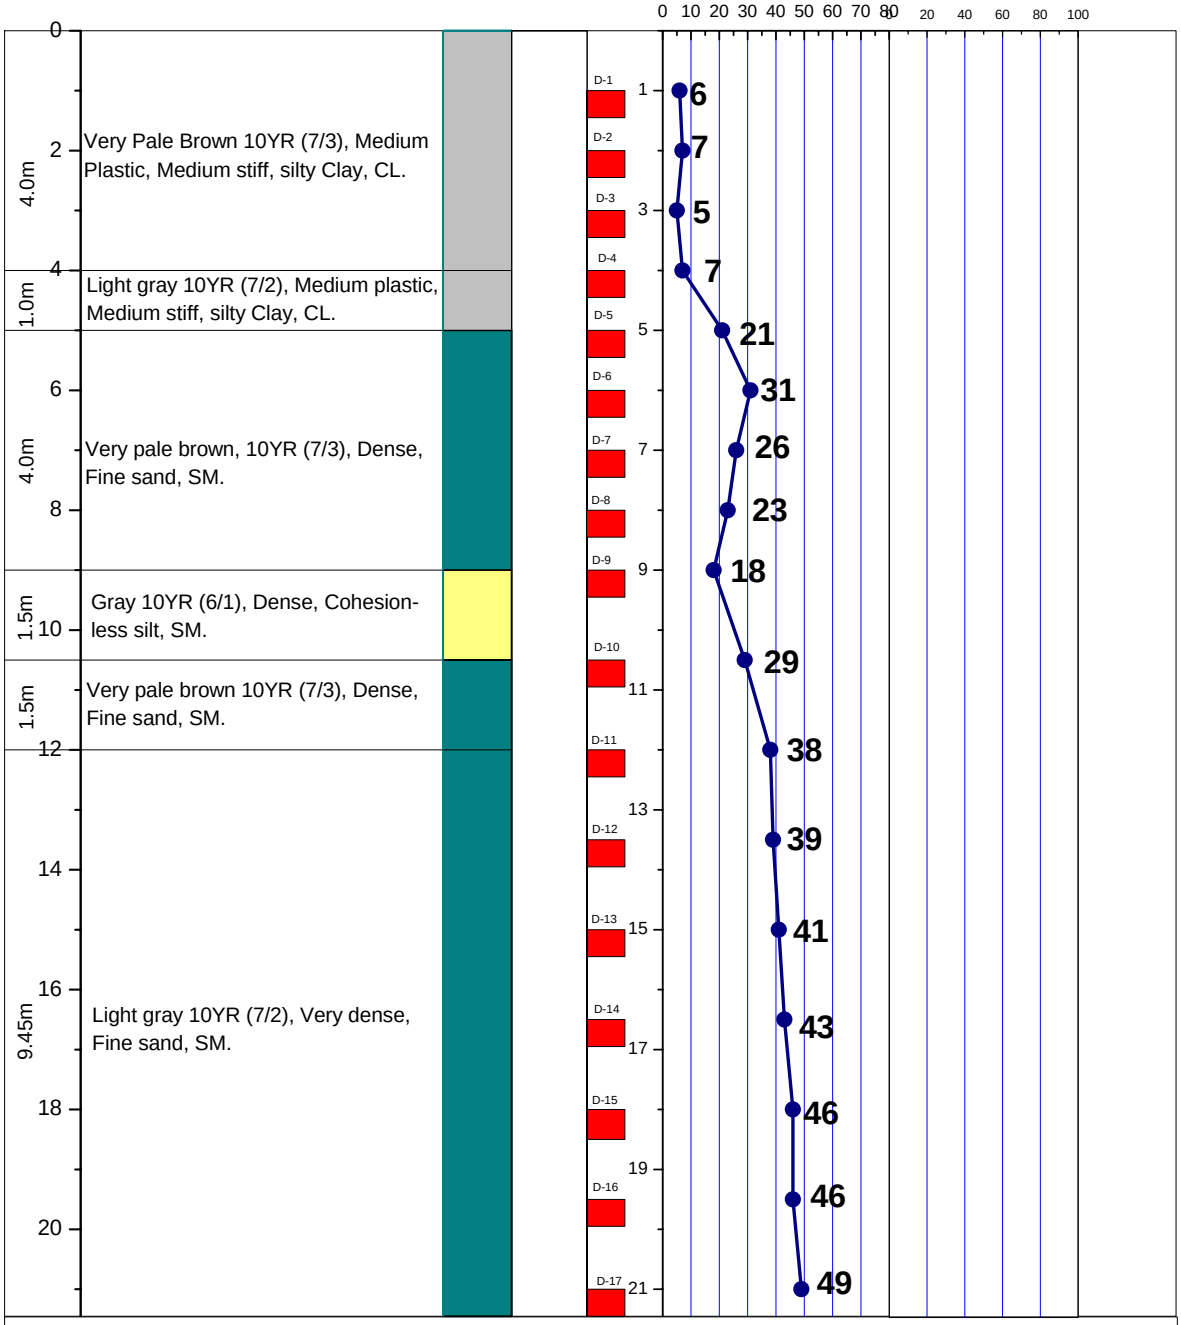

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
