A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION : Taltoli, Amtoli, Barguna.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING : 21.0m	R. L.: 3.04m below from Road Level.
CLIENT : TM International, Bangladesh Ltd.	DATE OF BORING : 17-01-2009	G. W. T : 1.21m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Brown 10YR (5/3), medium plastic, soft to very soft, silty Clay, CL.		UD-1, UD-2	D-1, D-2, D-3	5, 4, 1		
3.0m	Gray 10YR (6/1), very loose to loose, cohesionless silt, SM.			D-4, D-5, D-6	1, 1, 5		
3.0m	Gray 10YR (6/1), medium plastic, soft to stiff, silty Clay, CL.			D-7, D-8, D-9	7, 9, 14		
4.5m	Gray 10YR (6/1), medium dense, fine sand, SM.			D-10, D-11, D-12	14, 11, 11		
6.0m	Gray 10YR (6/1), medium dense, cohesionless silt, SM.			D-13, D-14, D-15	8, 8, 10		
1.95m	Gray 10YR (6/1), medium dense, silty Sand, SM.			D-16, D-17	12, 9		

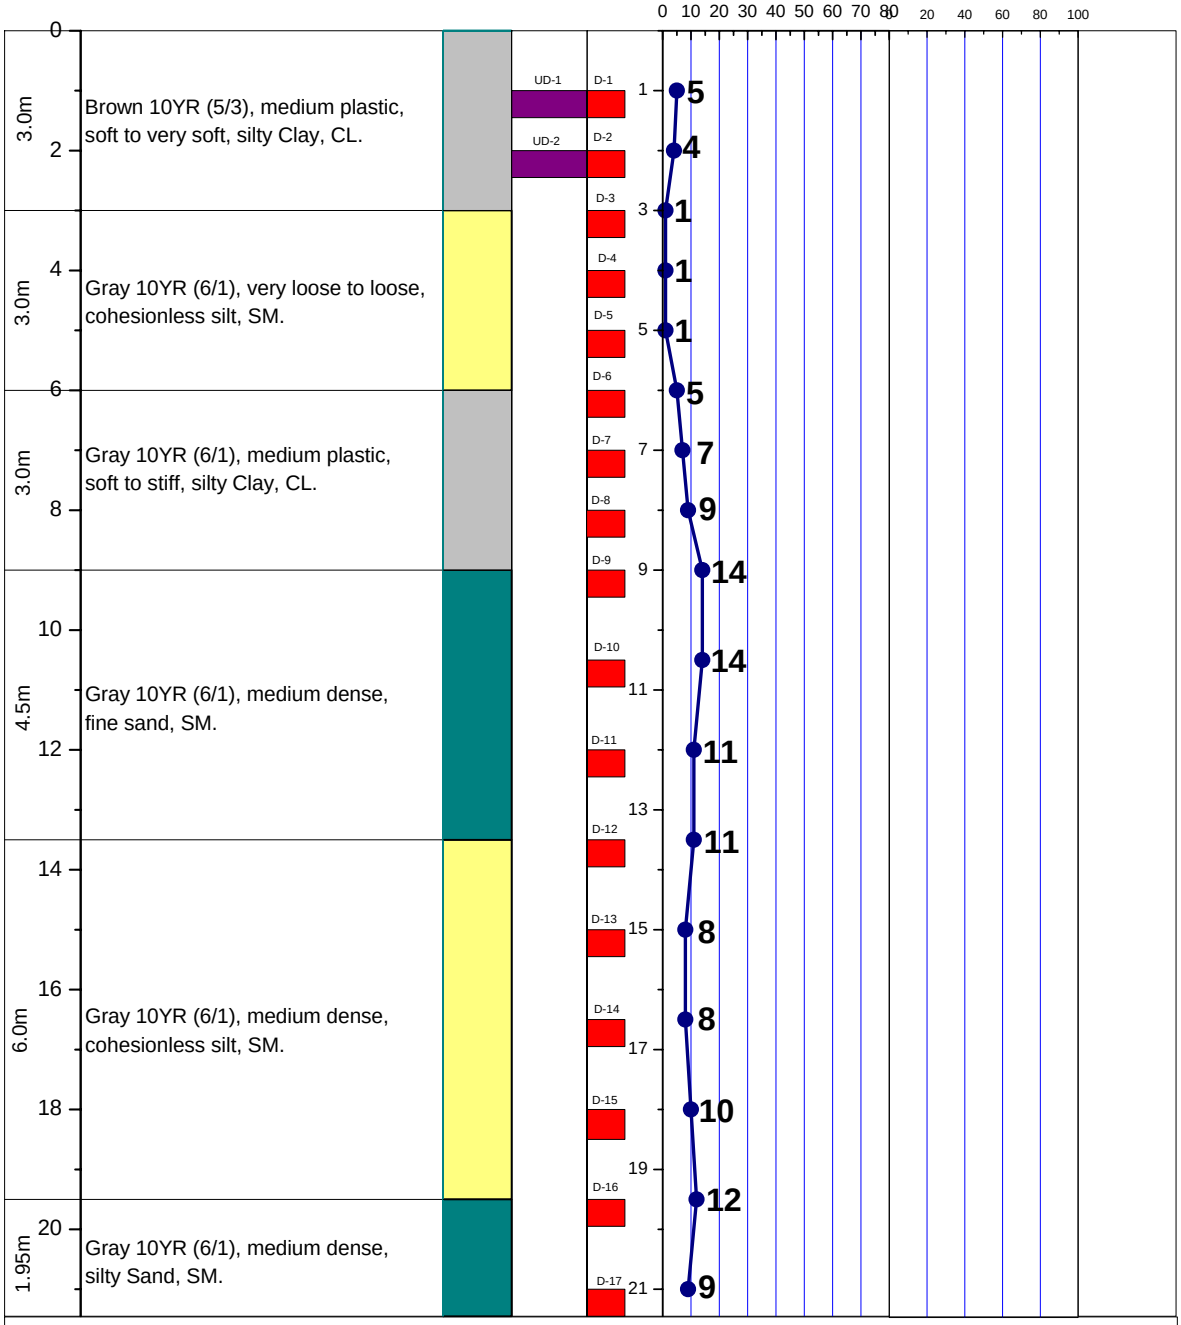

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
