A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION : Jangail, Salutikar.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING : 21.0m	R. L.: 1.52m below from Road Level.
CLIENT : Grameenphone Ltd.		DATE OF BORING : 31-07-2009.	G. W. T : 0.45m above from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
5.0m	Light gray 10YR (7/2), medium plastic, very soft to soft, silty Clay, CL.		UD-1, UD-2, UD-3, UD-4	D-1 to D-5	1, 1, 1, 1, 5		
4.0m	Gray 10YR (6/1), loose to medium dense, cohesionless Silt, SM.			D-6 to D-8	4, 6, 9		
6.0m	Gray 10YR (6/1), medium dense to dense, silty Sand, SM.			D-9 to D-12	11, 14, 14, 17		
6.45m	Gray 10YR (6/1), medium dense to very dense, silty Sand, SM.			D-13 to D-16	32, 31, 34, 33		

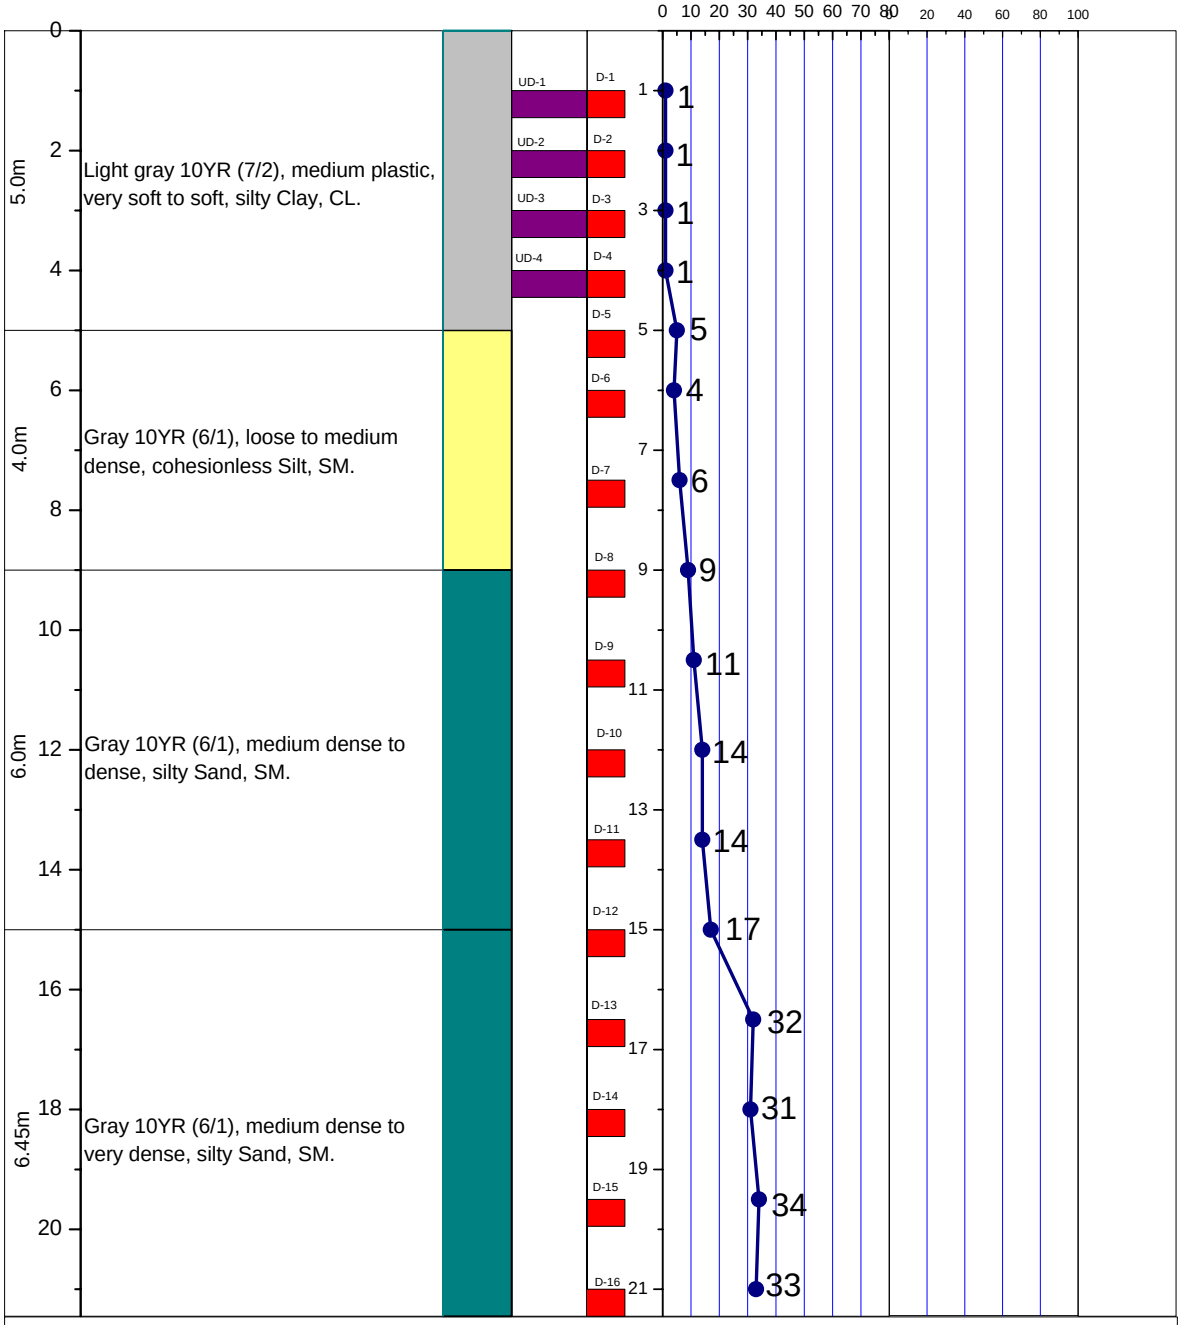

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
