A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION : Ghoshghar, Debidwar, Comilla.	
PROJECT : Telecommunication Tower.		DEPTH OF BORING : 21.0m	R. L.: 1.52m below from Road Level.
CLIENT : TM International, Bangladesh Ltd.		DATE OF BORING : 07-04-2009.	G. W. T : 0.10m above from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Brown 7.5YR (6/3), medium dense to dense, cohesionless silt, SM.			D-1 to D-3	11, 13, 21		
2.0m	Gray 7.5YR (5/1), dense to medium dense, fine sand, SM.			D-4 to D-5	16, 13		
1.0m	Gray 7.5YR (5/1), medium dense to dense, cohesionless silt, SM.			D-6	18		
9.0m	Gray 7.5YR (5/1), dense to very dense, fine sand, SM.			D-7 to D-12	17, 18, 33, 23, 27, 30		
6.45m	Gray 7.5YR (5/1), very dense, cohesionless silt, SM.			D-13 to D-17	29, 33, 36, 39, 41		

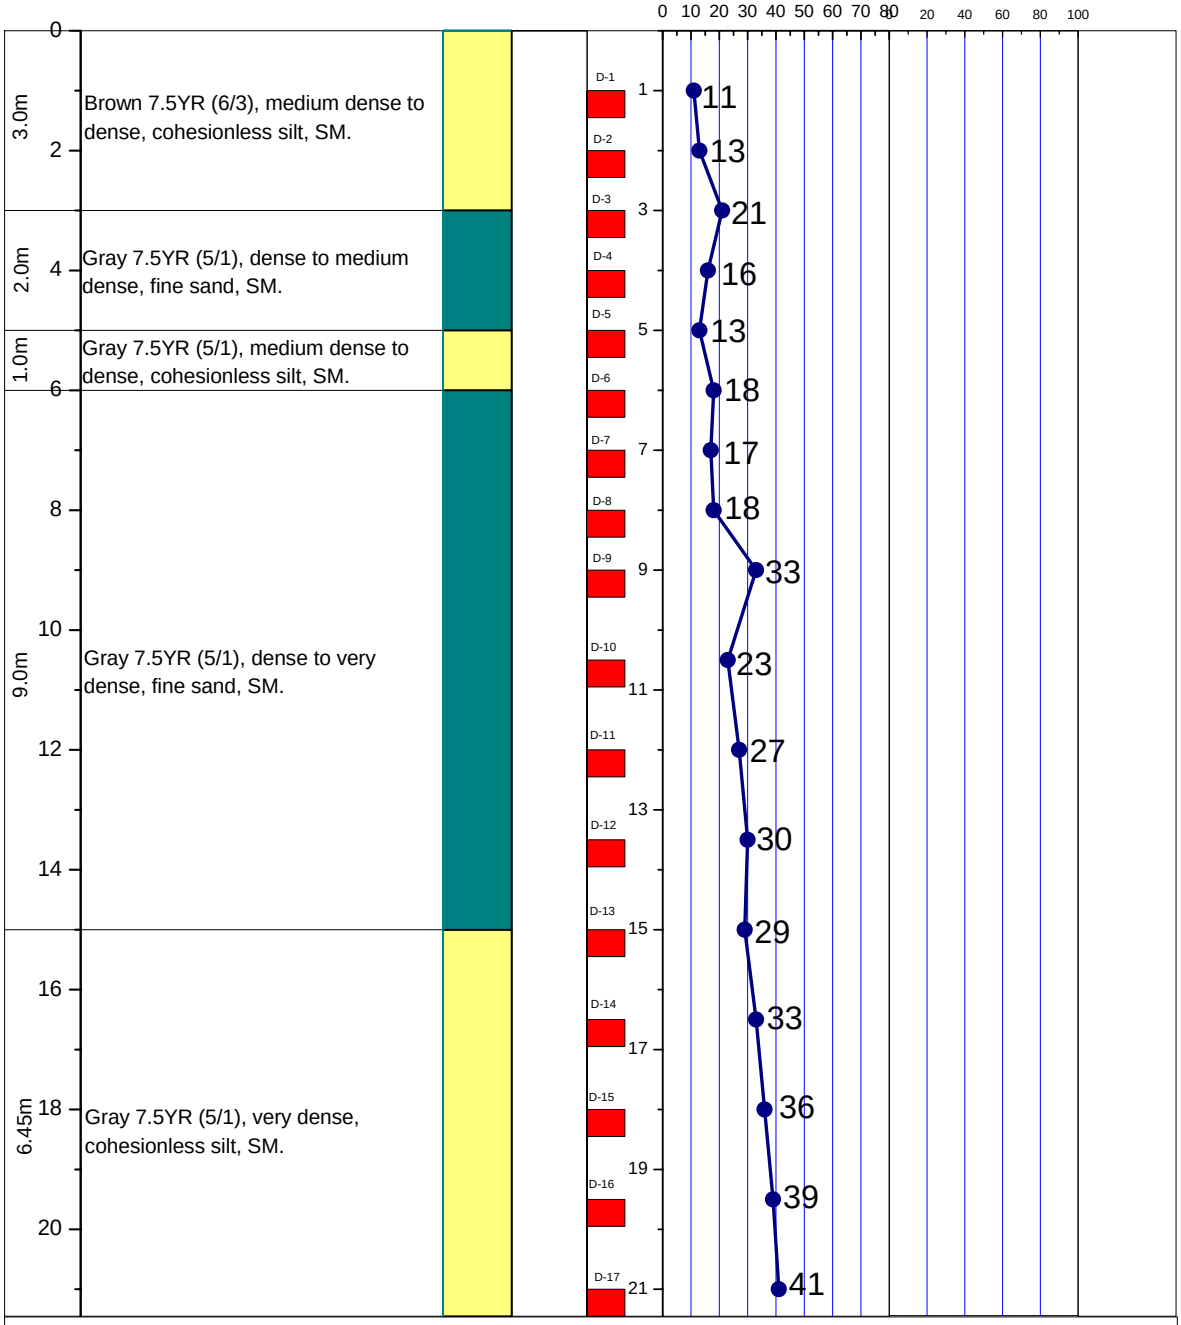

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
