A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION : Utrail, Utrail Hat, Shibchar, Madaripur.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING : 21.0m	R. L.: 2.13m below from Road Level.
CLIENT : Warid Telecom International Ltd.	DATE OF BORING: 12-08-2011.	G. W. T : 0.15m above from E.G.L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
4.5m	Pale Brown 10YR (6/3), medium plasticity, soft to medium stiff, silty Clay, CL.		UD-1, UD-2, UD-3	D-1 to D-3	5, 7, 9		
1.5m	Gray 7.5YR (5/1), low plasticity, medium stiff to stiff, silty Clay, CL.			D-4	15		
1.5m	Gray 7.5YR (5/1), medium dense to dense, silty Sand, SM.			D-5	21		
13.95m	Gray 7.5YR (5/1), dense to very dense, fine Sand, SM.			D-6 to D-14	37, 40, 42, 40, 47, 49, 44, 46, 48		

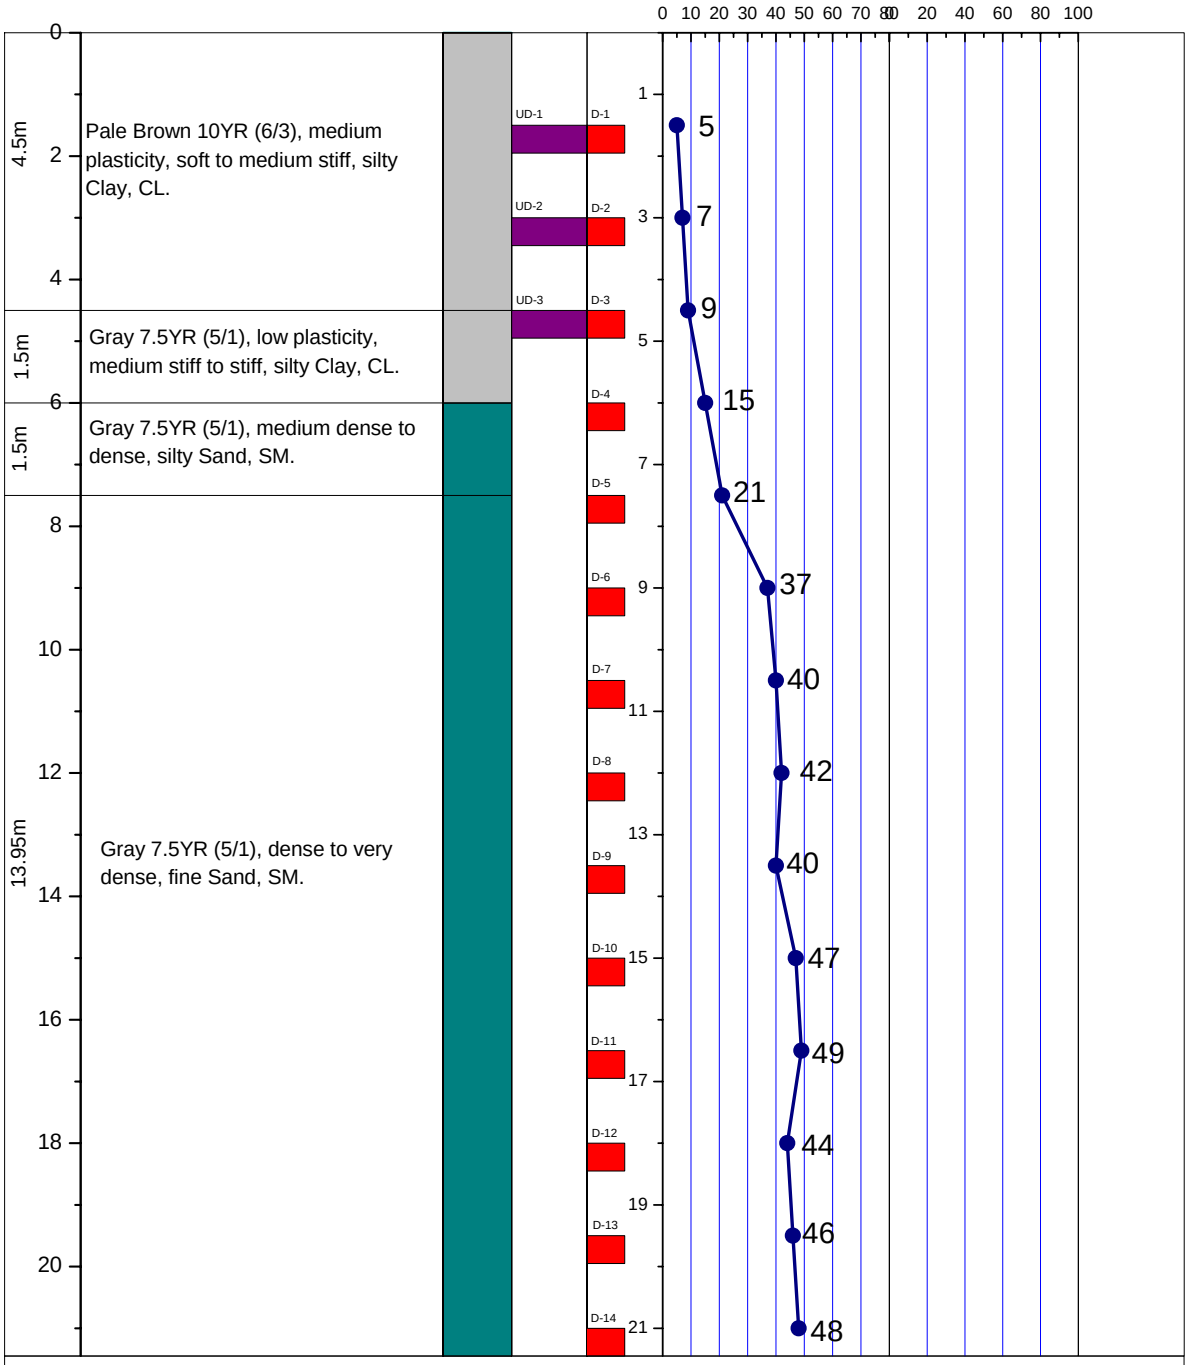

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SAND	SHALE	UNDISTURBED SAMPLE
MICACEOUS FINE SAND/SILT	SILT	PEAT/HIGHLY ORGANIC SOIL	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
